



Registered AD

HZL/CLZS/ENV/33/2024-25

30.11.2024

To,
The Deputy Director(S)/Scientist-C
MoEF & CC
Integrated Regional Office,
A-209 & 218, Aranya Bhawan,
Jhalana Institutional Area
Jaipur - 302004

Sub: Six Monthly EC compliance report of Hydro phase I & II, Pyro, Ausmelt & 290 MW CPP

Ref: Environmental Clearance Letter No. IA-J-11011/279/2006-IA-II(IND-I) dated, 29,12,2023

Sir.

Please find enclosed herewith the six-monthly compliance report with reference to above Environmental Clearances for Hydro phase I & II, Pyro, Ausmelt & 290 MW CPP of CLZS for period 01.04.2024 to 30.09.2024 with all the enclosures and annexures.

Thanking you, Yours faithfully,

[Manisha Bhati]

Manager - Environment

Chanderiya Lead Zinc Smelter

Cc:

The Member Secretary,
 Rajasthan State Pollution Control Board,
 4, Institutional Area, Jhalana Doongri,
 Jaipur (Raj.)- 302004

- In-Charge (Zonal Officer)
 Central Pollution Control Board,
 Vithal Market, Paryavaran Parisar, E-5, Arera Colony,
 Bhopal 462016 (MP)
- The Regional Officer, Rajasthan State Pollution Control Board, Near FCI Godown, Chanderiya, Chittorgarh – 312001
- Office Copy

CHANDERIYA LEAD ZINC SMELTER [HYDRO, PYRO, AUSMELT & 290 MW CPP]

Environment Compliance Report of Chanderiya Lead Zinc Smelter, Chittorgarh with reference to Environmental Clearance letter No. IA-J-11011/279/2006-IA-II(IND-I) dated, 29.12.2023 for Hydro phase I & II, Pyro, Ausmlet & 290 MW CPP

S.No.	CONDITION	STATUS
A. SPI	ECIFIC CONDITIONS:	
i.	This Environmental clearance is granted subject to final outcome of Hon'ble Supreme Court of India, Hon'ble High Court, Hon'ble NGT and any other Court of Law, if any, as may be applicable to this project.	
ii.	The project proponent shall comply with all the environmental protection measures and safeguards proposed in the documents submitted to the Ministry. All the recommendations made in the EIA/EMP in respect of environmental management, and risk mitigation measures relating to the project shall be implemented.	
		CCUS Capturing of carbon emitted and storage is no relevant to its utilization in Smelter Operation request to remove this condition. HZL has committed for NET ZERO by 2050. HZL is 1st metal and mining company in INDIA which has approved SBTi targets in alignment of 1.5° Centigrade Scenario. We have already started the work to achieve our short-term target of "reduction in Scope 1 & Scope 2 emissions by 50% by 2030" and long term target of "Net Zero by 2050". The Smelting process is an energy intensive process and around 90% of energy mix is electricity. We have already signed the agreement for captive utilization of 450 MW RE RTC power to reduce GHG emissions. As per the current planning, the remaining GHG emissions process will be shifted on electricity of Hydrogen based on availability of technology in upcoming years. The residual GHG emission will be offset by Carbon Capture Utilization & Sequestration techniques. These techniques will be used after 2040 for residual emission only. Remark: Detailed carbon Management Plan along with HZL de-carbonization strategy was part of Final

		EIA/EMP report of CLZS 1-C. HZL Commit to comply with General Condition (GC-VII (ii).
iv.	The water requirement of 38570 KLD (existing) shall be sourced from Gosunda Dam (Fresh Water) & Proposed STP Chittorgarh/ Udaipur/ other proposed STP's (Recycled Water) and 500 KLD additional water for the Minor Metal Unit shall be sourced from RO permeate water from ETP. No ground water abstraction is permitted. PP shall maximize the usage of treated water.	Noted & Is been complied.
V.	Following additional arrangements to control fugitive dust shall be provided: a) Fog / Mist Sprinklers at all conveyors point and on bulk raw material storage area (at the transfer points) like Iron Ore, Coal and for Fly Ash and similar solid waste storage areas. b) Proper covered vehicle shall be used while transport of materials. c) Wheel Washing mechanism shall be provided in entry and exit gates with complete recirculation system.	 In order to minimize fugitive emissions Zn Concentrate containing 8-10% moisture is being handled. Provision of water spraying at Zn concentrate stock yard has been provided and working satisfactorily. Dust control system has been provided at material transfer points. Mobile Vacuum dust sweeping system on industrial roads and vacuum dust cleaning system for plant area are exist at smelter to control airborne dust due to the vehicles movement. Regular road washing is being done on industrial roads. Truck & tyre washing system has been provided and working satisfactorily. All roads are cemented/concreted. Proper covered vehicles are used for the transportation of materials. Bag filters are installed in the Roaster, Calcine handling & storage section, Zinc atomizing unit, Dross milling section to control fugitive emissions.

Mobile Vaccum sweeper

		Road washing
vi.	All internal road and connecting road from project site to main highway shall be developed and maintained with suitable Million Axle Standard (MSA) as per the traffic load due to proposed project as per the action plan submitted.	All roads are cemented/concreted.
vii.	All stockyards shall be having impervious flooring and shall be equipped with water spray system for dust suppression. Stock yards shall also have garland drains to trap the run off material.	All stockyards have impervious flooring and also equipped with water spray system for dust suppression. Stockyards also have garland drains to trap the runoff material
viii.	Performance test shall be conducted on all pollution control systems every year and report shall be submitted to Regional Office of the MoEF&CC.	Efficient Air Pollution control Equipments (APCE) like Bag House Bag Filter/ ESP etc have been installed. Performance test of all APCE is been planned to get done by third party/Consultant and will be submitted by March 2025 to Regional office of MoEF& CC.
ix.	Particulate matter emission from stacks shall be less than 30 mg/Nm³. Action plan submitted to limit the dust emission shall be strictly implemented. The PP shall periodically conduct Mineralogical composition study of the PM10 and shall ensure the constituents are well within the permissible limits. The reports shall be submitted to MoEF&CC and uploaded in their six-monthly EC compliance report.	Particulate matter levels from Hydro I & II Stacks is less than 30 mg/Nm3. PM Emission from Pyro & Ausmelt Smelter norms is 150 mg/nm3 & 50mg/nm³ as per existing designed technology which will be reduced to maximum 100 mg/nm3 in pyro by replacing all existing bags of Bag filter with upgraded/ PTFE coated bags by December 2024 with an investment of more than Rs 1.5 Cr. Further reduction in the PM Emissions from pyro & Ausmelt unit to < 30mg/nm by December 2026 as technically it not feasible in the existing technology installed in the plant, which is more than 32 years old, any updation in this will require major technology change w.r.t Plant design accordingly will be explored and implemented.

		PM emissions standard from CPP Stack as per MOEF & CC Notification 7 th Dec 2015 for Thermal Power Plant installed after 1 st Jan 2003 is 50 mg/nm ³ .
		Mineralogical composition study of the PM10 will be completed by March 2025 through Expert Agency /Consultant and reports shall be submitted to MoEFCC.
X.	CEMS shall be provided on all process stacks and the signal shall be received in plant control room for central control of APCDs installed in the plant.	2) Pollution control systems are interlocked with
xi.	Risk assessment and Disaster Management Plan shall be strictly implemented as per the action plan submitted to the Ministry.	We will ensure the implementation of Disaster
xii.		SO2 emissions from H2SO4 Plant is been ensured at less than 1 kg/t from Hydro Zinc Smelters. SO2 emission from Pyro & Ausmelt Smelter unit operating at 2 kg/t of acid shall be reduced to 1.5 kg/t by improving the SO2 conversion efficiency using super cesium catalyst in 4th bed by December 2024 and <1 kg/t up to December 2026 as it will involve 100% technology upgradation in the existing TGT.
xiii.	Acid mist from H2SO4 plant shall be less than 30 mg/Nm ³ .	Acid mist from H2SO4 plant at Hydro units is been maintained at < 30mg / Nm3 and Acid mist less than 30 mg/Nm3. Existing Pyro Unit TGT is designed at 50 mg/Nm3 emission therefore, < 30 mg/Nm3 will be done by December 2026 with the upgradation of TGT technology in Pyro and Ausmelt.
xiv.	Particulate matter levels from the stacks shall be less than 30 mg/Nm ³ .	Particulate matter levels from Hydro I & II Stacks is been ensured at 30 mg/Nm3 and for Captive Power Plant Stacks maintained at 50 mg/Nm3. SPM Emissions from Pyro Metallurgical Smelter and Ausmelt shall be less than 30 mg/Nm3 by December 2026.
xv.	100% Solid waste generated shall be utilised/ properly disposed. The PP shall explore and implement the principles of 'Circular Economy'. The PP shall periodically conduct study for the presence of Heavy metals/ metalloids contamination and leaching in the	HZL at its CLZS Unit is disposing 100% of its generated solid waste through Third Party Vendor. Study to conduct Heavy metals/ metalloids contamination and leaching in the soil within 2 kms of the Project and to take remedial measures if any contamination Observed will be done by Expert

	soil within 2 kms of the Project and shall take all remedial measures in this respect. The reports shall be submitted to MoEF&CC and uploaded in their six-monthly EC compliance report.	MoEF&CC by June 2025. HZL is ensuring and implementing principles of 'Circular Economy' by it existing Waste to Wealth and waste to recovery Initiatives.
xvi.	and Berach River is flowing adjacent to the	Noted.
	project site in the East direction. Also, Gambhir Nadi(~4.0 km, S), Nagdi ka Nala (~8.5 km, NNE) and Canal (~8 km, WNW) are flowing within 10 Km. radius of the plant site. As submitted, a robust and full proof Drainage Conservation scheme to protect the natural drainage and its flow parameters; along with Soil conservation scheme and multiple Erosion control measures shall be strictly implemented.	out to prepare robust and full proof Drainage Conservation scheme to protect the natural drainage and its flow parameters, along with Soil conservation scheme and multiple Erosion control measures for implementation by December 2025.
xvii.	The proposed project shall be designed as "Zero Liquid Discharge" Plant. ETP shall be installed and there shall be no discharge of effluent from the plant. Domestic effluent shall be treated in Sewage Treatment Plant. MSW waste shall be treated in digester and recovered gas shall be used in the canteen.	Discharge" Plant.
		Organic waste is treated in Organic Waste Composter already present at Plant and Township and manure is used in horticulture activities.
xviii.	Existing ETP shall be strengthened to recycle additional effluent by installing MEE for RO rejects.	(1) All effluent is treated in ETP followed by RO and MEE.(2) Zero discharge is being maintained at our plant.
		Treated water monitoring results are annexed as Annexure-V.
xix.	submitted in the EIA/EMP report and reduce water dependence from the outside source.	We have constructed a dam having capacity very larger than our requirement. Further we have constructed Ponds/Anicuts. Apart from these HZL has constructed many rainwater harvesting structures (comprising of check dams, Weirs, Earthen check dams, cemented check dams etc).
	The nearest habitation to plant are Putholi (~0.5 km in SW), Ajoliya Ka Khera (~1 km in West) and Biliya (~ Adjacent in North) from plant site. There are approx. 75 villages and 1 city in 10 km radius study area. Project Proponent shall take appropriate environmental safeguard measures to minimise the impact on the habitation of the	Complied and added in the environment monitoring program.

	locals. The company shall also include these	
	locations in its environmental monitoring	
	program.	
xxi.	Solar Energy shall be generated at the roof	Is being complied at site. Solar Power is generated at
	tops of the plant and office buildings.	Hydro 2 CDSS Lab building, Hydro 1 leaching
		office, Switchyard control room building, Zinc
		School & Boy's Hostel/Utility Building at Zinc
		Nagar, Pyro Offices
	±	
		Solar Panel at roof top
xxii.	A proper action plan must be implemented to	E-Waste is disposed as per CLZS Waste Management
	dispose of the electronic waste generated in the industry.	Plan and is being send to the register recycler.
xxiii.	The PP shall implement the	Noted & is been complied at site. All the
	recommendations of the root cause analysis report on accident occurred in the Unit to prevent the future accident in the industry.	recommendations are closed.
xxiv.	Three tier Green Belt shall be developed in at	HZL Chanderiya has covered more than 37% Green
	least 37% of the project area and shall be	Belt at project area. We are working in the
	completed by 2023-24 all along the periphery	development of tree density up to 2500 per ha by
	of the project site of adequate width and tree	2025.
	density shall not be less than 2500 per ha.	Miyawaki plantation is developed at project site and
	Gap filling shall be undertaken and survival	plantation is being done at Jarofix-II dump yard.
	rate of green belt developed shall be	
	monitored on periodic basis to ensure that	
	damaged plants are replaced with new plants	
	in the subsequent years. Further, greenbelt	
	shall also be developed in the form of shelter	
	belt comprising of total of 6 rows of 2x2 m	A STATE OF THE PARTY OF THE PAR
	plantation with tall trees & broad leaves with	· · · · · · · · · · · · · · · · · · ·
	thick canopy along with windshield to act as	
	green barrier for air pollution & noise levels	- SOL
	towards the Putholi, Ajoliya Ka Khera and	
	Biliya villages inside the plant premises. All	
	d to d to d to the days to	
	the plantation work should be done in	
	consultation with Arid Forest Research	



		Percentage Green-cover Green-cover Chamber and New Acquired Combined
		Category Zon Grander Cling Land Land
		Dense Green-cover
		New Plantation Total Green-cover 55.20% 41.39%
		Kappa Apraida and Assessment 0.83
		Decode Second from 15 to copie resource.
		Reference data: Pris Communit of the
XXV.	Greening and Paving shall be implemented in	Noted & been Complied.
AAV.	the plant area to arrest soil erosion and dust	
	pollution from exposed soil surface.	
XXVI.	Air Cooled condensers shall be used in the	Existing CPP is designed on Water Coole
xxvi.	Air Cooled condensers shall be used in the captive power plant.	Existing CPP is designed on Water Coole condensers, this expansion project involves only
XXVI.	Air Cooled condensers shall be used in the captive power plant.	
XXVI.	The control of the co	condensers, this expansion project involves only
XXVI.	The control of the co	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption
XXVI.	The control of the co	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not be a superior of the condensers of the condensers of the condensers of the condensers.
XXVI.	The control of the co	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project.
XXVI.	The control of the co	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping.
XXVI.	captive power plant.	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revampine projects.
xxvi.	During operational phase at Captive Power	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revampine projects. We are ensuring coal dust exposures and maintain
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling areas.
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling areas. Annexed in Annexure-II.
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas.	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling areas. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling area. Annexed in Annexure-II. Heat stress analysis for the workmen is carried or and PPE'S given to workers as per site conditions.
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling areas Annexed in Annexure-II. Heat stress analysis for the workmen is carried or and PPE'S given to workers as per site condition SOP & nature of work.
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site condition SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the
	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as per site conductions.
xxvii.	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per Factories Act, 1948.	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling areas Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as perfactories Act, 1948.
xxvii.	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per Factories Act, 1948. As committed by the PP to adopt the five	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling areas Annexed in Annexure-II. Heat stress analysis for the workmen is carried or and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as per Factories Act, 1948 We have identified projects based on communications.
xxvii.	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per Factories Act, 1948. As committed by the PP to adopt the five revenue villages namely Ajoliya Ka Khera,	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as per Factories Act, 1948. We have identified projects based on community priorities and with significant local contributions.
xxvii.	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per Factories Act, 1948. As committed by the PP to adopt the five revenue villages namely Ajoliya Ka Khera, Biliya, Moonga Ka Khera, Nagri and Putholi,	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as perfactories Act, 1948. We have identified projects based on community priorities and with significant local contributions. We are implementing the submitted plan for sociological contributions.
xxvii.	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per Factories Act, 1948. As committed by the PP to adopt the five revenue villages namely Ajoliya Ka Khera, Biliya, Moonga Ka Khera, Nagri and Putholi, as a part of model village development plan,	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as perfactories Act, 1948. We have identified projects based on community priorities and with significant local contributions. We are implementing the submitted plan for socioleconomic development to develop them into model.
xxvii.	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per Factories Act, 1948. As committed by the PP to adopt the five revenue villages namely Ajoliya Ka Khera, Biliya, Moonga Ka Khera, Nagri and Putholi, as a part of model village development plan, project proponent shall strictly implement the	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as perfactories. Act, 1948 We have identified projects based on community priorities and with significant local contributions. We are implementing the submitted plan for socioleconomic development to develop them into modivillages.
xxvii.	During operational phase at Captive Power Plant, PP shall measure coal dust exposures and to maintain coal dust exposures within stipulated standards at coal handling areas. PP shall identify extreme hot areas through heat stress survey as well as noise monitoring within process plants to ensure that workers not exposed above 90 dBA levels as per Factories Act, 1948. As committed by the PP to adopt the five revenue villages namely Ajoliya Ka Khera, Biliya, Moonga Ka Khera, Nagri and Putholi, as a part of model village development plan,	condensers, this expansion project involves only Turbine Revamping. Air cooled condensers shall be considered for future expansion if any. No increase in water consumption in this proposal. Being an old unit, it is practically not possible to replace condensers during this project commissioning as this is only turbine revamping projects. We are ensuring coal dust exposures and maintain within stipulated standards at coal handling arease. Annexed in Annexure-II. Heat stress analysis for the workmen is carried on and PPE'S given to workers as per site conditions SOP & nature of work. Noise monitoring within process plants will be conducted before December 2024 to ensure the workers not exposed above 90 dBA levels as perfactories Act, 1948. We have identified projects based on community priorities and with significant local contributions. We are implementing the submitted plan for socioleconomic development to develop them into model.

disorders due to the project's operations. villages. PP shall extend the occupational Rainwater harvesting pits are constructed in the health monitoring to the villagers on a random basis to establish any health adjacent village and school. Plantation along the disorders due to the project's operations, PP roads, villages and schools and other suitable places shall also construct and maintain Rainwater has already developed. harvesting pits in the adiacent village and school. The PP shall develop avenue plantation along the roads, villages and schools and other suitable places. All the commitments made to the public We will ensure the satisfactory implementation of all the the commitments made to the public during the public during Public Hearing/Public Consultation hearing. The action plan based on the social impact shall be satisfactorily implemented. The action plan based on the assessment study of the project as per the EMP in social impact assessment study of the project accordance to the Ministry's OM dated 30.09.2020 as per the EMP in accordance to the will be implemented and progress will be submitted Ministry's OM dated 30.09.2020 shall be to the Regional office of MoEF&CC. strictly implemented and progress shall be submitted to the Regional Office of MoFF&CC The recommendations of the approved Site-Wild Life conservation plan is approved by PCCF Specific Wildlife Management Plan shall be Jaipur and will be implemented as submitted. implemented in consultation with the State Forest Department. The implementation report shall be furnished along with the sixmonthly compliance report to the concerned Regional Office of the MoEF&CC.

xxxi. The Plastic Waste Management Rules 2016. inter-alia, mandated banning of identified Single Use Plastic (SUP) items with effect from 01/07/2022 In this regard, CPCB has issued a direction to all the State Pollution Control Boards (SPCBs) Pollution Control Committees (PCCs) on 30/06/2022 to ensure the compliance of Notification published by Ministry on 12/08/2021 The technical guidelines issued by the CPCB in this regard available https://epcb.nic.in/technical_guidelines-3/ All the project proponents are hereby requested to sensitize and create awareness among people working within the Project area as well as its surrounding area on the ban of SUP in order to ensure the compliance of Notification published by this Ministry on 12/08/2021. A report, along photographs, on the measures taken shall also be included in the six monthly compliance report being submitted by the project proponents.

We have conducted awareness programs on the ban of SUP for the workers and people of nearby areas. Also distributed little was at cloth bags on behalf of world environment day 2024

SUP is banned at via. Commitment policy along with Bidder undertaking which is being ensured at site is attached as Annexure-XIX





xxxii. The project proponent shall adopt the Clean Air practices like mechanical collectors, wet scrubbers, fabric filters (bag houses). precipitators. combustion electrostatic systems (thermal oxidizers), condensers, absorbers, adsorbers, and biological degradation. Controlling emissions related to transportation shall include emission controls on vehicles as well as use of cleaner fuels. Sufficient numbers of additional truck mounted Fog/Mist water cannons shall be procured and operated regularly inside the project premises and also in the surrounding villages to arrest suspended dust in the atmosphere

pollution control To adopt clean land, allectors, wet scrubbers, equipments like fabric filter etc has the approvided

Linux's mounted with Fog/Mist Sufficient number water cannons have been operated inside the project premises regularly and docum surrounding villages to arrest suspended does not the atmosphere



Road washing

D. G	ENERAL CONDITIONS:	
I.	Statutory compliance:	
i.	The Environment Clearance (EC) granted to the project/ activity is strictly under the provisions of the EIA Notification, 2006 and its amendments issued from time to time. It does not tantamount/ construe to approvals/ consent/ permissions etc., required to be obtained or standards/conditions to be followed under any other	
	Acts/Rules/Subordinate legislations, etc., as may be applicable to the project.	
II.	Air quality monitoring and preservation	
i.	The project proponent shall install 24x7	Ta was assessed
	continuous emission monitoring system at process stacks to monitor stack emission as well as four Continuous Ambient Air Quality Station (CAAQS) one within and three outside the plant area at an angle of 120° each for monitoring AAQ parameters with respect to standards prescribed in Environment (Protection) Rules 1986 as amended from time to time. The CEMS and CAAQMS shall be connected to SPCB and CPCB online servers and calibrate these systems from time to time according to equipment supplier specification through labs recognized under Environment (Protection) Act, 1986 or NABL accredited laboratories.	Installed 24X7 continuous emission monitoring system at process stacks to monitor stack emission with respect to standards prescribed in Environment (Protection) Rules 1986 as amended from time to time and connected to SPCB and CPCB online servers and these systems are being calibrated according to equipment supplier specification through labs recognized under Environment (Protection) Act, 1986 or NABL accredited laboratories.
ii.	The project proponent shall monitor fugitive emissions in the plant premises at least once in every quarter through laboratories recognized under Environment (Protection) Act, 1986 or NABL accredited laboratories.	Fugitive emission monitoring is done by labs recognized under Environment (Protection) Act, 1986 or NABL accredited laboratories. Report annexed as Annexure-I.
iii.	office of CPCB and Regional Office of SPCB along with six-monthly monitoring report.	Stacks are connected with PCB server and data is being transferred regularly. Air quality monitoring, manual stack monitoring and manual air quality/fugitive emission reports are submitted to Regional Office of MoEF & CC, Zonal Office of CPCB and Regional Office to SPCB along with six monthly monitoring report. Manual stack monitoring report from Apr'24 to Sep'24 is attached as Annexure-IV. Continuous ambient air quality report from Apr'24 to Mar'24 is attached as Annexure-IX. Manual ambient air quality report is attached as Annexure-X. Continuous stack emission monitoring report is

Appropriate Air Pollution Control (APC)	7
system shall be provided for all the dust generating points including fugitive dust from all vulnerable sources, so as to comply prescribed stack emission and fugitive emission standards.	Appropriate Air Pollution Control (APC) system is provided for all the dust generating points including fugitive dust from all vulnerable sources, so as to comply prescribed stack emission and fugitive emission standards.
The project proponent shall provide leakage detection and mechanized bag cleaning facilities for better maintenance of bags.	Bag filter and differential pressure monitoring in place with periodic inspection system.
Pollution control system in the plant shall be provided as per the CREP Guidelines of CPCB.	CREP guidelines are strictly followed.
The project proponent shall ensure covered transportation and conveying of ore, coal and other raw material to prevent spillage and dust generation. Provide covered sheds for raw materials like	Transportation is being done in covered manner by wagons and trucky. Covered conveyers Raw material & Coal is being stored in covered shed,
coal, etc.	some coal in transit state is in open. Coal storage under the shed
	from all vulnerable sources, so as to comply prescribed stack emission and fugitive emission standards. The project proponent shall provide leakage detection and mechanized bag cleaning facilities for better maintenance of bags. Pollution control system in the plant shall be provided as per the CREP Guidelines of CPCB. The project proponent shall ensure covered transportation and conveying of ore, coal and other raw material to prevent spillage and dust generation.

		•
ix.	Practice use if low-sulphur tars for baking anodes.	We are not using low sulphur tars for baking anodes.
х.	Plant internal roads shall be concreted and	d Plant internal roads are concreted.
	sufficient number of mobile or stationer	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1
	vacuum cleaners shall be provided to clean	Contract to the contract to th
	plant roads, shop floors, roofs, regularly	
	shall be used to regularly clean the roads.	vehicles movement.
		Mobile Vaccum sweeper
xi.	Design the ventilation system for adequate	The state of the s
A).	air changes as per prevailing norms for all	() () () () () () () () () ()
	tunnels, motor houses, Oil Cellars.	
III.	Water quality monitoring and preservation	
i.	The project proponent shall install 24x7	The industry has already installed 24X7 continuous
***	continuous effluent monitoring system with	
	respect to standards prescribed in	
	Environment (Protection) Rules 1986 (G.S.R	and maintaining Zero Liquid discharge & no effluent
	414 (E) dated 30th May 2008; as amended	is discharged at any stage on the ground.
	from time to time and connected to SPCB	
	and CPCB online servers and calibrate these	
	system from time to time according to	
	equipment supplier specification through labs	
	recognised under Environment (Protection)	=
	Act, 1986 or NABL accredited laboratories.	
ii.	The project proponent shall monitor regularly	Ground water quality monitoring is being done and
	ground water quality at least twice a year	report is being submitted along with six monthly
	(pre and post-monsoon) at sufficient	compliance report.
	numbers of piezometers/sampling wells in	Ground water quality monitoring report is attached as
	the plant and adjacent areas through labs	Annexure-VII.
	recognised under Environment (Protection)	
	Act, 1986 and NABL accredited laboratories.	
iii.	The project proponent shall submit monthly	CLZS plant is maintaining zero liquid Discharge &
1500	summary report of continuous effluent	
	monitoring and results of manual stack	no effluent is discharged at any stage on the ground.
	monitoring and manual monitoring of air	Ground water quality is monitored & report is being
	quality / fugitive emission to Regional Office	submitted along with six monthly monitoring report.
	of MoEF&CC, Zonal office of CPCB and	
		Monthly summary report of continuous effluent

•

	Regional Office of SPCB along with six- monthly monitoring report.	monitoring is attached as Annexure-XII.
iv.	Sewage Treatment Plant shall be provided	Sewage water is being treated in STP plant at CLZ
	for treatment of domestic wastewater to meet	plant and Zinc Nagar.
	the prescribed standards.	SIP
ν.	Garland drains and collection pits shall be	Garland drains are available and merging with
	provided for each stock pile to arrest the run-	collection pits to arrest the run-off.
	off in the event of heavy rains and to check	
	the water pollution due to surface run off.	
vi.	The project proponent shall make efforts to	Industry is 100% recycling its wastewater through
	minimise water consumption in the plant	ETP, RO and MIL. Ireated wastewater is being
	complex by segregation of used water,	utilized in the process.
	practicing cascade use and by recycling	
	treated water.	
IV.	Noise monitoring and preventio	
i.	Noise quality shall be monitored as per the	Noise quality monitoring is done and report is
	prescribed Noise Pollution (Regulation and	annexed herewith six-monthly compliance report.
	Control) Rules, 2000 and report in this regard	Report is attached as Annexure-XI.
	shall be submitted to Regional Officer of the	
	Ministry as a part of six-monthly compliance	
	report.	
ii.	The ambient noise levels should conform to	The ambient noise levels are always within the
	1972 D 127 767 208 128 12 B 10256291 0 1276 M	The state of the s
	the standards prescribed under E(P) A Rules,	standards prescribed under EPA Rules 1986 viz 75
	the standards prescribed under E(P) A Rules, 1986 viz. 75 dB(A) during day time and 70	standards prescribed under EPA Rules,1986 viz. 75
	the standards prescribed under E(P) A Rules, 1986 viz. 75 dB(A) during day time and 70 dB(A) during night time.	standards prescribed under EPA Rules,1986 viz. 75 dBA (day time) and 70 dBA (night time).
V.	1986 viz. 75 dB(A) during day time and 70	
V.	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time.	dBA (day time) and 70 dBA (night time).
	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste	
	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of	dBA (day time) and 70 dBA (night time).
İŧ	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases.	dBA (day time) and 70 dBA (night time). Waste heat recovery system is in place.
	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases. Energy conservation measures may be	dBA (day time) and 70 dBA (night time). Waste heat recovery system is in place. Energy conservation measures are adopted:
İŧ	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases. Energy conservation measures may be adopted such as adoption of solar energy and	dBA (day time) and 70 dBA (night time). Waste heat recovery system is in place. Energy conservation measures are adopted: 1.In Offices and residential area LED lights available
İŧ	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases. Energy conservation measures may be adopted such as adoption of solar energy and provision of LED lights etc., to minimize the	dBA (day time) and 70 dBA (night time). Waste heat recovery system is in place. Energy conservation measures are adopted: LIn Offices and residential area LED lights available also under replacement as per requirement.
İŧ	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases. Energy conservation measures may be adopted such as adoption of solar energy and	dBA (day time) and 70 dBA (night time). Waste heat recovery system is in place. Energy conservation measures are adopted: 1.In Offices and residential area LED lights available also under replacement as per requirement. 2. Solar Power is generated at Hydro 2 CDSS /Lai
İŧ	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases. Energy conservation measures may be adopted such as adoption of solar energy and provision of LED lights etc., to minimize the	dBA (day time) and 70 dBA (night time). Waste heat recovery system is in place. Energy conservation measures are adopted: 1.In Offices and residential area LED lights available also under replacement as per requirement. 2. Solar Power is generated at Hydro 2 CDSS /La building, Hydro 1 leaching office, Switchyard control
İr	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases. Energy conservation measures may be adopted such as adoption of solar energy and provision of LED lights etc., to minimize the	dBA (day time) and 70 dBA (night time). Waste heat recovery system is in place. Energy conservation measures are adopted: 1.In Offices and residential area LED lights available also under replacement as per requirement. 2. Solar Power is generated at Hydro 2 CDSS /La
İr	1986 viz. 75 dB(A) during day time and 70 dB(A) during night time. Energy Conservation measures The project proponent shall provide waste heat recovery system (pre-heating of combustion air) at the flue gases. Energy conservation measures may be adopted such as adoption of solar energy and provision of LED lights etc., to minimize the	Waste heat recovery system is in place. Energy conservation measures are adopted: 1.In Offices and residential area LED lights available & also under replacement as per requirement. 2. Solar Power is generated at Hydro 2 CDSS /La building, Hydro 1 leaching office, Switchyard contror room building, Zinc School & Boy's Hostel/Utilit

VI.	Waste management	
i.		Presently 100 % utilization is being done and fly as
	All the fly ash shall be provided to cement	t is being sold to cement and brick manufactures.
	and cement brick manufacturers for further	is being sold to cement and orick manufactures.
	utilization to the	
	Understanding in this regard shall be	
	submitted to the Ministral - Basis - Loss	
ii.	submitted to the Ministry's Regional Office.	
11.	and metanic studge recovered	No oily scum generated, inorganic ETP sludge i
	from rolling mills ETP shall be mixed, dried,	disposed off in SLF in scientific manner after
	and briquetted and reused in melting	stabilization.
	Furnaces.	
111.	other mazardous	
	waste shall be disposed of as per the	
	Hazardous & Other waste (Management &	
	transboundary Movement) Rules, 2016 and	
	amendment thereof.	
iv.	Kitchen waste shall be composted or	Kitchen waste is being compost through OWC.
	converted to biogas for further use.	renent maste is being compost andagm on e.
VII.	Green Belt	
i.	The project proponent shall prepare GHG	CUC amissions inventors and adduction also is
1.		GHG emissions inventory and reduction plan is
	emissions inventory for the plant and shall	attached as Annexure-XIV.
	submit the programme for reduction of the	
	same including carbon sequestration	
	including plantation.	
11.	Project proponent shall submit a study report	Study report is attached as Annexure-XIV.
	on Decarbonisation program, which would	
	essentially consist of company's carbon	
	emissions, carbon budgeting/ balancing,	
	carbon sequestration activities and carbon	
	offsetting strategies. Further, the report shall	
	also contain time bound action plan to reduce	
	its carbon intensity of its operations and	
	supply chains, energy transition pathway	
	from fossil fuels to Renewable energy etc.	
	All these activities/ assessments should be	
	measurable and monitorable with defined	
	time frames", when PP comes for EC	
1	proposal. This study shall be formulated	
	keeping in view of India's Net-zero	
	commitment at the COP-26 Climate Summit.	
II.	Public hearing and Human health issues	
i.		Emergency preparedness plan is prepared and
1.	Hazard identification and Risk Assessment	implemented at site.
3	(HIRA) and Disaster Management Plan shall	
	be implemented.	Hant at a second of the second
ii.		Heat stress analysis for the workmen is carried out
	the for the workmen who work in	and PPE'S given to workers as per site condition,
	stress analysis for the workmen who work in high temperature work zone and provide	and TTE 5 given to workers as per site condition,

	Personal Protection Equipment (PPE).	SOP & nature of work.
iii		All project related labours are local & from near by area, No stay arrangement required. We have site facility of medical, safe drinking water, wash/rest house.
iv.		PME is being done of workers on regular basis and record is being maintained.
IX.	Environment Management	
i.	The project proponent shall comply with the provisions contained in this Ministry's OM vide F.No. 22-65/2017-IA.III dated 30/09/2020.	Noted & will be complied
ii.	The company shall have a well laid down environmental policy duly approve by the Board of Directors. The environmental policy should prescribe for standard operating procedures to have proper checks and balances and to bring into focus any infringements/deviation/violation of the environmental / forest / wildlife norms / conditions. The company shall have defined system of reporting infringements / deviation / violation of the environmental / forest / wildlife norms / conditions and / or shareholders / stake holders. The copy of the board resolution in this regard shall be submitted to the MoEF&CC as a part of sixmonthly report.	Company has environment policy duly approved by Board of Director. Annexed as Annexure-XVI.
iii.	A separate Environmental Cell both at the project and company head quarter level, with qualified personnel shall be set up under the control of senior Executive, who will directly to the head of the organization.	A separate Environmental Cell both at the project and company head quarter level, with qualified personnel already set up under the control of Associate General Manager, he directly reports to the head of the organization.
X.	Miscellaneous	
8	environmental clearance granted for their project along with the environmental conditions and safeguards at their cost by	Environment clearance granted for this project published in two local newspapers of District or state and this EC is displayed in company website permanently. Refer Annexure- XVII-A & B.

	website permanently.	
ii.		
	shall be submitted by the mail	
	shall be submitted by the project proponents	& RSPCB office of Chittorgarh.
	to the Heads of local bodies, Panchayats and	Refer Annexure-XVIII
	Municipal Bodies in addition to the relevant	
	offices of the Government who in turn has to	
	display the same for 30 days from the date of	
	receipt.	
iii.	The project proponent shall upload the status	Compliance of environment clearance condition
	of compliance of the stipulated environment	including results of most of the total of the
	clearance conditions, including results of	
	monitored data on their website and update	company website and updated on half yearly basis.
	the same on half-yearly basis.	
iv.	The project proposest 1.11	
	The project proponent shall monitor the	Ambient levels as well as stack emission is displaye
	criteria pollutants level namely; PM10, SO2,	at company outer gate and put on the website of th
	NOx (ambient levels as well as stack	company along with half yearly compliance report.
	emissions) or critical sectoral parameters,	***************************************
	indicated for the projects and display the	1
	same at a convenient location for disclosure	
	to the public and put on the website of the	
	company.	
V.	The project proponent shall submit six-	Six monthly Environment Clearance compliance
	monthly reports on the status of the	
	compliance of the stipulated environmental	report submitted on regular basis.
	conditions on the website of the ministry of	Here we are submitting report for the period of
	Environment, Forest and Climate Change at	April'2024 to September'2024.
	environment clearance portal.	
vi.		
* 1.	The project proponent shall submit the environmental statement for each financial	Environment statement for each financial year is
	environmental statement for each financial	being submitted in Form V to State Pollution Control
	year in Form-V to the concerned State	Board as prescribed under the Environment
	Pollution Control Board as prescribed under	(Protection) Rules,1986 as amended subsequently and
	the Environment (Protection) Rules, 1986, as	put on the website of the company.
	amended subsequently and put on the	, p
	website of the company.	
vii.	The project proponent shall inform the	Agreed. All the details of plant activities is informed
	Regional Office as well as the Ministry, the	to RO & MoEF.
	date of financial closure and final approval of	
	the project by the concerned authorities,	
	commencing the land development work and	
	start of production operation by the project.	
iii.		Noted 9 in Land
	commitments and recommendations made in	Noted & is been complied.
	the EIA/EMP report, commitment made	
	during Public Hearing and also that during	
	their presentation to the Expert Appraisal	
	Committee.	
х.	The PP shall put all the environment related	Noted & is been complied.
	expenditure, expenditure related to Action	

	Plan on the PH issues, and other commitments made in the EIA/EMP Report etc. in the company web site for the information to public/public domain. The PP shall also put the information on the left over funds allocated to EMP and PH as committed in the earlier ECs and shall be carried out and spent in next three years, in the company web site for the information to public/public domain.	
х.	No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment, Forests and Climate Change (MoEF&CC).	Agreed. No further expansion or modifications in the plant is carried out without prior approval of the Ministry of Environment. Forests and Climate Change (MoEF & CC).
xi.	The Regional Office of this Ministry shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data / information/monitoring reports.	Agreed and we extend full cooperation of the officer (S) of the Regional Office by furnishing the requisite data/information/monitoring reports.

Annexure - I

HINDUSTAN ZINC LIMITED

CHANDERIA LEAD ZINC SMELTER

Work Zone (8 - Hours) Environment Monitoring Results

(Apr'24 - Sept'24)

Month Location	Parameters/ Unit	Prescribed Standards*	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
			Pyro Pl	ant				
	SPM mg/m ³	10	0.76	0.838	0.448	0.54	0.31	0.451
	SO ₂ mg/m ³	5	NIL	NIL	0.012	NIL	NIL	0.011
Pyro RMH	Zn mg/m ³	5	0.089	0.114	BDL	0.05	0.027	BDL
	Pb mg/m ³	0.15	BDL	BDL	< 0.1	BDL	BDL	< 0.05
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL
Pyro Sinter Area	SPM mg/m ³	10	0.83	0.754	0.491	0.491	0.594	0.485
	SO ₂ mg/m ³	5	NIL	NIL	0.012	NIL	NIL	0.014
	Zn mg/m ³	5	0.113	0.099	BDL	0.064	0.068	BDL
	Pb mg/m ³	0.15	BDL	BDL	< 0.1	BDL	BDL	< 0.05
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	10	0.92	0.901	0.518	0.852	0.732	0.523
DD Cooting	SO ₂ mg/m ³	5	NIL	NIL	0.012	NIL	NIL	0.011
LRP Casting	Zn mg/m ³	5	0.104	0.086	BDL	0.075	0.034	BDL
Area	Pb mg/m ³	0.15	BDL	BDL	< 0.1	BDL	BDL	< 0.05
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	10	0.87	0.807	0.390	0.914	0.72	0.980
DDV 5	SO ₂ mg/m ³	5	NIL	NIL	0.011	NIL	NIL	0.010
LRP K-5	Zn mg/m ³	5	0.088	0.062	BDL	0.084	0.026	BDL
Dross Area	Pb mg/m ³	0.15	BDL	BDL	< 0.1	BDL	BDL	< 0.05
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL

Manisha Bhati

Manager - Environment

Annexure - I

HINDUSTAN ZINC LIMITED CHANDERIA LEAD ZINC SMELTER

Work Zone (8 - Hours) Environment Monitoring Results

(Apr'24 - Sept'24)

Month Location	Parameters/ Unit	Prescribed Standards*	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept*24
		C	PP, H-1 & I	I-2 Plant			-	
	SPM mg/m ³	10	0.404	0.377	0.479	0.515	0.471	0.485
H-1	SO ₂ mg/m ³	5	NIL	NIL	0.012	NIL	NIL	0.013
Purification	Zn mg/m ³	5	0.077	0.069	BDL	0.098	0.090	BDL
. arrication	Pb mg/m ³	0.15	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	10	0.116	0.202	0.449	0.331	0.229	0.456
H-1 Cell House	SO ₂ mg/m ³	5	NIL	NIL	0.013	0.096	0.144	0.010
	Zn mg/m ³	5	BDL	BDL	BDL	BDL	BDL	BDL
	Pb mg/m ³	0.15	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	10	0.302	0.422	0.482	0.417	0.368	0.491
H-2	SO ₂ mg/m ³	5	NIL	NIL	0.012	NIL	NIL	0.011
Purification	Zn mg/m ³	5	0.056	0.073	BDL	0.077	0.070	BDL
Fullication	Pb mg/m ³	0.15	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	10	0.15	0.144	0.471	0.194	0.179	0.485
	SO ₂ mg/m ³	5	NIL	NIL	0.010	0.095	0.156	0.012
H-2 Cell	Zn mg/m ³	5	BDL	BDL	BDL	BDL	BDL	BDL
House	Pb mg/m ³	0.15	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	10	0.457	0.587	0.468	0.762	0.562	0.471
	SO ₂ mg/m ³	5	NIL	NIL	0.010	NIL	NIL	0.011
CPP Coal	Zn mg/m ³	5	0.04	0.04	BDL	0.052	0.021	BDL
Yard	Pb mg/m ³	0.15	BDL	BDL	< 0.1	BDL	BDL	< 0.05
	Cd mg/m ³	0.05	BDL	BDL	BDL	BDL	BDL	BDL

Manisha Bhati

Manager - Environment

Annexure - II

HINDUSTAN ZINC LIMITED CHANDERIA LEAD ZINC SMELTER

Work Zone (15 - Minute) Environment Monitoring Results

(Apr'24 - Sept'24)

Month Location	Parameters/ Unit	Prescribed Standards*	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
			Pyro Pl	ant				
	SPM mg/m ³	-	2.66	4.66	4.33	3.00	2.33	3.33
	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
Pyro RMH	Zn mg/m³	10	0.04	0.08	0.07	0.04	0.03	0.04
	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	-	4.33	3.66	2.00	3.00	2.00	4.33
Pyro Sinter	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
Area	Zn mg/m ³	10	0.06	0.06	0.02	0.04	0.03	0.07
Aica	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	12	4.00	3.00	3.66	1.66	2.33	4.00
LRP Casting	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
Area	Zn mg/m ³	10	0.07	0.05	0.05	0.02	0.03	0.07
Alea	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	:₩:	5.33	4.33	4.66	3.00	4.33	4.00
I DD I/ 6	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
LRP K-5	Zn mg/m ³	10	0.07	0.07	0.07	0.03	0.06	0.05
Dross Area	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL

Manisha Bhati

Manager - Environment

Annexure - II

HINDUSTAN ZINC LIMITED

CHANDERIA LEAD ZINC SMELTER

Work Zone (15 - Minute) Environment Monitoring Results

(Apr'24 - Sept'24)

Month Location	Parameters/ Unit	Prescribed Standards*	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
		C	PP, H-1 & I	H-2 Plant				
	SPM mg/m ³	-	2.00	1.33	1.66	2.00	1.66	2.33
H-1	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
n-1 Purification	Zn mg/m ³	10	0.02	0.02	0.02	0.03	0.02	0.03
	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	1-1	4.00	3.00	5.00	4.33	2.66	3.66
H-1 Roaster	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
Area	Zn mg/m ³	10	0.05	0.03	0.06	0.06	0.03	0.05
Area	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	-	4.33	2.33	1.33	2.33	1.33	2.00
H-2	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
Purification	Zn mg/m ³	10	0.07	0.03	0.02	0.04	0.02	0.02
1 uniteation	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	=	2.33	5.33	5.00	2.00	2.66	2.66
H-2 Roaster	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
Area	Zn mg/m ³	10	0.04	0.07	0.07	0.03	0.03	0.03
, neu	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL
	SPM mg/m ³	<u>-</u>	3.66	5.33	2.33	4.00	3.33	1.66
CPP Coal	SO ₂ mg/m ³	10	NIL	NIL	NIL	NIL	NIL	NIL
Yard	Zn mg/m ³	10	BDL	BDL	BDL	BDL	BDL	BDL
ı ulu	Pb mg/m ³	0.45	BDL	BDL	BDL	BDL	BDL	BDL
	Cd mg/m ³	0.2	BDL	BDL	BDL	BDL	BDL	BDL

BDL- Below Detection Limit (The measurement of uncertainty at 95% confidence level is 0.004 Abs. in AAS)

Manisha Bhati Manager - Environment

Annexure - III

HINDUSTAN ZINC LIMITED

CHANDERIA LEAD ZINC SMELTER

STACK HEIGHT

S. No.	Stack Attached to	Height(m)
Ausmelt		Tiergin(iii)
1	Dust extraction system of feed handling	25
2	Hygiene and ventilation system	35
3	Ausmelt furnace	30
4	SO ₂ absorption tower	52
Hydro 1		
1	Zinc dross milling bag filter	20
2	Zinc atomizing bag filter (Zinc Dust)	30
3	Zinc melting furnace bag filter (1st stack)	30
4	Zinc melting furnace bag filter (2nd stack)	30
5	Acid plant	30
Pyro		100
1	Sinter Venturi	45
2	Sinter Main	
3	Crusher Venturi	75
4	Crusher Main	75 75
5	ISF slagging floor	
6	ZRP fume extraction	75
7	ZRP (Main) ventilation stack	35
8	LRP Main	75 75
9	Copper Recovery Plant	30
10	LRP Copper Drossing	
11	PYRO Acid Plant (TGT)	34
Hydro 2	(101)	75
1	Zinc Melting Furnace bag filter – 1	30
2	Zinc Melting Furnace bag filter - 2	30
3	Zinc Dross Milling bag filter	30
4	Zinc atomizing bag filter (Zinc Dust)	30
5	Acid plant	100
CPP		100
1	Captive power plant 154 MW	165
2	Captive power plant 100 MW	165
3	Coal Crusher	20

Manisha Bhati

Managar - Environment

Chanderia Lead Zinc Smelter

Stack Monitoring Results (PM & LEAD)

(Apr'24 - Sept'24)

Location	Parameters	Limit	Unit	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
C	PM	150	Mg/Nm ³	18.17	20.68	35.9	34.94	34.71	34.2
Sinter Main	Lead	10	Mg/Nm ³	2.80	3.09	2.28	6.13	5.57	2.26
Sinter Venturi	PM	150	Mg/Nm ³	NA	NA	NA	36.45	49.86	35.9
	Lead	10	Mg/Nm ³	NA	NA	NA	1.99	5.35	2.84
Crusher	PM	150	Mg/Nm ³	23.53	24.47	37.8	41.94	39.79	36.1
Main	Lead	10	Mg/Nm ³	1.63	1.74	3.01	2.87	3.31	2.98
Crusher	PM	150	Mg/Nm ³	11.49	14.21	37.4	16.24	14.59	36.5
Venturi	Lead	10	Mg/Nm ³	0.96	1.37	2.08	1.57	1.49	1.98
	PM	150	Mg/Nm ³	27.27	24.12	38.6	21.52	16.70	37.6
LRP Main	Lead	10	Mg/Nm ³	3.24	2.72	1.68	8.50	6.02	1.55
	PM	150	Mg/Nm ³	12.54	11.39	9.82	PSD	PSD	PSD
ZRP Main	Lead	10	Mg/Nm ³	BDL	BDL	BDL	PSD	PSD	PSD
	PM	150	Mg/Nm ³	19.29	17.83	22.33	PSD	PSD	PSD
ZRP Fume	Lead	10	Mg/Nm ³	BDL	BDL	BDL	PSD	PSD	PSD

^{*}PSD - Plant Under Shut Down *

Manisha Bhati

Manager - Environment

^{*}NA- Not Analyzed due to plant was under maintenance*

Chanderia Lead Zinc Smelter Stack Monitoring Results (PM & LEAD)

(Apr'24 - Sept'24)

Location	Parameters	Limit	Unit	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
LRP Copper Drossing	PM	150	Mg/Nm ³	10.78	12.32	36.8	12.44	13.57	35.2
	Lead	10	Mg/Nm ³	0.91	0.99	2.19	4,72	5.38	2.26
SF Slagging	PM	150	Mg/Nm ³	94.92	67.95	33.5	59.83	67.81	32.5
Floor	Lead	10	Mg/Nm ³	7.12	9.58	2.14	7.95	6.82	2.06
CRP Milling	PM	150	Mg/Nm ³	9.62	7.76	8.40	11.52	17.16	24.33
	Lead	10	Mg/Nm ³	0.50	0.33	0.42	0.81	1.39	2.23
Ausmelt	PM	30	Mg/Nm ³	26.12	28.53	29.3	8.89	9.09	28.3
RMH	Lead	10	Mg/Nm ³	2.08	2.57	2.16	1.41	1.38	2.13
Ausmelt Hygiene	PM	30	Mg/Nm ³	8.53	13.46	27.3	15.56	16.05	28.5
	Lead	10	Mg/Nm ³	0.40	0.80	2.24	0.64	0.53	2.32

Manisha Bhati

Manager - Environment

Chanderia Lead Zinc Smelter

Stack Monitoring Results (PM)

(Apr'24 - Sept'24)

Location	Parameters	Limit	Unit	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
H-1 ZMC – 1	PM	30	Mg/Nm ³	18.44	22.44	21.4	10.53	13.22	20.7
H-1 ZMC – 2	PM	30	Mg/Nm ³	13.87	18.32	21.9	11.70	10.41	20.4
H-1 Zinc Dust	PM	30	Mg/Nm ³	21.59	15.98	20.6	9.89	8.55	19.9
H-1 Zinc Dross	PM	30	Mg/Nm ³	19.88	13.86	18.7	15.93	24.70	17.6
H-2 ZMC -1	PM	30	Mg/Nm ³	17.19	19.48	20.6	13.30	15.10	19.8
H-2 ZMC-2	PM	30	Mg/Nm ³	12.86	13.15	18.8	12.39	10.82	19.2
H-2 Zinc Dross	PM	30	Mg/Nm ³	22.03	18.29	22.3	25.79	21.24	21.3
H-2 Zinc Dust	PM	30	Mg/Nm ³	19.40	9.97	19.2	9.43	7.84	18.6
	PM	50	Mg/Nm ³	41.12	28.77	37.1	18.35	39.06	36.2
CPP (154 MW) Unit - 1 & 2	SO ₂	600	Mg/Nm ³	525.79	457.78	930.8	474.86	397.97	925.6
	NOx	450	Mg/Nm ³	NA	NA	349.8	NA	NA	342.5
	Hg	0.03	Mg/Nm ³	NA	NA	< 0.01	NA	NA	< 0.01
	PM	50	Mg/Nm ³	28.40	31.84	29.3	41.79	45.23	31.2
CPP (100 MW) Unit – 3	SO ₂	600	Mg/Nm ³	756.11	387.71	970.4	335.98	358.23	975.5
3000000 TU	NO _x	450	Mg/Nm ³	NA	NA	360.8	NA	NA	365.2
	Нд	0.03	Mg/Nm ³	NA	NA	< 0.01	NA	NA	< 0.01
Coal Crusher	PM	50	Mg/Nm ³	5.29	8.19	26.9	7.87	9.35	25.3

NA - Not Analyzed

Manisha Bhati

Manager - Environment

Chanderia Lead Zinc Smelter Treated Water Monitoring Results

(Apr'24 - Sept'24)

ETP Outlet- (Hydro - 2)

S.NO.	Parameter	Unit	Limit	Result Apr-Jun'24	Result Jul-Sept'24
1	рН	-	5.5-9.0	7.35	7.32
2	Chloride	Mg/I	1000	83.7	80.2
3	Oil & Grease	Mg/I	10.0	< 4.0	BLQ(LOQ-4.0)
4	Total Residual Chlorine	Mg/l	1.0	0.44	0.48
5	Ammonical Nitrogen (as N)	Mg/l	50.0	< 1.0	BLQ(LOQ-1.0)
6	Nitrate (as NO ₃)	Mg/I	10.0	4.92	5.03
7	BOD	Mg/l	30	20.0	19.0
8	COD	Mg/l	250	118.9	115.5
9	TSS	Mg/l	100	57.0	59.0
10	Fluoride (as F)	Mg/l	2.0	0.84	0.81
11	Sulphate	Mg/l	1000	140.5	145.5

Manisha Bhati

Manager - Environment

Chanderia Lead Zinc Smelter Treated Water Monitoring Results

(Apr'24 - Sept'24)

ETP Outlet - (Hydro - 2)

S.NO.	Parameter	Unit	Limit	Result Apr-Jun'24	Result Jul-Sept'24
12	Phosphate (as P)	Mg/I	5.0	0.82	0.85
13	Cyanide	Mg/I	0.2	Absent	Absent
14	Hexavalent Chromium	Mg/l	0.1	< 0.05	BLQ(LOQ-0.05)
15	Cadmium	Mg/I	2.0	< 0.001	BLQ(LOQ-0.001)
16	Total Chromium	Mg/I	2.0	< 0.005	BLQ(LOQ-0.005)
17	Copper (as Cu)	Mg/I	1.0	0.053	0.056
18	Iron (as Fe)	Mg/l	1.0	0.41	0.49
19	Lead (as Pb)	Mg/l	0.1	< 0.005	BLQ(LOQ-0.005)
20	Nickel (as Ni)	Mg/I	3.0	< 0.01	BLQ(LOQ-0.01)
21	Zinc (as Zn)	Mg/I	1.0	0.57	0.61

Manisha Bhati

Manager - Environment

Chanderia Lead Zinc Smelter

Treated Water Monitoring Results

(Apr'24 - Sept'24)

ETP Outlet - (PYRO)

S.NO.	Parameter	Unit	Limit	Result Apr-Jun'24	Result Jul-Sept'24
1	рН	-	5.5-9.0	7.29	7.23
2	Chloride	Mg/l	1000	82.4	85.5
3	Oil & Grease	Mg/l	10.0	< 4.0	BLQ(LOQ-4.0)
4	Total Residual Chlorine	Mg/l	1.0	0.33	0.36
5	Ammonical Nitrogen (as N)	Mg/l	50.0	< 1.0	BLQ(LOQ-1.0)
6	Nitrate (as NO ₃)	Mg/l	10.0	4.92	5.06
7	BOD	Mg/l	30	22.0	21.0
8	COD	Mg/l	250	128.6	125.5
9	TSS	Mg/I	100	54.0	56.0
10	Fluoride (as F)	Mg/l	2.0	0.71	0.75
11	Sulphate	Mg/l	1000	148.2	151.2

Manisha Bhati

Manager - Environment

Chanderia Lead Zinc Smelter Treated Water Monitoring Results

(Apr'24 - Sept'24)

ETP Outlet - (PYRO)

S.NO.	Parameter	Unit	Limit	Result Apr-Jun'24	Result Jul-Sept'24
12	Phosphate (as P)	Mg/I	5.0	0.74	0.78
13	Cyanide	Mg/l	0.2	Absent	Absent
14	Hexavalent Chromium	Mg/l	0.1	< 0.05	BLQ(LOQ-0.05)
15	Cadmium	Mg/l	2.0	< 0.001	BLQ(LOQ-0.001)
16	Total Chromium	Mg/I	2.0	< 0.005	BLQ(LOQ-0.005)
17	Copper (as Cu)	Mg/l	1.0	0.052	0.056
18	Iron (as Fe)	Mg/I	1.0	0.25	0.26
19	Lead (as Pb)	Mg/l	0.1	< 0.005	BLQ(LOQ-0.005)
20	Nickel (as Ni)	Mg/I	3.0	< 0.01	BLQ(LOQ-0.01)
21	Zinc (as Zn)	Mg/I	1.0	0.42	0.45

Manisha Bhati

Manager - Environment Chanderia Lead Zinc Smelter

Chanderia Lead Zinc Smelter <u>Water Monitoring Results</u>

(Apr'24 - Sept'24)

Bearach River Up Stream Report

Parameter	Unit	Limit	Result Apr-Jun'24	Result Jul-Sept'24
pH	-	6.5 – 8.5	8.27	8.04
Zinc	Mg/l	15.0	0.331	0.276
Lead	Mg/l	0.1	BDL	BDL
Cadmium	Mg/I	0.01	BDL	BDL
Copper	Mg/l	1.5	BDL	BDL
Iron	Mg/I	5.0	BDL	BDL
Hardness	Mg/I	600	236	204
Chloride	Mg/l	600	86.2	78.1
Sulphate	Mg/I	1000	110.9	96.8
TDS	Mg/l	1500	975	1028

Manisha Bhati

Manager - Environment

Chanderia Lead Zinc Smelter Water Monitoring Results

(Apr'24 - Sept'24)

Bearach River Down Stream Report

Parameter	Unit	Limit	Result Apr-Jun'24	Result Jul-Sept'24
рН	-	6.5 - 8.5	8.11	8.12
Zinc	Mg/l	15.0	0.306	0.244
Lead	Mg/l	0.1	BDL	BDL
Cadmium	Mg/I	0.01	BDL	BDL
Copper	Mg/l	1.5	BDL	BDL
Iron	Mg/I	5.0	BDL	BDL
Hardness	Mg/I	600	224	220
Chloride	Mg/I	600	96.7	81.4
Sulphate	Mg/l	1000	89.8	89.9
TDS	Mg/I	1500	942	1065

^{*}BDL- Below Detection Limit (The measurement of uncertainty at 95% confidence level is 0.004 Abs. in AAS)*

Manisha Bhati

Manager - Environment

Chanderia Lead Zinc Smelter

(Piezometer Borewell Results Apr'24 - Jun'24)

S.	Location	pН	Zn	Pb	Cd	Hardness	Chloride	Sulphate	TDS
NO.	Limit (IS: 10500)	6.5-8.5	5.0-15.0	0.01	0.003	200-600	250-1000	200-400	500-200
1	Piezo Borewell-1	7.24	< 0.01	< 0.005	< 0.001	410.0	85.5	120.3	780.0
2	Piezo Borewell-2	7.12	< 0.01	< 0.005	< 0.001	43.0	75.6	123.5	890.0
3	Piezo Borewell-3				D	RY	0.823033		
4	Piezo Borewell-4	7.26	< 0.01	< 0.005	< 0.001	469.0	120.5	201.5	1020.0
5	Piezo Borewell-5	7.28	< 0.01	< 0.005	< 0.001	425.0	85.6	134.5	956.0
6	Piezo Borewell-6	7.22	< 0.01	< 0.005	< 0.001	502.0	132.5	210.3	1056.0
7	Piezo Borewell-7	7.19	< 0.01	< 0.005	< 0.001	478.0	95.6	154.2	989.0
8	Piezo Borewell-8	7.29	< 0.01	< 0.005	< 0.001	398.0	79.5	136.5	990.0
9	Piezo Borewell-9	7.21	< 0.01	< 0.005	< 0.001	488.0	110.5	240.3	1202.0
10	Piezo Borewell-10	7.36	< 0.01	< 0.005	< 0.001	456.0	102.5	231.2	1054.0
11	Piezo Borewell-11	7.18	< 0.01	< 0.005	< 0.001	402.0	95.6	154.7	989.0
12	Piezo Borewell-12	7.29	< 0.01	< 0.005	< 0.001	502.0	140.5	236.5	1123.0
13	Piezo Borewell-13				DR		140.5	250.5	1123.0
14	Piezo Borewell-14	7.19	< 0.01	< 0.005	< 0.001	452.0	95.8	142.5	1058.0
15	Piezo Borewell-15	7.22	< 0.01	< 0.005	< 0.001	415.0	105.6	214.2	
16	Piezo Borewell-16	7.18	< 0.01	< 0.005	< 0.001	540.0	180.5		1069.0
17	Piezo Borewell-17	7.17	< 0.01	< 0.005	< 0.001	475.0	110.5	284.6	1256.0
18	Piezo Borewell-18	7.34	< 0.01	< 0.005	< 0.001	412.0	110.9	236.5 265.4	1036.0
19	Piezo Near Fumer				DR		110.5	203.4	1056.0
20	Piezo Near Borrow pit	7.22	0.075	< 0.005	< 0.001	486.0	210.9	209.9	1418.0
21	Piezo Near RO Reject Pond	6.84	0.078	< 0.005	< 0.001	594.0	198.2	190.5	1974.0

Manisha Bhati

Manager- Environment

Annexure - VII

HINDUSTAN ZINC LIMITED

Chanderia Lead Zinc Smelter

(Piezometer Borewell Results Jul'24 - Sept'24)

S.	Location	pН	Zn	Pb	Cd	Hardness	Chloride	Sulphate	TDS
NO.	Limit (IS: 10500)	6.5-8.5	5.0-15.0	0.01	0.003	200-600	250-1000	-	
1	Piezo Borewell-1	7.26	< 0.01		T INCHES AND THE		1000000	200-400	500-2000
2	Piezo Borewell-2	7.16	< 0.01	< 0.005	< 0.001	248.0	44.9	75.9	402.0
3	Piezo Borewell-3	7.15	< 0.01	< 0.005	< 0.001	436.0	72.9	125.5	892.0
4	Piezo Borewell-4	7.23		< 0.005	< 0.001	268.0	35.5	76.5	401.0
5	Piezo Borewell-5	7.26	< 0.01	< 0.005	< 0.001	475.0	125.5	210.5	1023.0
6	Piezo Borewell-6	W. 175.115	< 0.01	< 0.005	< 0.001	430.0	82.5	132.0	975.0
7	Piezo Borewell-7	7.16	< 0.01	< 0.005	< 0.001	512.0	135.6	312.5	1068.0
8	Piezo Borewell-8	7.23	< 0.01	< 0.005	< 0.001	478.0	94.6	162.5	1023.0
9	Piezo Borewell-9	7.23	< 0.01	< 0.005	< 0.001	495.0	93.5	162.5	1023.0
10		7.23	< 0.01	< 0.005	< 0.001	502.0	93.5	156.2	998.0
1000	Piezo Borewell-10	7.25	< 0.01	< 0.005	< 0.001	462.0	105.5	235.5	1056.0
11	Piezo Borewell-11	7.15	< 0.01	< 0.005	< 0.001	415.0	93.5	300000000000000000000000000000000000000	
12	Piezo Borewell-12	7.25	< 0.01	< 0.005				152.6	989.0
13	Piezo Borewell-13		0.01	< 0.003	< 0.001	512.0	143.5	230.5	1140.0
14	Piezo Borewell-14	7.15			DR	Y			
15	Piezo Borewell-15	7.15	< 0.01	< 0.005	< 0.001	466.0	93.2	145.5	1065.0
16		7.18	< 0.01	< 0.005	< 0.001	425.0	110.6	218.5	1078.0
17	Piezo Borewell-16	7.26	< 0.01	< 0.005	< 0.001	556.0	185.9	290.5	1274.0
	Piezo Borewell-17	7.19	< 0.01	< 0.005	< 0.001	480.0	112.5	240.5	
18	Piezo Borewell-18	7.31	< 0.01	< 0.005	< 0.001	420.0	115.5		1042.0
19	Piezo Near Fumer	7.26	0.068	< 0.005	< 0.001	522.0		270.5	1062.0
20	Piezo Near Borrow pit	7.18	< 0.01	< 0.005	< 0.001	499.0	178.6 215.5	208.0	1130.0
21	Piezo Near RO Reject Pond	6.91	< 0.01	< 0.005	< 0.001	601.0	195.5	189.6	1423.0

Manisha Bhati

Manager- Environment

Annexure - VIII

HINDUSTAN ZINC LIMITED Chanderia Lead Zinc Smelter Complex

Putholi, Chanderia, Dist. Chittorgarh, Rajasthan.

ACID PLANT MONITORING (Apr'24 - Sept'24)

$\begin{array}{c} \textbf{Month} \rightarrow \\ \textbf{Location} \downarrow \end{array}$	Parameters	Prescribed Limits	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
Acid Plant H ₂ SO ₄ F	SO ₂ (1 Kg/T of H ₂ SO ₄ Productio n) =135 PPM	135 ppm	98.11	106.14	76.4	100.04	95.04	75.2
=2 ws	Acid Mist	30 (mg/nm ³)	29.03	25.90	17.8	27.04	26.89	16.9
Acid Plant (Hydro-2)	SO ₂ (1 Kg/T of H ₂ SO ₄ Productio n) = 135 PPM	135 ppm	96.58	94.76	69.8	109.32	117.13	68.5
	Acid Mist	30 (mg/nm ³)	29.28	28.33	13.7	25.96	24.34	12.3
Acid Plant TGT	SO ₂ (2 Kg/T of H ₂ SO ₄ Productio n) =224 PPM	224 ppm	92.26	78.96	81.9	36.81	48.91	79.6
(Pyro)	Acid Mist	50 (mg/nm ³)	0 (mg/nm³) 23.62	25.09	19.7	26.08	28.14	18.5
Cansolve acid plant	SO ₂ (1 Kg/T of H ₂ SO ₄ Productio n) =111 PPM	111 ppm	106.87	109.30	90.8	108.69	98.82	89.3
(Ausmelt)	Acid Mist	30 (mg/nm ³)	25.19	29.14	21.3	27.41	30.22	20.5

Manisha Bhati

Manager- Environment

Annexure - IX HINDUSTAN ZINC LIMITED

Chanderia Lead Zinc Smelter

Ambient Air Quality (CAAQM) Report

AMBIENT AIR QUALITY STATUS OF CLZS

Direction West

		CAAQM	S NO.1 (N	ear C1 O	ffice)		
			LOCAT				
Parameter	Standard of AAQ	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
PM 2.5	60	31.52	33.24	17.41	10.53	8.42	12.27
PM 10	100	72.66	72.15	38.29	23.86	5200.000	13.37
SO_X	80	9.82	22.25	7.02		19.34	31.81
NO_X	80	23.72	48.79		8.03	11.15	11.47
CO	2	0.80		17.75	13.83	13.1	13.64
		0.80	0.91	0.5	0.50	0.44	0.56

Direction East

			S NO.2 (DI LOCATI				
Parameter	Standard of AAQ	Apr'24	May'24	Jun'24	Jul'24	412.4	0
PM 2.5			5-1 E-100-10	Jun 24	3u1 24	Aug'24	Sept'24
- No. 200 (1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1900 - 1	60	27.3	30.02	23.45	15.45	17.34	23.4
PM 10	100	71.79	75.7	52.76	31.23	27.22	
SO_X	80	NA	NA	NA			41.44
NO_X	80	25.24	22.33		22.35	18.76	16.96
CO	2			17.24	14.13	16.75	15.5
Remarks	4	1.05	1.09 Ox analyser	1.32	1.04	0.72	1.11

Direction South

		CAAQMS	S NO.3 (Ch	ittorgarh	Fort)		
			LOCATI	ION	1011)		
Parameter	Standard of AAQ	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
PM 10	100	82.8	78.5	57.0	40.6		
SO_X	80	22.1	22.4	18.0	40.6	37.7	38.6
NO_X	80	8.8	7.8		14.9	14.7	13.1
		0.0	7.0	6.6	5.1	4.9	4.9

Direction North

		CAAQ	MS NO.4	(Pond No	1)						
	LOCATION										
Parameter	Standard of AAQ	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24				
PM 2.5	60	32.19	NA	57.91	35.47	26.5	24.79				
PM 10	100	82.66	NA	92.97	72.95	52.14	38.42				
SO_X	80	16.47	NA	23.92	17.93	30.17	11.84				
NO_X	80	38.11	NA	32.52	10.92	15.46	25.36				
CO	2	NA	NA	0.76	0.72	0.88	1.01				
Remarks		Analyser was Under Maintenance in May'24									

Direction North

		CAAQMS	NO.5 (Ra	ilway Ya	rd)		
			LOCATIO				
Parameter	Standard of AAQ	Apr'24	May'24	Jun'24	Jul'24	Aug'24	Sept'24
PM 2.5	60	38.3	34.45	20.18	24.9	23.29	34.25
PM 10	100	77.52	83.31	60.46	71.37	39.78	52.18
SO_X	80	27.29	35.79	8.49	6.3	7.22	11.06
NO_X	80	45.05	67.35	50.48	30.06	30.88	26.77
CO	2	0.56	0.97	0.88	0.63	0.87	1.04

Manisha Bhati

Manager- Environment Chanderia Lead Zinc Smelter

Annexure – X HINDUSTAN ZINC LIMITED

Chanderia Lead Zinc Smelter

Ambient Air Quality Monitoring Results (Inside Plant)

Quarterly Monitoring (Apr'24 - Jun'24)

Name of Monitoring Station		Parameters (Values are in μg/m³)									
	PM (2.5)	PM (10)	Lead (Pb)	CO	NO ₂	SO ₂					
Limit	60 μg/m ³	100 μg/m ³	$1.0 \mu g/m^3$	4 mg/m ³	80 μg/m ³	80 μg/m ³					
Near CISF Colony C1	56.9	84.6	0.19	1.14	30.8	12.7					
Near LOCO Shed C2	55.3	84.9	0.19	1.19	33.4	13.7					
Near Slag Gate	56.2	87.4	0.29	1.17	34.6	11.9					
Near DM Plant	54.8	91.7	0.21	1.19	34.7	11.5					

Ambient Air Quality Monitoring Results

Quarterly Monitoring (Jul'24 - Sept'24)

Name of Monitoring Station	Parameters (Values are in μg/m³)									
		PM (10)	Lead (Pb) 1.0μg/m ³	СО	NO ₂	SO ₂				
		$100 \mu g/m^3$		4 mg/m ³	80 μg/m ³	80 μg/m ³				
Near CISF Colony C1	57.4	88.3	0.18	1.23	32.5	11.3				
Near LOCO Shed C2	54.7	88.5	0.21	1.16	31.2					
Near Slag Gate	58.4	90.3	0.25		31.2	12.6				
- rour oraș oute	30.4	90.3	0.20	1.21	31.2	12.6				
Near DM Plant	55.8	86.3	0.23	1.22	32.1	13.4				

Manisha Bhati

Manager- Environment

HINDUSTAN ZINC LIMITED CHANDERIA LEAD ZINC SMELTER

Ambient Air Quality Monitoring Report (Outside Plant)

Quarterly Monitoring (Apr'24 - Jun'24)

Name of Monitoring Station	Parameters (Values are in μg/m³)									
	PM (2.5)	PM (10)	Lead (Pb)	СО	NO ₂	SO ₂				
Limit	60 μg/m ³	100 μg/m ³	1.0μg/m ³	4 mg/m ³	80 μg/m ³	80 μg/m ³				
Putholi	54.7	88.6	< 0.1	1.22	29.4	11.7				
Munga Ka Khera	53.8	86.7	< 0.1	1.23	25.3	13.4				
Nagari	56.2	94.8	< 0.1	1.19	34.1					
Billiya	52.6	85.3	< 0.1	1.13	26.4	13.5				
Ajoliya Ka Khera	56.4	82.9	< 0.1	1.18	27.3	12.7				
Anwalhera	55.7	89.4	< 0.1	1.16	27.3	11.9				
Zinc Nagar	56.7	91.9	< 0.1	1.21	29.4	13.5				

Quarterly Monitoring (Jul'24 - Sept'24)

Name of Monitoring Station	Parameters (Values are in μg/m³)									
Station	PM (2.5)	PM (10)	Lead (Pb)	CO	NO_2	SO ₂				
Limit	60 μg/m ³	100 μg/m ³	1.0μg/m ³	4 mg/m ³	80 μg/m ³	80 μg/m ³				
Putholi	57.8	90.5	< 0.1	1.18	33.6	12.5				
Munga Ka Khera	58.4	95.3	< 0.1	1.21	28.4	12.6				
Nagari	57.4	98.5	< 0.1	1.22	32.1	12.6				
Billiya	54.1	88.3	< 0.1	1.16	28.9	12.6				
Ajoliya Ka Khera	59.1	87.2	< 0.1	1.23	25.8	11.6				
Anwalhera	56.3	91.5	< 0.1	1.24	29.5	12.4				
Zinc Nagar	58.4	95.6	< 0.1	1.19	30.2	12.4				

Manisha Bhati

Manager- Environment

Annexure - XI HINDUSTAN ZINC LIMITED

Chanderia Lead Zinc Smelter

Ambient Noise Monitoring Results

(Apr'24 - Jun'24)

S.No.	Testing Protocol	Parameters/ Unit	Point of Collection	Observed Value (L eq)	Observed Value (L eq)
			Noise Standard(dB)	Day - 75	Night – 70
1	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near CISF Colony C1	70.9	55.2
2	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near Loco shade C2	70.1	56.8
3	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near Slag gate	69.9	52.4
4	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near DM Plant	69.8	56.2

(Jul'24 - Sept'24)

S.No.	Testing Protocol	Parameters	Point of Collection	Observed Value (L eq)	Observed Value (L eq)
			Noise Standard(dB)	Day - 75	Night - 70
1	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near CISF Colony C1	70.1	56.9
2	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near Loco shade C2	69.9	57.8
3	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near Slag gate	69.3	51.9
4	IS 9989-1981 (RA 2014)	Noise Level (dB)	Near DM Plant	68.5	55.9

Manisha Bhati

Manager- Environment

Annexure-XII

Hindustan Zinc Limited

Chanderiya Lead Zinc Smelter

Online emission monitoring report

s.no	(mg/Nm³)		Pyro Sinter- Venturi- PM (mg/Nm³)	enturi- PM Main- PM		Pyro ISF-PM (mg/Nm³)	
1	April-2024	7.5	NA	8.83	(mg/Nm³) 14.65	65.86	
2	May-2024	5.54	NA	9.25	11.83	42.72	
3	June-2024	2.61	NA	11.77	14.49	71.02	
4	July-2024	18.46	8.28	13.63	26.45	50.45	
5	August-2024	9.11	13.63	14.07	14.75	27.66	
6	September-2024	12.73	32.94	18.17	22.25	30.25	
7	Prescribed Standards	0-150	0-150	0-150	0-150	0-150	
8	Remarks		From Feb to June- 2024 Plant was under maintenance				

s.no	Month	Pyro ZRP Main-PM (mg/Nm3)	Pyro ZRP Fume- PM (mg/Nm3)	Pyro LRP Main-PM (mg/Nm3)	Pyro LRP Cu Dross-PM (mg/Nm3)	Pyro TGT- SO2(ppm)
1	April-2024	7.87	16.45	14.77	0	56.19
2	May-2024	11.04	10.45	10.05	14.27	52.67
3	June-2024	9.42	13.35	6.55	10.86	53.14
4	July-2024	8.09	7.62	9.77	14.97	50.55
5	August-2024	8.07	5.32	5.49	14.3	39.42
6	September-2024	9.39	6.38	4.41	10.37	74.85
7	Prescribed Standards	0 - 150	0 - 150	0 - 150	0 - 150	0 – 224
8	Remarks	-			Analyser was under maintenance till Apr'24	

**Pyro CRP Milling is not in operation.

Manisha Bhati

Environment Head

Hindustan Zinc Limited

Chanderiya Lead Zinc Smelter

Online emission monitoring report

S.NO	Month	H1-ZD- PM (mg/Nm³)	H1-ZA- PM (mg/Nm³)	H1-ZMF 1- PM (mg/Nm ³)	H1-ZMF 2- PM (mg/Nm³)	H1-AP-SO ₂ (ppm)
1	April-2024	11.81	9.06	15.87	17.47	63.86
2	May-2024	10.95	6.81	8.11	14.84	82.15
3	June-2024	8.36	8.25	5.4	9.7	83.07
4	July-2024	6.23	6.71	4.15	7.76	81.74
5	August-2024	4.57	6.7	5.57	7.66	77.32
6	September-2024	6.43	6.62	4.1	7.95	76.85
7	Prescribed Standards	0 - 30	0 - 30	0 - 30	0 - 30	0 - 135

S.NO	Month	H2-ZD-PM (mg/Nm³)	H2-ZA-PM (mg/Nm³)	H2-ZMF-1- PM (mg/Nm ³)	H2-ZMF-2- PM (mg/Nm ³)	H2-AP- SO ₂ (ppm)	CPP Coal Crusher-PM (mg/Nm³)
1	April-2024	1.64	13.12	11.75	10.69	78.27	0
2	May-2024	1.07	12.63	12.98	10.65	81.23	38.18
3	June-2024	1.06	11.41	9.47	8.87	79.36	7.05
4	July-2024	1.09	2.58	10.55	7.67	78.51	3.99
5	August-2024	1.21	3.58	6.13	6.49	89.72	4.83
6	September- 2024	1.0	3.99	7.11	5.51	81.1	3.39
7	Prescribed Standards	0 - 30	0 - 30	0 - 30	0 - 30	0 - 135	0 - 50
8	Remarks						Analyser was unde maintenance in Apr'24

Manisha Bhati

Environment Head

Online emission monitoring report

S.NO	Month	CPP_UNIT- 1&2-PM (mg/Nm³)	CPP_UNIT1&2- SO ₂ (mg/Nm ³)	CPP_UNIT- 1&2-NOx (mg/Nm³)	CPP_UNIT- 3-PM	CPP_UNIT- 3-SO ₂	CPP_UNIT-
1	April-2024	28.56	2240		(mg/Nm³)	(mg/Nm³)	(mg/Nm ³)
2	May-2024	39.08		376.71	16.69	1267	279.71
3	June-2024		1159	345.52	34.48	609.62	206.99
		36.77	1008	360.78	30.05	338.35	126.56
4	July-2024	19.45	1276	456.9	41.39	588.73	\$1000 Market 1990
5	August- 2024	24.93	1167	536.55	33.31	788.23	182.49 329.53
6	September- 2024	50.46	1345	504.47	41.47	886.69	290.58
7	Prescribed Standards	0 - 50	0-600	0 - 450	0 - 50	0 - 600	0 - 450

S.NO	Month	CPP UNIT_1_2-Mercury (ug/m³)	CPP UNIT_3-Mercury (ug/m³)
1	April-2024	8.34	11.07
2	May-2024	8.06	12.2
3	June-2024	4.89	12.06
4	July-2024	2.85	11.75
5	August-2024	1.13	10,95
6	September-2024	5.45	1.23
7	Prescribed Standards	0 - 30	0 - 30

Manisha Bhati

Environment Head

Annexure-XIII

Hindustan Zinc Limited

Chanderiya Lead Zinc Smelter

Online effluent monitoring report

S. No	Month	ETP1-Flow (m³/hr)	ETP1-TSS (ppm)	ETP1-pH (pH)	ETP2-Flow (m ³ /hr)	ETP2-TSS (ppm)	ETP2-pH (pH)	FDD-Flow Meter (m)
1	April-2024	0	5.85	4.62	0			30. 20
2	May-2024	0	5.08	1/4100000		21.85	6.99	0
3				6.79	0	34.87	6.77	0
3	June-2024	0	5.72	7.09	0	14.37	6.55	0
4	July-2024	0	2.39	7.48	0	15.58	000000	
5	August- 2024	0	0.57	7.26	0	9.83	6.87	0
6	September- 2024	0	0.57	7.7	0	11.42	6.69	0
7	Prescribed Standards	0 - 100	0 - 100	6.5 - 9	0 - 100	0 - 100	6.5 - 9	0 - 100


Manisha Bhati

Environment Head







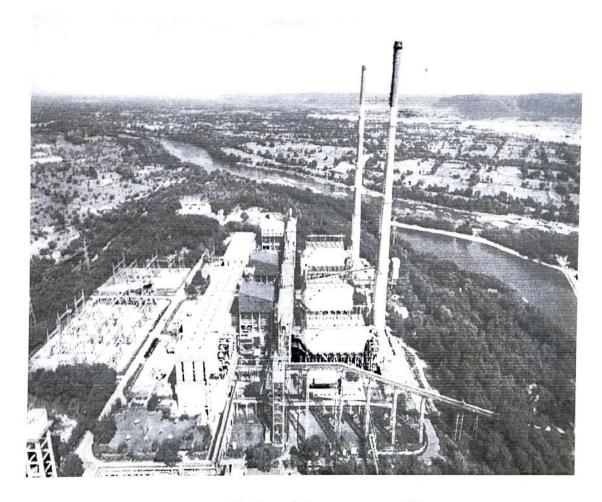

Energy Carbon Management Plan Chanderiya Smelting Complex

Document published on: 5th Aug 2024.





Contents

- 1. Introduction of CSC Plant
- 2. Greenhouse Gas management
- 2.1 Context and drivers
- 2.2 Vision
- 2.3 Objectives and strategy
- 3. Emissions baseline and projections
- 3.1 Scope
- 3.2 Baseline
- 3.3 Emissions since 2015
- 3.4 Targets
- 4. Implementation Plan
- 4.1 Emission reduction opportunities
- 4.2 Energy and fuel saving projects past and ongoing.
- 5. GHG Reduction measures:
- 6. Knowledge, Awareness and Communication
- 7. Legal and other requirement
- 8. Risk Management
- 8.1 Risk assessment
- 8.2 Initiatives and opportunities





Foreword to 2024 CSC Energy Carbon Management Plan

Chanderiya Smelting Complex is the largest Zinc producing plant in India where zinc can be produced using pyro metallurgical or hydrometallurgical processes, depending on the type of concentrate used as charge. Coke and power are the main inputs which are responsible for GHG emissions. A lot of amounts of heat and flue gases are generated in different processes of zinc manufacturing. There is high scope in utilizing the heat and flue gases to reduce the energy consumption in turn GHG gas emissions. Lot of work has been done and many projects have been completed in last few years for Energy saving, utilization of heat of gases. Still there is lot of scope in utilizing heat and reduction in energy consumption. In 2022-23 the total emissions were 2145900 tCO2e and specific emissions 3.44 tCO2e per ton of metal. In 2023-24 the total emissions were decreased to 2331303 tCO2e and specific emissions decrease 3.72 tCO2e per ton of metal. In the financial year FY'24 total emission and specific emission increased due to higher reliance on CPPs during FY 2023-24

CSC has taken a target of reduction in scope 1 and 2 emissions against its 2016-17 baseline by 14% by 2026-27 in terms of absolute emissions. This is a reduction of tCO2e against the baseline 20,78,464 tCO2e. CSC will be able to achieve this target well before the target completion date.

We will also seek to further reduction in our scope 3 emissions.





1. INTRODUCTION OF CSC PLANT

HZL manufactures zinc as its main product at its Chanderiya smelting unit in Rajasthan. Zinc smelting is the process of converting zinc concentrates into pure zinc. Zinc can be produced using pyro metallurgical or hydrometallurgical processes, depending on the type of concentrate used as a charge. HZL had only a pyro process-based manufacturing unit (commissioned in 1991) till 2005 - when a unit based on the

The facility went through another capacity addition with the commissioning of another unit in 2007, a zinc smelter (based on hydro process). The total installed capacity at Chanderiya smelting unit is 6,09,000 tons per annum (TPA) of refined zinc. The refined Lead capacity is 95,000 tons per annum.

The total 290 MW capacity coal base thermal power plant, 22.3 MW WHRB and 0.91MW solar plants installed to fulfill the requirement of the in-house demand.

2. Greenhouse Gas Management

2.1 Context and drivers

We are focussed on accelerating actions to lower carbon emissions generated during our operations. Our environment conservation efforts are driven by a strategic thrust on minimising and mitigating our impact on water, land, air quality, climate, and biodiversity. We are also committed to building harmonious relations with our stakeholders, to reduce the environmental footprint of our operations by deploying resource management systems and controls.

GHG management plan identifies the organization's current carbon emissions and a logical series of technical and managerial steps that must be taken to arrive at the required reduction target.

Avoiding use of fossil fuels and reducing dependency on them shall play a vital role in our net zero journey, substituting the conventional energy use by renewable energy and offsetting the greenhouse gas being emitted by sequestering techniques such as afforestation.

Avoid

Reduce

Substitute

Offset





- A wide range of INDIA programs, regulation and guidance now exist that encourage all sectors of society to reduce carbon emissions like REC, RPO, PAT incentives for the renewable energy plants and efficiency improvement.
- We believe in creating long term value for our stakeholders and with stakeholders and communities we work with becoming climate conscious, responsible business becomes our priority.
- In line with becoming a sustainable business organization we have to reduce our energy consumption and move away from conventional energy sources to renewable energy sources. It has to be noted that carbon management shall yield financial savings too and can be achieved by using techniques such as utilizing waste heat.
- This would also help reduce CLZS's financial liability to purchase REC under the RPO regulation of state government of Rajasthan.
- We believe that measures aimed at reduction of GHG emissions have the potential for Climate Change reduction and CSC acts as a leader for other units of HZL in delivering carbon emission reductions.
- We understand the reputational risk associated with climate change and GHG emissions and hence we are determined to reduce our emissions and strive towards a net zero journey by 2050 as envisaged by HZL.
- A target is set for the HZL to reduce Scope 1 and 2 total emissions 14 % by 2026-27 against a 2016-17 baseline, all units of HZL are required to produce an Energy Carbon Management Plan showing how it will contribute to achieving this Target.
- Long term rises in utility costs would increase CLZS's operating costs. Thus, it is important to analyze opportunities for increased efficiency in the use of energy.
- CSC should discharge it corporate responsibility, in part by contributing to HZL targets to reduce Green House Gas emissions.









HINDUSTAN ZINC

Energy & Climate Change Policy

Industrial 7 or 1 immedia committee to minimizing the impact of climate change on its own but should be as well as on the environment and occurry. We a mitorgi abornte mitt stacenniders to draen mela meanmiful schien en ci mete colarge

This Energy & Compte Change policy shall be a us to define, strategize, plan and malament espent a road—as, towards removing climate goals The policy is forward leading and ecos an energy and a smalley disafter businesses across methodoldus 7 or smalley

This polity is applicable to all Minduster Paris in the Successional Consistency substitutions, and ventures and acquisitions interested the substitution of parishers are proportionally and the substitution of the substitution contractor emologies, que nesa partners, suppliers, and others with whom I production fine scen business.

madicition this policy is specificable throughout the sparational idequite of the asserts and mines covering stages from exponential and planning ta evaluar and approximation and classics. I wither more presented to approximate and expension of the control

Objectives of the Energy & Climate Change Policy

Hinducton Zint will stress in:

- About and maintain garba, best practices on climate and energy management and minimaling promining gar idless, emissions throughout our speratures including
 - comply with local envirant unal regulations
 - augment with the overall adjections of the fland Agreement
 - measuring energy unage and preachouse gas emissions like on "All excoss an operating, and peoplesment and maintain year. anyear efforts to reduce energy tonsumption and Disti similations including infractioning three wasts energy wherever goasials
 - mossuring and disclesing greatheuse great emissions deaped to series the solve value coal including agreement and downstream emissions
 - setting energy and G45 reduction espainish in a geometrian and advisor fire's commitment to become a net term contain THEFTONE DY TOND
- Conducting kasso is mantate under stand the impact of climates; harge unithe liviaries aurder afforcing consider and time according
- belegrate contain change considerations into our strategic eponous; timerated planning and enalyzing the commit related notes and epperimenties both physical and transition.
- Adapt and future proof our facilities to the physical risks of the was change and to achieve an orderly framer on to a world in which better parterior ste entire mis
- include the adoption of carbon ackning or a milar machinisms into our investment section. The rig
- Promote engage, and invest in energy contumptor reduction organization clusters energy (uniters at online given curate business and tiese amengy and masserize banding from anargy by whose recovery
- Foster resease have remission techniques within all operations leading to optimize this attain of rescouncy which community improve the efficiently of operations of missional geography consumption and resources see
- Report BHG emissions climate trajectory scorum analysis and climate change tips analysis on yearly trave in alignment with internationally recognized prediction is be Totalord in Climate Physical Discharge - TCFD and CDPs and mark climary with other stakeholders to reduce energy consilings on and cores intensity
- Communicate our approach and conservents activaly to statesfulders, and work closely with national and global policy makers to incompressive and equitable unatement policies within the content of our operation
- Support joint efforts by the private and public sectors to reduce the impacts of comple change.
- Ostaborate with our employees, ender communities, business partners, runtomers, and other students decision schools our communities. energy and greenfraces passemission reduction
- Engage with relevant stateholders to suiting causely and capability or density and proactively manage climate related that and
- Encourage and officence our pusiness purpoers including supplyings on a adopt energy conferential practices, set arealy, and climate targett and report on the ir practices
- Review the performance against the poorly on a periodic against ensure in unagement of mergy & climbral not upper our object was including the staring of great practices throughout the organization and includes access

Responsibility & Review

This policy is part of the Vederra Sustantability Framework and each of substanting a finite discress success success companion on some plants and prowill be discussible for concrosing and setting the palicy and the flavourize Committee are deep processed on the flavourized continues and the continues and the flavourized continues and the c asspeciated standards. The tineral follogoner line out review this policy annually endirecommend appropriate five a provide floars as may exem-

Resided additional process. Employments Policy biopres sets Policy Water Folicy.

Marine Haland

Arun Misra

LEO & Who e - me Director HZL

Date: 06' August, 2024





2.2 VISION:

The vision will be achieved through implementation of the measures outlined in the Carbon Management Plan. We envisage a low-carbon environment in which:

- Adopt and maintain global approaches on carbon and energy management to reduce our specific greenhouse gas emissions throughout our operations, including:
 - Measuring our direct energy usage and carbon emissions and maintaining our year-on-year efforts to reduce energy consumption across our operations.
 - Defining specific energy and carbon reduction targets, seeking to achieve substantial decarbonization of our business by 2050.
 - Maximising the benefits of process improvements and technology advancements.
 - integrating climate change considerations into our strategic approach, including the adaptation of carbon pricing or similar mechanisms into our investment decision-making.
- Extend our approach to reporting carbon emissions in compliance with internationally recognised protocols.
- Invest in clean energy and energy recovery projects.
- Engage with stakeholder and provide for adaption to future-proof our business.
- Communicate our approach and achievements actively to stakeholders and work closely with policymakers to encourage effective and equitable abatement policies within our sectors of operation.
- Consider carbon emissions for our project and R&D investments in line with Vedanta's sustainable development commitments.

2.3 Objectives and strategy

This Energy and Carbon Management Plan is prepared for achieving the targeted emission reduction at CSC. The ECMP is also made in line with Energy and Climate Change Management policy of HZL. energy and carbon assessment being carried out once a year.

The strategic objectives of the ECMP are to:

- Evaluate opportunities to improve energy efficiencies or implement lower emissions sources.
- Achieve science based GHG emission targets through impactful actions.
- Reduce carbon footprint by enhancing renewable energy portfolio.
- > Set challenging but achievable carbon reduction targets over the medium and long term.
- Develop systems to ensure that accurate data and reporting tools are available.
- Measure the Company's performance against milestones and report to all stakeholders.





- Sonority of approach with the HZL's policy framework, particularly the Energy and Climate change management policy.
- Plays important role in achieving HZL's targets.
- Achieve reduction in cost of product.

Net Zero Strategy

- Our net zero strategy is in line with Reducing fossil fuel-based energy use in our operations by using innovative energy efficiency technologies and process optimization.
- > Shifting to renewables and/ or low-carbon solutions where possible.
- Replace diesel fueled transportation vehicles with Electric vehicles, Turbine revamping of all the CPPs, install Hydrogen or Electric/ Induction Furnaces, enhance our carbon Capture, Storage and Utilization capacity etc.
- Climate Change risk assessment based on TCFD guidelines.

CSC Scope 1, 2 and 3 emissions contributing factors (source) are as follows:

Scope 1 – Direct emissions	
Fuels burnt (Coal, Biomass, LDO, HSD) at C	CPP for generation of electricity
Fuels burnt (Coke) at PYRO – for Process	o and an or electricity
Propane/PNG at Pyro, Hydro-1 and Hydro-	-2
LDO/HSD/LSHS at Pyro, Hydro-1 and Hydro	
Diesel at DG sets (production of electricity), Pyro, H1, H2 and CPP
Scope 2 – Emissions associated	with the use of electricity
Electricity purchased from AVVNL, IEX	
Scope 3 – Indirect emissions	
Transport of material – cathodes, finished,	goods, coal, concentrate
Bus travel of employees	
End-of-Life Treatment of Sold products	
Fuel & Energy related	
Purchased Goods & Services	





Scope 1 & 2 Emissions Baseline and Projections

3.1 Scope

CSC's initial Carbon Management Strategy and Implementation Plan focused on energy, Fossil fuel and coal used, Utilization of waste heat and flue gases, reduction in energy of Cell house, Sinter and Refinery. However, this new plan extends the scope to include all areas of CSC complex.

3.2 Baseline

We have calculated that our Scope 1 and 2 emissions in 2016-17 as

Scope	2016	-17
Scope 1 (tCO2e)	2056034	98.92%
Scope 2 (tCO2e)	22430	1.08%
Total emission (tCO2e)	2078464	2.0070
Production (MT)	403980	

CSC's carbon emissions in FY 2016-17 had reported 2056034 tones CO₂e in scope1 and 22430 tons CO₂e in Scope 2. This had been taken as base line.


3.3 Emissions from FY 2016-17

The table below indicates the Scope 1 and 2 emissions being produced across the entire CSC. The emissions have been calculated on a power and fuel consumption basis.

2016-17	2017-18	2018-19	2019-20	2020 21	2024 22		
2056024	2272170				2021-22	2022-23	2023-24
		221/235	2206921	2217395	2040810	1757142	2285384
22430	32885	32292	42054	65145	186152		The second second
2078464	2405055	2249527	2249075				45919
402000					2226962	2145900	2331303
403360	584758	543/13	552049	581814	590635	623910	627473
5.14	4.11	4.14	4.07	3.92	3.77	3.44	3.72
	2056034 22430 2078464 403980	2056034 2372170 22430 32885 2078464 2405055 403980 584758	2056034 2372170 2217235 22430 32885 32292 2078464 2405055 2249527 403980 584758 543713	2056034 2372170 2217235 2206921 22430 32885 32292 42054 2078464 2405055 2249527 2248975 403980 584758 543713 552049	2056034 2372170 2217235 2206921 2217395 22430 32885 32292 42054 65145 2078464 2405055 2249527 2248975 2282540 403980 584758 543713 552049 581814	2056034 2372170 2217235 2206921 2217395 2040810 22430 32885 32292 42054 65145 186152 2078464 2405055 2249527 2248975 2282540 2226962 403980 584758 543713 552049 581814 590635	2056034 2372170 2217235 2206921 2217395 2040810 1757142 22430 32885 32292 42054 65145 186152 388758 2078464 2405055 2249527 2248975 2282540 2226962 2145900 403980 584758 543713 552049 581814 590635 623910 5.14 4.11 4.14 4.07 3.03 2.27







GHG emission Plant wise: -

Plant	2016-17	2017 10	T					
CPP (tCO2e)		2017-18	2018-19	2019-20	2020-21	2021-22	2022-23	2023-24
	153387	166575	161040	160463	162555			2023-24
Hydro 1 (tCO2e)	740568	857623				144285	121844	154048
Hydro 2 (tCO2e)			834159	843749	928337	880423	855555	893164
	764556	909301	877494	870731	921012	892316		
Pyro (tCO2e)	113626	457844	343487	333464		A	853908	930031
Total (tCO2e)	2078464	2405055			283820	343633	395138	391952
	1 20/0404	2403055	2249527	2248975	2282540	2226962	2145900	2331303

GHG Emission as per Fuel Consumption: -

Fuel	2016-17	2017-18	2018-19	2010 20	2022			
Coal (tCO2e)	1752027	2054214		2019-20	2020-21	2021-22	2022-23	2023-24
HSD (tCO2e)	10466		1995777	1993426	2047435	1810693	1477346	2004368
Propane/LPG (tCO2e)		20299	47296	40934	23326	39886	45507	
	16157	16691	9922	5213	422	0		49099
Coke (tCO2e)	250641	258136	164239	165886			20497	23443
FO (tCO2e)	26744	22831	0		136710	171718	206610	208474
PNG(tCO2e)		22031	- 0	0	0	0	0	0
Purchased Electricity (tCO2e)	22.42.0			1462	9502	18513	7182	
		32885	32292	42054	65145	186152		0
Total (tCO2e)	2078464	54 2405055 22499	2249527	2248975			388758	45919
			JJE1	22-03/3	2282540	2226962	2145900	2331303

3.4 Targets

A target is set for HZL to reduce scope 1 and 2 absolute emissions by 14 % by 2026-27 against 2016-17 baseline. In line with the same the target of CSC is set to reduce the Scope 1 and 2 absolute emissions by 14 % by 2026-27 against 2016-17 baseline


Scope	2016-17 2056034	2017-18	2018-10	2010 20	2020 24						
Scope 1 (tCO2e)	2055024		2010-15	2013-20	2020-21	2021-22	2022-23	2023-24	2024-25	2025 20	2022
stope I (tcoze)	2056034	2027249	1998465	1969680	1940896	1912111	1003333		2024-23	2025-20	2026-27
Scope 2 (tCO2e)	2056034 22430	22116	21802	21400	21174		1003327	1854542	1825758	1796973	1768189
Total emission (tron-)	20000	22110	21002	21483	21174	20860	20546	20232	19910	1000	2,00103
Total ellission (tCO2e)	2078464	2049365	2020267	1991168	1962070	1922071 1000	1002070		13310	19004	19290
Total emission (tCO2e)						1332371	19038/3	1874774	1845676	1816577	1787479





Now we have taken revise emission targets for the coming year but aggregate emission target by FY 2026-27 is less as per previous.

Scope	2016.17	2017 40									
Total emission (+CO2+)	2016-17 2078464	2017-18	2018-19	2019-20	2020-21	2021-22	2022-23	2023-24	2024-25	2025.26	2026 27
Total emission (tCO2e)	2078464	2405055	2249527	2248975	2282540	2226962	2145900	2331303	2202721	1555104	107604
						2420302	2143300	2331303	2302/31	1565104	1276914



Achievement till 2023-24: -

In FY 23-24 the total emissions have increased by 7.95% and we have increased specific emission from 3.44 tCO2e/MT to 3.72 tCO2e/MT. Now we need to put more focus on reduction of emission to achieve the set target. We will also seek to further assess and reduce our scope 3 emissions.

In calculating progress towards this target on an annual basis, benchmarking will need to consider the following statistics for each year: Emissions from the following sections: CPP

Hydro 1

Hydro 2

PYRO

Logistic

Administration

Changes in these statistics will need to be considered in the calculation of percentage change in CO2 emissions. It is considered that growth in these areas is likely to result in an increase in energy consumption and carbon emissions.

Scope 3 Emissions

The calculation of the Scope 3 emission is not possible unit wise due to constraint of the double counting. As materials are inbound for some units could be outbound for some other units. The calculation of the Scope 3 Emission is being done at the company level.





4. Implementation Plan

4.1 Emission Reduction Opportunities

The purpose of this section of the plan is to list and priorities all the opportunities identified for carbon emissions savings and sustainable practices which have been collected from suggestions made at brainstorming sessions/research & innovation was tailored to producing project opportunities that would either directly or indirectly reduce the carbon emissions from CSC.

4.2 Energy and fuel saving projects past and ongoing

CSC has been very active in the field of utility conservation for a long time. Many energy conservation and fuel saving projects have been done and are in progress too.

Following carbon and energy emission reduction project, we have implemented on site in FY 2023-24

s.no.	Project Details	Actual Energy saving (GJ)	Actual GHG reduction (Tonnes)
1	U3 MV ABB VFDs Availability Improvement	6280	1675
2	Reduce M&C Power Norms from 142 to 135 Units/MT	3675	980
3	Reduction in Specific LDO consumption from 93Ltr/MT to 86Ltr/MT	10043	744
4	CH Auxiliary specific to be reduce by 5%	2715	724
5	MC norms to be reduce by 5 Units/MT of Ingots	2118	565
6	Fills Pack Replacement	1110	296
7	Reduction in sinter plant fresh air fan Power consumption	818	
8	ACWP VFD Installation in Unit-3	612	218
9	Reduce Power Consumption in Cooling Towers (Hydro 2)	522	163
10	Feed water pump power consumption reduction (17.25KWh/Hr)	267	139
11	CT Fan-4 VFD Installation		71
12	HMT Conventional Lights to be replaced with LED Lights	262	70
13	Centac Power Consumption reduction by 2% (Hydro 1)	209	56
14	Furnace CT pump power reduction (11.5KWh/Hr)	171	45
15	Occupancy Sensor Installation in MCCs	146	39
16	Occupancy based Automation of Airconditioning Units in Offices	76	20
17	All seal pot pumps to be run with LT interlock	66	18
18	Reduction in propane consumption	45	12
19	Installation of Solar (pole mounted) lights at boundary wall area	6	2
	the state of solar (pole mounted) lights at boundary wall area	5	1
	Total	29145	5838





5. GHG Reduction measures

Few of the things which could be done to reduce GHG emissions at CSC are categorized under the following heads i.e., Behavioral Measure, Efficiency Measures, Fuel Replacement Measures and Long-Term Measures

Governance

We have established Energy and carbon management community, who looks after governance for energy conservation, energy and carbon risk assessment, mitigation strategies and continual improvement in energy and carbon management. The committee plays a strategic role in all business decisions to ensure workplace safety, eliminating any potential damage to the environment, enhancing a commitment towards stakeholders, and maintaining our reputation etc.

Behavioral Measures

Behavioral changes are certain to be an important component in reducing greenhouse gas emissions (GHG) and combating climate change. There are few measures which could be circulated to employee through various engagement modes.

- > Switch off appliances lights, fans, Air conditioners etc. when not in use.
- > If leaving the computer for a while, put it on standby. You'll be able to restart it quickly, and it'll take less energy than shutting it down and then restarting it.
- Awareness and training programs: Employee awareness trainings and workshops conducted to let everyone know that they're making changes to reduce your impact on the environment.
- > Switch to public transportation, carpooling, biking, telecommuting and other innovative ways to save energy and reduce greenhouse gas emissions on your way to and from work.
- Annual maintenance of refrigerators, ACs, removal of blockages from air vents, replacing older light bulbs with energy-saving fluorescent bulbs.

Efficiency Measures

- Undertake energy audit (Internal Energy audit/brainstorming session once in year & External energy audit once in three year) on a regular basis to highlight major energy consuming sections and equipment's including. A well-conducted energy audit would reveal the areas of wastage of energy, and it would lead to suggestions for possible energy savings in all sectors.
 All operating units are certified ISO 50001 Energy Management System
- ➤ Maintenance of air conditioners and similar equipment's should be done on a regular basis across corporate offices, units and guest houses. Outdated equipment's should be replaced with energy efficient ones (Star rating).
- > Turbine revamp was carried out at CPP to increase the process efficiency.





Innovation

Innovative technologies such as SAP are being implemented to automate and reduce manual errors in a process. This would improve collection of data and increase accuracy. This would help establish a regular and up-to-date monitoring programme for air emissions (point and fugitive) arising from the operations. Across the business, we continue to pursue improvements to air quality management, focusing on emissions of particulate matter, SO2, NOx etc emitted by our operational activities.

Lighting Management

- Replace dated air conditioners and fans.
- Replacing existing lights with CFL and LED.
- Installation of auto transformers and operating all lighting feeders at 210 V.
- Use of voltage controllers on lighting feeders.
- Maximizing the use of natural daylight, wherever possible.
- Use of sensor-based lighting controls at selected locations i.e., washrooms and passageways.

Motor Management

- Avoid using motors at part loads (and avoid over-sized motors)
- Use of soft starters
- Replacement of old motors with high efficiency ones
- Sizing the motor to variable load
- Improving the input power quality
- Power factor correction by installing capacitors.
- Speed control of induction motor
 - 1. Multi-speed motors
 - 11. Variable speed drives
 - III. New Direct current drives
 - Wound rotor AC motor drives (slip ring induction motors) IV.

Employee Commute & Business Travel

- Strategies for reduction
 - i. Increase % of employees using Mass Transit
 - ii. Encourage Carpooling/Bus Pooling
 - iii. Use of cleaner fuels for Buses and compliance to Euro 2 standards
 - iv. Onsite emission and tyre pressure tests.
 - v. Encourage the use of net meetings, Video Conferencing and Telepresence

Green Computing

- Conversion of building as green building for the optimum utilization of natural resources
- Optimum utilization of the IT infrastructure through Server Consolidation and virtualization






- vi. Desktop level virtualization
- All CRT monitors to be replaced with LCD.
- Green Procurement: All equipment to be energy star certified.
- Green Data Centers
 - vii. Evaluating the performance of all our current data centers.
 - viii. New data centers as per the latest technology and HVAC systems.


Fuel Switch/Replacement Measures

Switching to Cleaner Fuels

As evident from the analysis of data analysis, we can reduce emissions by substituting PNG from propane gas in Pyro, Hydro1 and Hydro 2 plant. However, an assessment of materiality of emissions at the plant is required before evaluating reduction measures. The second way of reducing the emissions in this category is using solar heaters for preheating the water. This technology is well established and is being used in other companies across India. Electric forklifts, two trucks and golf carts have introduced by business partners to reduce emissions. Till 15 vehicles deployed in CLZS.



Biomass substitution in Coal Fuel

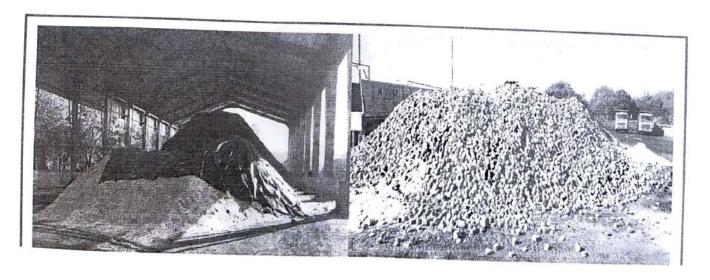



STATE REMOTE SENSING APPLICATION CENTRE DEPARTMENT OF SCIENCE & TECHNOLOGY GOVERNMENT OF RAJASTHAN

F()DST/SRSAC/CHANDERIYA-GREEN-COVER/2021 / 75%

Date: 2.5 Mar 2021

To.

Mrs. Manisha Bhati

Deputy Manager - Environment,

HZL, CLZS Complex,

P.O.: Putholi-312021, Dist.: Chittorgarh (Raj.)

Vedanta Resources Pvt. Ltd.

e-mail: manisha.bhati@vedanta.co.in

Mobile: +91-9116134090

SUB.: Final Report for Green Cover Study of Chanderiya Lead Zinc Smelter Complex at

Chittorgarh Rajasthan.

REF.: Purchase Order 4500006323 dated 19 Jan 2021

Ma'am,

With the above reference, please find enclosed the final report of green cover assessment for the study area with the results derived using IRS-Cartosat-2E and ESA-Sentinel-2 satellite imageries.

With regards,

Project Director cum Deputy Secretary SRSAC, DST, Jodhpur

F()DST/SRSAC/CHANDERIYA-GREEN-COVER/2021 / 7.54-55

Date: 25 Mar 2021

Copy to:

PS to Secretary, DST, GOR, Japur

Project Director cum Deputy Secretary SRSAC, DST, Jodhpur


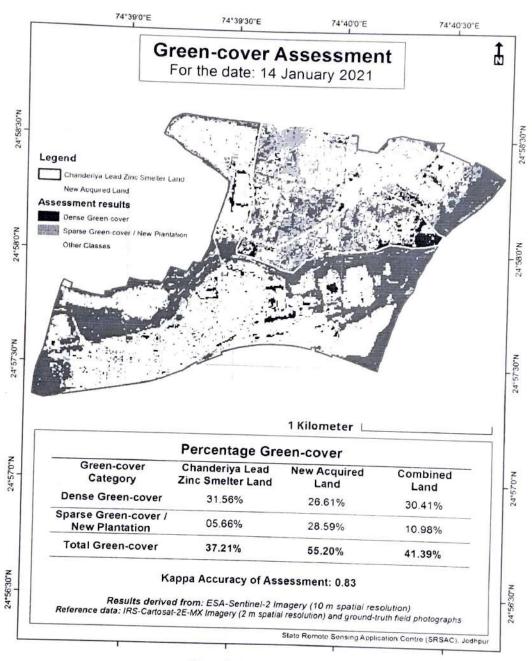


Figure 6: Assessment results







HINDUSTAN ZINC

Environmental Policy

Purpose

 $Hindustan\,Zinc\,Limited\,is\,committed\,to\,achieving\,excellence\,in\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,managemental\,management.\,Our\,goal\,is\,to\,minimise\,environmental\,managemental\,ma$ impacts of our business across the entire lifecycle by implementing pollution-prevention and natural resource conservation

This policy is forward looking and sets a vision for businesses across the Hindustan Zinc Limited.

Scope

This policy is applicable to all Hindustan Zinc Limited business units, including subsidiaries, joint ventures, and acquisitions, managed sites, licensees, outsourcing partners, corporate offices, and research facilities. This policy is also applicable to all Hindustan Zinc Limited employees, contractor employees, business partners, suppliers, and others with whom Hindustan Zinc

In addition, this policy is applicable throughout the operational lifecycle of the projects and mines, covering stages from exploration and planning to evaluation, operation, and closure. Furthermore, it extends to activities in our upstream and downstream value chain, limited to distribution, logistics, and sale of products and services to the customer.

Objectives of the Environmental Policy

Hindustan Zinc will strive to:

- Comply with applicable national, regional, and local environmental regulations and statutory obligations. In the absence (or lack) of appropriate legislation, industry best practices and applicable international standards will be used. ٠
- $Develop, implement, and improve environmental \, management \, systems, consistent \, with \, world-class \, standards.$
- Set targets and objectives to avoid, reduce or mitigate Environmental impacts on people and planet.
- Consistently assess our environmental risks, manage our impacts, take appropriate mitigation and adaptation measures, and communicate our environmental strategy to our stakeholders.
- Incorporate appropriate environmental criteria for all business decisions including the planning, operationalization, and
- Conduct regular environmental review and due diligence of the projects (including for mergers & acquisitions) to identify, prioritize, assess, and take effective actions for mitigating the potential environmental risks.
- Drive continuous environmental performance improvement by implementing appropriate available practices and
- Conserve natural resources by adopting environment-friendly and energy-efficient technologies through process
- Apply mitigation hierarchy (avoid, reduce, reuse, recycle, disposal) to environmental impacts and adopt the principles of
- Manage impacts related to energy, carbon emissions, waste, nature, air emissions, land-use & biodiversity, and water. ě.
- Raise awareness of internal and internal stakeholders including business partners, suppliers, and other stakeholders on adoption of practices in alignment with our policies, thereby fostering a collective commitment to managing environmental
- Provide appropriate training to all employees and emphasise the importance of minimising risks to environment, while also understanding the impacts of their work activities on the environment. .
- $Communicate\ with\ all\ our\ stake holders\ on\ the\ progress\ and\ performance\ of\ Environment\ management.$
- Review the performance against the policy on a periodic basis to ensure management of environmental impacts as per our objectives including the sharing of good practices throughout the organization and stakeholders.

Responsibility & Review

This policy is part of the Vedanta Sustainability Framework, and each Hindustan Zinc Limited business unit shall implement this policy. Our CEO will be accountable for controlling and setting the policy, and the Executive Committee are responsible for the full implementation of the policy and associated standards. The Board ESG committee will review this policy annually and recommend appropriate revisions to the Board as may deem necessary.


Related additional policies: Energy & Climate Change Policy, Biodiversity Policy, Water Policy, Tailing Management Policy.

Arun Mibra

Arun Misra

CEO & Whole Time Director, HZL

Date: 1" September, 2023



2024 के पहले कर लोगों को

डूंगरपुर। विछीवाडा करबे में सर्व समाज और विभिन्न संगठनों की बैठक आशापुरा धाम पर आयोजित हुई। बैठक में 22 जनवरी को अयोध्या में कर इसे भव्य रूप में मनाया जाएगा इस बारे में जानकारी देते हुए सर्व समाज ने बताया कि इस अवसर पर सर्व प्रथम आशापुरा धाम से एक विशाल शोभायात्रा निकाली जाएगी। जो करबे के विभिन्न भागों से गुजरती हुई बिछीवाड़ा में रिथत राम मंदिर जाएगी जहां मंदिर एक विशाल पताका चढ़ाई जाएगी और फिर विभिन्न विधि विधान के बाद अयोध्या में मूर्ति प्रतिष्ठान के बाद 521 दीपक की एक सामूहिक आस्ती एवं हनुमान चालीसा का पाठ पढ़ा जाएगा। इसके पश्चात महाप्रसाद का वितरण किया जाएगा। ग्रामीणों ने बताया कि प्रत्येक घर पे भगवान राम कि पटाका चढ़ाई जाएगी एवं आंगन में रंगीली सजाई जायेगी वही हर घर पे 21 दीपक प्रज्वलित किए जायेंगे वहीं कस्बे में स्थित प्रत्येक मंदिर पे 501दीप प्रज्विति किए जायेंगे। करणीराज सिंह, महंत महेंद्र सिंह, राजेंद्र सिंह, गणेश कलाल, ताराचंद पांचाल, वाब्लाल लवाना,वीएचपी

प्रतिनिधि मौजूद थे एवं कार्यक्रम को सफल बनाने के लिए सभी ने अपनी राय दी कार्यक्रम में महिलाओं कि भागीदारी पर भी चर्चा की।

पा -धरणेन्द्र जैन

होने वाले विशाल कार्यक्रम में बिछीवाड़ा में भी कई कार्यक्रम आयोजित के डॉक्टर कश्यपनाथ, दिनेश शाह, बसंत टेलर एवं विभिन्न समाज के

> O Piramal pital & Housing Finance

a and same, great same of पूरन श्रीमाली, श्याम सोनी, गोविन्द प्रजापत, राहुल पंडित जी, गोविन्द पुरोहित, धनराज मीणा, अधिनाश, रवि सानी, मुनिसज, नारायण, शिवराज, देवराज कमलेश पालीवाल महित अन्य मौजूद रहे।

सर्व साधारण को सूचित किया जाता है कि भारत सरवार के पर्णवरण वन और जलवायु परिवर्तन मंत्रालय के पत्र क्षमांक IA-J-11011/279/2006-IA-II(IND-I) हिनाक 29.12 2023 के द्वारा मेरार्र हिंदुरतान जिंक लिगिटेंड ग्राम पुठीली, जाजिलिया का खेळा और बिलिया तहसील - गंपरार और बित्तीडगढ़ , जिला - विशीडगढ़ में मौजूदा चंदेरिया लेड जिक स्मेल्टर के भीतर विस्तार (हाइड्डो प्लाट में इंडक्शन फर्नेंस, 1 स्लेब कास्टिंग ताइन और हापड़ों ना में आरजेड़नों पूनिट के एकीकरण , कुल धातु के आधार पर पापने मूनिट में उत्पादन मिश्रण में बदलाव और 1 लेड़ रिफाइनरी की रथापना, आधुनिकरण और स्थापना क माध्यम से सी.पी.पी. का दिस्तार , 1 बैस प्रेगर टरबाइन जनरेटर , माइनर मेटला की रिकवरी और 5 डी जी सेट की स्थापना) हेतु पर्यावरण स्वीकृति (क्लीयरेंस) प्रदान की गई है। उक्त स्वीकृति को पर्यावरण, वन और जलवायु परिवर्तन मंत्रालय नी वेबसाइट www.moef.gov.in पर देखा जा सकता है एतं इसकी प्रतितिषि राजस्थान राज्य प्रदुषण नियंत्रण मंडल/कमेटी के पास भी उपलब्ध है।

सी चंद्र CEO Smelters, HZL

पिरामल केतिहरू एंड हाइसिंग कायन्त्रन्त स्थितंड स्वतान्त्र प्रमादन पर प्रभावन पायक्षणा प्राप्त है। प्राप्ति का विचार हाजरिता प्राप्तान्त्र वर्तेवीरल सिवित्र है। प्रीष्ठित व्यवस्था पर वृद्धिक है। हमें भीता है स्वतान और विचीत्र विचार अस्ता वह रेट पत. कार्य अन्तर, प्राप्त स्टेंबर के स्वती, एक्ट्रेंबर मार्च, कुल दर्शका, हुद्धे ६० ००० होता

रीप्रदेशक L65910MH1984PLC032039 । रेस्ट्राट www.pram.alfinance.com देख वार्यावव : हिन्दु देश, देसदेव व त्यापर गर्द गरिक प्रदेशक देश के देशे अवस्थित के राज्ये अवस्थार देश

मीना <u>रा</u>पना मेनवुरेटाच नेका एड रिकास्ट्रका और प्राणनविकार अनेद्रा एड एस्पोनिट औप रीकपुरिटी इंटरेस्ट प्राट 2002 अस्तान सेकपुरिटी इंटरेस्ट (प्राथमेरीट) विकास २००२ के विकास ३(१) राहबायत अपुण्डेव (३(२) के अतार्थित विकास क्रिक्टन एड हार्जरीया प्रकासक विकारित (जीतरायाण्याला) त्यार्थ का विकास हार्जरीया प्रकासक विकारित (जीतरायाण्याला) त्यार्थ का विकास हार्जरीया प्रकासक विकारित (जीतरायाण्याला) रेक्टर मानावर आर एक्टर के प्रकार प्र असेद्रत एउ परकोतीर और सीवपुरिश इंटरेस्ट एक्ट, 2002 (स्टोर्की एक्ट) के उनुस्तित अनक्षति वृक्त औरकार के साव अधिकारोक काम के अनकी है। अस्ति के प्रतिकृत अधिकारी है। सीवचुरियाइनीका प्रतिकार्द्रमास्य और परावस्तिकास असेद्रम प्रत कार्योगीट और सीवचुरियाइनीका प्रतिकार्द्रमास्य और परावस्तिकास असेद्रम प्रतिकारी में सीवचुरियाइनीका प्रतिकार्द्रमास्य और परावस्तिकास असेद्रम प्रतिकारी में सीवचुरियाइनीका प्रतिकार्द्रमास्य अवाक्ताकारत का प्रमानून अध्यक्त हा राजपुरत्यामका प्रभावमञ्जालक काम प्रभावनाथ अन्यता प्रभावनाथ अन्य राजपुरत्य इटरत्य प्रया, राज्य स्वस् प्रवा) के अंतर्गत प्रथा अध्यक्त के राज सेन्युरेटी इंटरेस्ट (एकोसेनेट) निवस, २००२ के सिथा 3 सहनायन प्रथा के अनुसर्गत १३(१२) अस्पीत स्वार प्रवाट के विचार के आतार क्या जावावर का चार स्वयुक्त बटस्ट स्थावास्तात कावत, राज्य वा क्या उ सहवायत एसट का अनुवाय काराश उसकार स्वट प्यट क अनुवाद (अर्थ) के असर्वात संघा सुचल जाते वर्धावृत्त अधिवाते को की गई है, क्षिप्त सर्वास (अर्थ कर्वायर) को विचा निर्देशक रक्ता का व्यवस करते के विचा संघा सुवना अभी को आई की एवं सुवान इस एकर की आते हैं की. एक बाद सबर कार्नवार को लेकर कर पदान करने के विश्व किस किसीकर रकत कर पदान रूपर सुवान के प्रकारण की निर्म है 60 दिन के अंदर किया गया है पूर्व अधिक काल संदर सुचल में दिने का है। कार्य का पुन प्रवास को निर्म है दिना के प्रवास का प्रवास कर प्रवास का के पास सबर कार्जबार हात जिस्के रखा था. स्वर कार्जबार को पीतीरकरमञ्जूण हमा पान किर्स्क रूपभात के लिए कर्ज यह होकर रक्तम उद्यान सहन्य होगा।

	marks D.O. A	ाता के लिए कर्न यह किया स्वाभ एकत करना होगा। संपतित का प्रसा			
(बोरेट) हासा का एसरी अंबर ०५७०००००००२२) भेवर विश्व मानावत (उमारकार्त) भेवर बोवर (स्व उमारकार्त १)	27-11-2023 / 75, 104334/- (2), (3), (3), 所面 中央	पर्वेट अंदर ४ ए (एमेटर्स आहर केन्स्सान के करन			
रम्बाराज्य सर्वता का एसकी संबर 09000004553) जमवीर यंत्र राज्योरी (उधारकार्त) सरेता वेदी (रफ-उधारकार्त)	२७:11-2023 / रू 240163/ (दे सन्ध चन्नेत्र इत्तर एक से विस्तार राज्ये) एनविष् (06-01-2023)	USC SIZE Q-201 MINE STEEDS STREET 326			
(जवपुर-वैज्ञारी शाया का एससी संबर 00900016021) स्रकेट कुमर (उदारकती) वीरी वी (स्कारणावारी)	२७-११-२०२३ / रु १६३२२००/- (पंद्रश्च साम्य अहारीन हजार से से कार्य) पुस्तेष (०० १० २०२३)	पहेंद्र संद्रा प्रकाश वर्षेत्र स्था के			
(उवापुर-देशको शाका का प्रतिनी संदर 00900016:394) स्वाम राम (उपारकार्य) उम्मोद राम (राह-उपारकार्य १)	27-11-2023 / र. 1403386/ रह. पेदह लगा तंत्र से क्रिकाओ रुप्ति (१८०१० २०२३)	प्रकारीका, एसीज, वांस्थात होड उद्यूप अवद्र व प्रकार कर कर कर कर कर कर कर कर कर कर कर कर कर			
(अयपुर : प्रमुशाई रोड खाळा का पुलरी संबर २०९०:२०१४:४८:५) और एकाह ब्रह्मोलिय (उपारवसर्च) भन्मा (संव:उपारवसर्च १)	20 12 2023 / ਲਾਪਰੇ 840732/- (370 ਲਾਣ) ਬਾਨੀਲ ਛ-ਫ਼ਾ ਨਾਜ ਦੀ ਥਾਜ਼ਿਤ ਨੁਪਲੇ) ਪ੍ਰਮੁਕਤਾ (00 11 2023)				
कारनपुर सावत का प्रस्ती शक्त 24000002931) क्रील कुन (उमारकारी) दुर्जन कुन (सह-उमारकार्त 1)	Del de la la la la la la la la la la la la la	tele sign 3. Series was those to be seen			
जयपुर - प्रभागाई रोड शास्ता का पलसी नंबर १९३०६०४ ४४५६६) एकाम पुली (उपरकर्ता) बस्तरे देखे सफ-उपरकार्त १)	माख वर्षय सी चीरतर रूपने और शिरुप्त देसे।	के सहस्यात कर के के प्रकृत कर कहत और का अनुक्रों 1100 के अपने के का क्षेत्र के के अपने अपने के अपने अ			

अवस्था अन्य प्राप्त करें। किसै से प्रतित को स्टर एकट के अन्योत प्रवृत्ति स्टर एक एक किए प्रतित करें कि से स्टर स्टर्भ हमेशास करें। किसै से प्रतित को स्टर एकट के अन्योत प्रवृत्ति स्टर एक एक के एका अन्य अन्य के स्टर्भ के स्ट ERRY (plung adjust)

चिरमाम केविटन एवड स्टानिंग काववस्थ रिकीर्टर

वरीद फाईनेंस

दिनों बाद सुभाष की शादी है, वह निपटाने के बाद दिसम्बर में वापस यहां सड़ा गांव आ जाएंगे। गोविन्दराम यहां से जाने के बाद भी उससे कुछ दिनों तक सम्पर्क में रहा और गाड़ी कि किश्ते समय पर जमा करवाने का आश्वासन देता रहा। आरोपी ने दो किश्ते जमा करवाई और इसके बाद किश्त जमा नहीं करवाई। इस पर कंपनी की और से उसके फोन आया और उससने आरोपियों से सम्पर्क करना चाहा तो आरोपी ने उसे फोन पर धमकाया तथा पैसे एवं गाडी भूल जाने के लिए कहा। साथ ही धमकायाँ कि अगर सीकर में पैसे लेने या गाडी लेने के लिए आया तो उसे जान से मारने की धमकी दी। कंपनी की और से उसे लगातार लीगल नोटिस मिल रहे है।

化多点。1986年198日,1986年198日,1986年198日

हुन्छाया अजनलात गमा का स्थित व नागीर जिले तह होस

पात्रका न्यूज नटवक

वाला का अब बख्शा नहा

कार्यस् राज म बराजगारा

तीरप और जेम्स लगाकर इसे बेरिकट की कीम, चौकलट पह पक जोएं तो उस पर ते बार मिनट तक संकेंगे। जब करिट करेंगे। आपका मिनी व्या है। फर पतट कर इसी प्रकार तीन

584 पर अपनी क पन स कड क्ल

會

1

मुख्यमंत्री ने कहा कि कांग्रेस

बुधवार की धोद इलाके के बोसाणा यात्रा के शिविर में बोल रहे थे। गांव में विकासत भारत संकल्प सोच भी नहीं सकेगा। मुख्यमंत्र

भी अपराधी राजस्थान आने की

ok.com/patrikaSheNews

अपराधियों पर शिकंजा कसना गुरू हो गया है। आने वाले समय में कोई शरणस्थली वन तया था। अव प्रदेश इसरे राज्यों के बदमाशों की हो गया है। कांग्रेस राज में प्रदेश के बेरोजगारों को दर्द देने बालों को अंत बंद्धा नहीं जीएगा। पहले

STATE OF मीना शया

> ही प्रदेश की जनता के स्वामिधान और सम्मान लौटाने का काम शुरू प्रदेश में भाजपा की सरकार के आते स्वापिमान को गिराने के काम हुए राजस्थान के मान-सम्मान और ने कहा कि कांग्रेस के राज मीकर, मुख्यमंत्री भजनताल शर्मा बासाणा गांव में आयोजित शिवेर में जानकारी होते सीएम भजनताल

खत्म होगा नकल माफिया और गुंडाराज

नकल माफिया और गुडाराज ख़त्म कर देंगे। पहले अपराधी थेखाँफ थे, लेकिन अब अपराधियों पर नकेल कराने के को पंडित दीनवयाल उपाध्याय के अंत्योदय से जोड़ते हुए कहा कि जब प्रवेश अपराध मुक्त होगा क्योंकि मोदी की ग्रारंटी की संस्कार बन गई। लिए भी एसआइटी गांधेत कर दी है, अब आमजन बेखेंक रहें। प्रदेश में मुख्यमंत्री ने नागौर जिले के खियाला गांव में विकत्तित भारत संकल्प यात

राज में 19 में 17 पेपर लीक हो गए। इससे बेरोजगारों के साथ उनके परिजन का भी सिस्टम से विश्वास 19 रौरान एसआईटी का बादा किया उठ गया था। भाजपा ने चुनाव के

te take

चारिकाओं स मुनतार्थ करते हुए गाँप अवस्ति न कहा था कि गया है, उसे पूर्व तया सक्ते नहा स्त्री क्षेत्र मागते. में हिंडनवर्ग रिपोर्ट में तो कुछ कहा सामा को संकता। गिराक्ट देखने को जिन्हा विकल क बाद समुद्र के ग्रवता में वर्त ममूह ने रिपोर्ट को जातित कर 여러- 그룹하는 하라라는 왕리구 अन्त शक्त के क्षेत्रत वा था। इत्सांक तिवार अन रिपार्ट के मुताबिक अवनी ने

n.vvw.moef.gav.in २२ देखा के सकता है एवं इसकी प्रतिस्थिते राजसान ाज्य प्रद्वाचा

村最 CEO Smelters, HZL

ा। व्यवस्त्रकारी के पात भी उपल्या है।

में भी आयोजित की जाएकी के बातर और मंत्रालय के दुरा गहली चार यह परीक्षा छानामगढ़ अप्रेल के सेशन में यह मिनती मध्य की लोख है पर गई है। और बढ़ने की संधानना है ला का अवंदर क 340

र्ता क्षेत्र के बहु के ने 24 बिंदर को फिएना भूगीशत रहा

24 जनशरी में एक

निर्देश देते हैं। इस चलते में युन्ताह महोते के भीता, जान गर्म करने हैं। 計場的以及中国公司 ित्य हैं और दोषिकों तक पहुंचने ित्तार के हुन्त हैन जाता है के भरत संबंध के चित्रा के जी जांच एजेंसी ने इसे गंभीरता से

राजस्थान पत्रिका

Date Park To

मध्यमिक शिक्ष बोर्ड अलगर।

एक बरी और 5 की भी सेट की स्थापना) तुतु पर्गावरण रही कृति (क्वोपरेस) प्रवास की गई है। माध्यम ते सी.पी.फी. का विकास । केंक्र प्रोप्तर उत्त्वादम फनरेटर , गाउनम नेटरह की रहाडेन निभागी काताब और 1 एंड हे काहनगं भी खालना, आहु नैकरण और तताना के ाडतो असे आर्थाताओ पूर्वर के तर्मा करता, जार शतु के अधार कर टाउटे गुरू व जिस सीमानि को पर्यावरण, तम और जलवाडु परिवर्तन स्काटन को नेप्स्कृ 29 12 2023 के इस मैठन रिज़ेटन जिल हिन्देर ग्राम पुरस्ति अस्तिमान सम्बंह अर्थ विशेष स्वनीत स्पृतिस और पेटाइन्ड जिला- पेटानमह में सेट्ड में सेट के ित्र सोस्टर के भीतर विसंतर (तांड हो जात में इंडक्सन करीत, १ सोड कर्नेटर जान्त्र और ाउन महत्वप के पत्र कर्नाक IA-J-11011/279/2006-IA-III/10-1) दर्गक

पंचकर्म टेक्निशियन सर्टिफिकेट कोर्स राष्ट्रीय आयुर्त सरकार जोरावर जिंह गेट, आमेर रोड, जयपुर - 302002 (अस्प्रिंग्संत्रालयं, भारतं सरकार) मानद विश्वविद्यालय (डी-नोर्व)

आवंदन करें। सीनियर सैकेण्ड्री योग्यता धारक इच्छक अध्ययो वेबसाईट देखकर स्परत विवरण संस्थान की वेबसाईट www.nla.nic.in पर दिया गया है दिनीक 05.02.2024 तक आवेदन आमंत्रित किये जाते हैं। संस्थान में पंचकर्म टेक्निशियन सर्टिफिकेट कोर्स (1) वर्षीय) में प्रवेश हेतु दिनाक: 02.01.2024 स्य प्रकाश श्रम

(संयुक्त निर्शक्त)

उदयपुर सिटी एक्सप्रेस ट्रेन 1 घटे 14 मिनट भोपाल, दुबई, वाराणसी जाने वाली फ्लाइट आला हजरत एक्सप्रेस ट्रेन 1 घंटे 8 मिनट देरी से पहुंची। इधर, जयपुर इंटरनेशनल रयरपोट पर सुबह पीने सात बजे उदयपुर और सुबह 8.35 बजे अहमदाबाद जाने वाली पैलाइट भी ऐनवक्त पर रह हुई। अधिकाश भागों में हत्की बारिश हो छह जनवरी के बाद प्रदेश के

20.00 4.00 V

असर से प्रदेश में अधिकांक भागों मे तापमान में गिरावट आएगी। तापमान जनवरी बाद नए पश्चिमी विक्षोम के हल्की बारिश हो सकती है। जिसले Phones and the same 4. मौसम विभाग के अनुसार छह गिरने के साथ नमी बढ़ने से

पश्चिमी विक्षोभ छह जनवरी को

STATE AND ABOUT ABOUT को संभावना जताई है।

कर रहे ट्रक ड्राइक्सों ने बुधवार क प्रशासन से आस्वासन मिलने के ह हड़ताल बत्न कर दी। हालांकि इ पहले सोमवार से धुरू हुई दुकों स डडताल के कारण कई राज्यों से इ तमात हो गई। अनुपाद जिले के प्रमावित हुई। श्रीगंगानगर में भी बालकों की हडताल तीसरे दिन वाले जरूरी सामान की अपनित

बांसवाडा में बाहन चालक शाम रायसिंहनगर कर्य में शही कु चालकों को हाईवे से हटा दिया। चालकों की हड़ताल से रिफाइनरी निमणि कार्य दो दिन से पूरी तरह से बंद पड़ा है। हड़ताल के चलते कोई हड़ताल के चलते बाइमेर जिले में कई पम्प पर पेट्रोल-डीजल खत्म हो वाहन भीतर नहीं जा रहा है। इच्स तीन दिनों से आपूर्ति उप पड़ी है। वहीं रोडबेज बसे तो चली लेकिन यात्री भार कम मिला। जिले में निजी बमों गया। पम संचालको का कहना

मरम्मत करवा रेलवे का ब्रह्म। तार टूटने की घटना के चलते परिचम डीलक्स एक्सप्रेस, पुणे. निजामुदीन दुरतो के साथ कड दरंती के साथ ही जयपुर-कीयंबद्र, अमृतसर-मुंबई रोकी गई ट्रेन

> बाद अपलाइन पर भी द्रम क आवाजाही शुरू कर दी गई।

हिसार-मृद्ध दुरता रुक्सप्रस (12240) के इंजन के पैटीग्राफ की कार्बन सिट्ट्रप के दूरकर ओक्सहेड लाइन में उलझने बॉल्टेज बिजली लाइन (ओएनई) टूट गई। इसके चलते अपलाइन मार्ग की कई ट्रेने रास्ते में अटक गई। रात को की मरम्मत शुरू की, जो सुबह तक जारी रही। मरम्मत और परीक्षण के ही तीन टाकर कैंगनों ने विद्युत लाइन से करीब डेड किलोमीटर तक हाई

सुपरफास्ट ट्रेन 2 घंटे 35 मिनट, शालीमार एक्सप्रेस ट्रेन 2 घंटे 22 मिनट, खजुराहो-

36 मिनट व प्रयागराज-बीकानर सुपरफास्ट שייוניםן ישישיר עשוו לשמוא ביו צ ער 8 घंटे 29 मिनट देरी से पहुंची। बाड़मेर्







Date: 18-01-2024

Subject:

Environmental Clearance for "Expansion within the existing Chanderiya Lead Zinc Smelter Complex at villages: Putholi, Ajoliya Ka Khera & Biliya, Tehsil: Gangrar & Chittorgarh, District: Chittorgarh (Rajasthan)" by M/s. Hindustan Zinc Limited -Regarding issuance of Unvironment Clearance

Sir.

With reference to the aforesaid subject, we would like to inform you that the "Expansion within the existing Chanderiya Lead Zinc Smelter Complex [Expansion in Hydro Plant by adding 1 Induction Furnace, 1 Slab Casting Line &Integration of RZO Unit in Hydro-II, Change in Product Mix in Pyro Unit on total metal basis & Installation of 1 Lead Refinery, Expansion of CPP through Modernization and Installation of TBPTG, Recovery of Minor Metals & Installation of 5 DG Set] at villages: Putholi, Ajoliya Ka Khera & Biliya, Tehsil: Gangrar & Chittorgarh, District: Chittorgarh (Rajasthan)" by M/s. Hindustan Zinc Limited Project is been granted Environment Clearance MoEF&CC, New Delhi on 29.12.2023. vide File no. IA F11011/2/9/2006 IA II(IND-1) on 29.12.2023 . EC letter has been annexed herewith for your records and reference.

Thanking you & with regards,

For Hindustan Zinc Limited

AGM - Environment

Chanderiya Lead Zinc Smelter Unit

सरपंच ग्राम पंचायत पुटोती वं. अ. पंगायर (जिल्लाइगई

Encl.: As above

Hindustan Zinc Limited

Registered Office

Yashad Bhawan, Udaipur-313 004, Rajasthan, INDIA. 1 +91 294 6604000-02 | www.hzlindia.com CIN: L27204RJ1966PLC001208

Chanderiya Lead Zinc Smelter P.O. Putholi, Chittorgarh-312021, Rajasthan, INDIA

P Manojkumar



From: Anoop Kumar

Sent: Saturday, August 31, 2024 5:22 PM To: ALL HZL EMPLOYEES OF CSC LOCATION Cc:

Manas Tyagi; Kamod Singh; Tarun Meghwal; Manisha Bhati; TC Khatri; Tannu Mittal Subject:


Addressing Plastic Pollution at Zinc Nagar Residential Campus Attachments:


SUP Alternative English.pdf; WhatsApp Audio 2022-06-22 at 4.23.13 PM (1).mpeg

Dear All,

We would like to bring to your attention a serious matter that affects all of us and that is the harmful impact of plastic on our environment. Single-use plastics in particular have become a significant threat to the well-being of

In an effort to reduce plastic waste and promote sustainability, we would like to inform you that single-use plastics (including plastic/polythene carry bags etc.) are now banned in our colony (Zinc Nagar) w.e.f. 1st Sept 2024. All Shop owners in Zinc Nagar have been intimated by Admin team in writing and there shall be penal consequences





Plastic: Useful for = minutes, harmful for decades.

Ban on usage of single use plastic in zinc colony from 1st september







Plastic toothbrush: 500 years to break down.

Plastic bottles: 450 years to break down.

Plastic straws: 200 years to break down.





Coffee cups: 30 years to break down.

Plastic bag: 20 years to break down.

Therefore, we appeal you to please carry a non-plastic carry bag with you when you go for shopping. This simple act will significantly reduce the amount of plastic waste generated in our community.

Let's work together to protect our environment and create a cleaner, greener future for ourselves and future generations.

Thank you for your cooperation and support.

Many Jingles and video available on RSPCB Website Videos – link https://environment.rajasthan.gov.in/content/environment/en/rajasthan-state-pollution-control-board/information/WasteManagement/PlasticWasteManagement/EliminationOfSUP/Creatives.html

Regards,

<u>List of Single Use Plastic Items to be banned w.e.f.</u> 01.07.2022 and its alternative

S.No Banned Single Use Plastic Items		Alternative to banned Single Use				
1.	Ear buds with plastic sticks	Plastic Items				
2.	Plastic sticks for balloons	Ear buds with wooden/Bamboo sticks				
3.	Plastic flags	Wooden/Bamboo sticks for balloons				
4.	Candy sticks	Cloth/Paper flags				
5.	Ice-cream sticks	Wooden/Bamboo sticks				
6.	Polystyrene [Thermocol] for decoration	Wooden/Bamboo sticks Paper/Cloth/Tree leaves for decoration				
7.	Plates, cups, glasses	Steel/Ceramic/glass plates, cups, glass. Compostable/Biodegradable plastic items. Cutlery made of tree leaves				
8.	Forks	Steel/Bamboo/Sugarcane fiber(Bagasse) based Compostable/ Biodegradable plastic forks				
9.	Spoons	Steel / Bamboo/Ceramic/ Sugarcand fiber(Bagasse) based Compostable Biodegradable plastic spoons				
10.	Knives	Wood/Steel knives and knives made from Compostable/Biodegradable plastic				
11.	Straw	Paper/Bamboo/Compostable/Biodegradable plastic Straw				
12.	Trays	Steel/Glass/ Compostable/Biodegradable plastic Trays				
13.	Wrapping or packing films around sweet boxes, invitation card, and cigarette packets	Films made of Compostable/Biodegradable plastic				
14.	Plastic or PVC banners less than 100 micron	Banner made from Cloth/paper and Plastic or PVC banners more than 100 micron				
15.	Stirrers	Wood/Steel Stirrers				



Commitment to Reduce Single Use Plastic in HZL

HINDUSTAN ZINC

Dear All.

In compliance with the Advisory from Ministry of Environment, Forest and Climate Change (MoEFCC) on 11th Sept'19 to curb the use of Single-Use Plastic, HZL is also committed to reduce the use of below mentioned Single Use Plastic from 2nd October 2019, and shift to other environmental friendly materials. This advisory is applicable to all the Units, Offices and Township of HZL and we expect all employees and contract employees to comply the

- All plastic carry bags, with or without handles, irrespective of thickness and size
- Plastic cutlery including plates, plastic cups, straws, stirrers etc., Cutlery and other decorative items made of Styrofoam (Thermocol).
 - Artificial flowers, banners, flags, flower pots
 - PET plastic water bottles
- Plastic stationary items like folders, etc.
 - Food packages and containers

Plastic being non-biodegradable appears to be a hazard for safe and clean environment and we are aware of the harmful effects of littered plastic that is accumulated over time which poses serious threat to our ecosystem.

This is our time to stand up together and contribute in reducing per capita consumption of plastic.

All are suggested to make the changes accordingly at your work place and at home so that we can successfully reach the Target of elimination of Single-Use Plastic by 2022. Units are suggested to organize awareness sessions for Employees, Contractor Employees, Families at township and to our Suppliers to raise awareness on reducing Single Use Plastic. Various campaigns and drives to be initiated at all the locations, visual displays, cloth bags distributions, vending machines installation at prominent places etc. can contribute to the advisory. Encourage source segregation of waste, standardized Waste collection and transportation systems and other best practices should be inculcated.

We look forward to all of us implementing the plan with innovation and creativity and lead by example in the industry for introducing best environment-friendly sustainable practices.

Sunil Duggal

स्वत्छता ही सेवा... 🗬 CEO & Whole Time Director



Bidder's Undertaking to Comply with Plastic Waste Management (Amendment) Rules, 2021 on Prohibition of Single Use Plastic (SUP) items

,	
O, Hindustan Zinc Limited	
bject : Acknowledgement and Undertaking to comply with the Plastic Waste Manageme mendment) Rules, 2021 on Prohibition of Single Use Plastic (SUP) items at Hindustan Zir emises.	ent nc Limited
nder Ref:	
ntract Ref:	
icknowledge and understand the	

I, acknowledge and understand the responsibilities as a Supplier/ Service provider/ Aggregator/ Contractor/ Sub- Contractor/ Consultant/ or as an individual/entity (Bidder) engaged by Hindustan Zinc Limited (HZL) and undertake to comply with the Plastic Waste Management (Amendment Rules) 2021 and accept to operate and undertake all activities in such a manner as to meet Vedanta's Environment Social Governance (ESG) commitments. I understand, acknowledge and accept that the responsibilities and obligations mentioned below including but not limited to, are mandatory criterion, to qualify for the tender.

Following responsibilities and obligations including but not limited to as enumerated below, are agreed to be complied upon by the Bidder to qualify for a successful Bid, for the tendered Services/ Supplies/ EPC/ Consulting/ or any other work of any nature whatsoever for which the Company has proposed to engage the Bidder:

- That the identified Single Use Plastics (SUPs) shall not be used by any means while delivering services/ materials in any form.
- That they shall provide the details and information of the possible SUP items which they shall
 be using as a part of the contractual requirements. Whereas the Bidder must propose to be
 adopting alternative materials to replace SUPs to deliver Scope of the Work of the Contract.
- That the packaging of any Chemicals, Materials, Goods, Consumables, or any other Commodities shall not use Single Use Plastics (SUPs).
- That the Bidder shall not use any Single Use Plastic items either for packaging, distribution, storage or otherwise for any materials, goods, supplies or for rendering of any services.
- That no manpower of the Bidder shall use or carry any prohibited SUPs items within the HZL Premises. Refer Annexure-1 Guidance Document on Prohibited of Single Use Plastics (SUPs)
- That in case any SUPs are required to be used for any unavoidable reasons, the Bidder shall
 declare the same and submit a list of all such SUPs along with the plan for effective
 management (collection, segregation, recycling/repurposing, disposal) of such SUPs along
 with this declaration. In absence of such plan, it shall be deemed that no SUPs shall be used
 by the Bidder in any manner for discharging its obligations under its proposed scope of work
 for which the Bid is being made.
- That in case any SUPs are required to be used for any unavoidable reasons, the Bidder shall submit a list of all such types of SUPs which they shall be using as a part of the contractual requirements. Refer Annexure-2 Guidance Document on Types of Single Use Plastics (SUPs).

The Bidder shall be solely responsible and liable for use of any SUPs and no liability of any nature whatsoever shall be accepted by the Company for the usage of SUPs by the Bidder or its subcontractors. The Bidder shall indemnify HZL for any loss or damage sustained by HZL due to the Bidder's usage of Single Use Plastic in contravention of the law.

I hereby affirm my compliance to the above requirements as per applicable laws, regulations

Vedanta's ESG commitment and agree to be bound by the same	s per	applicable	laws.	regulations
Bidder name:	9.			6018 (10113
Date:				
Place:				
Authorized signatory & stamp				

NOTE: Upon award of the Contract to the Bidder, this Declaration shall form part of the Contract and any non-compliance or breach of the same shall entitle HZL to avail the available contractual remedies along with the remedies available under the law.

Annexure-1: Guidance Document on Prohibition of Single Use Plastics

Hindustan Zinc, a subsidiary of Vedanta Limited, is India's largest and world's second largest fully integrated Zinc-Lead miner that has over 77% market share in India's primary zinc industry, is among the top six silver producers globally and a part of the Wind Energy business.

Our Business Partners' commitment to and fulfilment of the ESG (Environment, Social & Governance) Expectations is a matter of paramount importance to HZL and will be assessed as a factor when HZL considers awarding commercial opportunities. HZL will apply the ESG Expectations on a global basis and will integrate them into the various practices involved in HZL's qualification, evaluation, selection,

At HZL we are committed to identifying, reducing, and mitigating the negative impacts of our business activities on people and on the environment. We are on a journey to embed sustainability into our business to protect, connect and power a more sustainable world.

Environmental Social & Governance (ESG) is a renewed way 'how we do business'- to meet the expectations of stakeholders/ suppliers/ customers/ contractors/ employees/ consultants/ shareholders. In alignment with the same we have announced several bold commitments like Net Zero by 2050 or before and Net Water Positivity by 2030. Similarly, we aim to achieve zero usage of Single Use plastics in our premises and be compliant with the applicable laws.

We as an Organisation are committed towards demonstrating our compliance towards the latest Plastic Waste Management (Amendment) Rules, 2021 from Ministry of Environment, Forest, and Climate Change (MoEF&CC), prohibiting use of Single Use Plastic (SUP) items effective from 1st July 2022 and restricting usage of plastic bags with thickness less than 120 micron from December 2022.

In furtherance of the same, all our service providers and suppliers of chemicals, goods, consumables, and commodities are required to ensure that plastic materials shall not be used for packing of material and in case of integrated plastic lining of the product, the thickness of the same must be above 150 micron and the same shall be notified to the HZL procurement team in advance before accepting the order or dispatching the item along with an effective collection and disposal plan from the HZL

Single-use plastic commodity means any plastic item intended to be used only once for the same purpose before being disposed-off or recycled, e.g., disposable straw & cutlery, Poly & Non-woven carry bags, PET Bottles, packaging materials like films, wrappers, foam sheets etc., In addition to the identified Single Use Plastic items by the Ministry of Environment, Forest and Climate Change vide its notification No. G.S.R. 571(E) dated 12th August 2021, below is an indicative list of the Single Use Plastics the use of which in any manner whatsoever is restricted on the HZL Premises:

- 1. Poly and Non-Woven Carry bags,
- 2. Polystyrene (Styrofoam or Thermocol) items e.g., plates, cups, decorative balls etc.
- 3. Plastic plates, cups, glasses, cutlery such as forks, spoons, knives, straw, trays, stirrers
- 4. Plastic covers, caps, and lids
- 5. Laminated disposable plates, bowls, cups, and glasses of paper 6. Plastic films for Wrapping or packing and multi-layered plastics as packaging material
- 6. Packet with overwrap films of plastic e.g., cigarette packets etc.
- 7. Plastic or PVC banners (Flex)
- 8. PET Bottles
- 9. Plastic sticks with Ice cream, flags, balloons etc.
- 10. Stationery items of SUPs e.g., Sticky files, plastic folders etc.
- 11. Plastic sheets and plastic table spread etc.
- 12. Food Items in Multi-layered Plastic packaging.
- 13. All other item of Single Use Plastic or packed in single use plastic

Poly and Non-Woven Carry bags	Indicative Image
The Note Woven Carry Dags	4 A COUNTY
Styrofoam or Thermocol items e.g., plates, cups, etc., PET Bottles, Plastic flags, or decorative items etc.	
Plastic plates, cups, glasses, cutlery such as forks, spoons, knives, straw, trays, wrapping, stirrers, Disposable	
aminated disposable plates, bowls	
cups, and glass etc	

Plastic films/clings for Wrapping or packing Plastic Packaging. Overwrap films

Single Use Stationery Items of plastics, PVC banners, Plastic sheets etc.

Annexure-2: Guidance Document on Types of Single Use Plastics

Most plastics are not infinitely recyclable like some other materials, such as glass. They are 'down-cycled' rather than recycled; made into lower grade products which are eventually not recyclable. "Plastic" means material which contains as an essential ingredient a high polymer.

Resin identification codes will indicate the type of plastic that an item is made from. RIC, is a set of symbols appearing on plastic products that identify the plastic resin out of which the product is made.

Please tick the appropriate box below, indicating the types of plastics you shall be using as a part of

Recycling Number	Image	Polymer Name	Sec. II				
	1	Polyethylene Terephthalate (PETE)	Recycling Picked up through any				
	4		Picked up through most curb side recycling programs				
े रि		High-Density Polyethylene (HDPE)	Picked up through most curb side recycling programs, although some allow only those containers with necks				
0	1	Polyvinyl Chloride (PVC)					
2400	くむ		Too long life for significant recycling volumes.				
0	1	Law-Density Polyethylene (LDPE)	LOPE is and a fe				
- 1	(4)		LDPE is not often recycled through curb side programs and is a significant source of plastic pollution. LDPE can often be returned to many stores for recycling				
	Polypropylene (PP)		Picked up through most curb side recycling programs.				
- (ت:		and recycling programs.				
o I .	1	6Polystyrene (PS)	Del				
(ند:		Polystyrene is often not recycled through curb side programs as it is too lightweight to be economical to recycle, usually incinerated instead.				
		Miscellaneous Plastics (Mix plastics) multi-materials like					
- (ت.	Acrylonitrile Butadiene Styrene, [ABS] Polyphenylene Oxide, [PPO] Polycarbonate, [PC] Polybutylene Terephthalate [PBT]	Number 7 plastics are not typically recycled as they are mostly specialty produced in limited volumes				
