

Vide Letter No.: HZLP/M&C/25-26/H-I

Date: 26/11/2025

To,
The Regional Officer (North Central Zone),
Ministry of Environment, Forests & Climate Change,
25, Subhash Road, Dehradun, Uttarakhand-248001

Subject: Submission of Environment Clearance compliance report for Pantnagar Zinc-Lead melting & casting Plant (Zinc Metal- 4,65,000 TPA & Lead Metal- 1,50,000 TPA) of M/s Hindustan Zinc Limited, Plot No 2 & 3, Sector 14, IIE, SIDCUL, Pantnagar, Dist. U.S. Nagar for the period April-2025 to Sept-2025.

Ref; Letter No:- J-11011/327/2010/IA-II (I) dated 26.04.2011 from MoEF&CC.

Dear Sir,

With reference to the aforesaid subject, we have obtained Environment Clearance from Ministry of Environment, Forest and Climate Change, New Delhi for Pantnagar Zinc-Lead melting & casting Plant (Zinc Metal- 4, 65,000 TPA & Lead metal- 1, 50,000 TPA) on dated 26.04.2011.

Please find enclosed herewith the Compliance report of Environment Clearance for Pantnagar Zinc-Lead melting & casting Plant of M/s Hindustan Zinc Limited, Plot No 2 & 3, Sector 14, IIE, SIDCUL, Pantnagar, Dist. U.S. Nagar for the period of April-2025 to September-2025.

In case any additional information / documents / clarifications are required, the same may kindly be informed to us.

Thanking you.



(Anamika Jha)

SBU Director

Pantnagar Zinc-Lead melting & casting Plant
Hindustan Zinc Limited

Hindustan Zinc Limited
Pantnagar Metal Plant
Plot No.2&3, Sector 14, IIE, SIDCUL
Rudrapur - 263153, Uttarakhand

CC:

1. Regional Officer, CPCB, Lucknow
2. MS office, UEPPCB, Dehradun
3. Regional Officer, UEPPCB, Kashipur
4. Office copy, HZL



Compliance Report of Environment Clearance (April-2025 to September-2025)

Name of the Project: M/s Hindustan Zinc Limited
Pantnagar Zinc-Lead melting & casting Plant

Location of the Project: Plot No.- 2 & 3, Sector 14, IIE, SIDCUL,
Pantnagar, District - Udham Singh Nagar,
Uttarakhand – 263153

Clearance Letter No: J-11011/327/2010/IA-II (I) Dt.26th April 2011 from MoEF&CC

Period of Compliance Report: April-2025 to September-2025

S.No	Condition	Compliance Status
A	Specific conditions.	
1	On-line ambient air quality monitoring and continuous stack monitoring facilities for all the stacks shall be provided and sufficient air pollution control devices viz. bag filters shall be provided to keep the emission levels below 50 mg/Nm ³ by installing energy efficient technology.	Being Complied. Efficient bag filters and continuous stack monitoring PM analyzers have been provided in all process stacks. Continuous on-line Ambient air quality monitoring station (CAAQMS) is also installed in the plant premises to monitor the ambient air continuously. Emission levels are being maintained well within the stipulated limit. Copy of Ambient air & Stack emission quality monitoring reports attached herewith as Annexure-1(a) & 1 (b) respectively. Photograph of CEMS & CAAQMS are attached herewith as Annexure-2.
2	The National Ambient Air Quality Standards issued by the Ministry vide G.S.R. No. 826(E) dated 16 th November, 2009 should be followed.	Noted and being Complied. Ambient air quality monitoring results are well within the NAAQs limits.
3	Gaseous emission levels including secondary fugitive emissions from all the sources shall be controlled within the latest permissible limits issued by the Ministry vide G.S.R. 414(E) dated 30 th May, 2008 and regularly monitored. Guidelines / Code of Practice issued by the CPCB should be followed.	Being Complied. All Gaseous emission are being controlled through efficient bag filters connected to adequate stacks height provided for proper dispersion. In addition, monthly work zone monitoring is also being carried out. Reports of stack emission and work zone are attached herewith as Annexure-1(b) & 1(c) respectively.
4	The total water requirement shall not exceed 500 KLD. Permission to draw water from the Competent Authority shall be obtained. No effluent shall be discharged and 'zero' discharge should be adopted.	Being Complied. Water requirement of Zinc and Lead M&C process and silver process is limited to 260m ³ /day (20% reduction from previously issued NOC- 325m ³ /day). For which CGWA is already given consent (Letter no.: CGWA/NOC/IND/ORIG/2018/4160 on dated 17 Oct 2018 & 01 Mar 2019 and corrigendum letter against condition no 3 on date 02 July 2019 & its

Hindustan Zinc Limited
Pantnagar Metal Plant
Plot No 2&3, Sector 14, IIE, SIDCUL
Rudrapur – 263153, Uttarakhand

		<p>renewal). The present CGWA NOC 2nd renewal is valid till 26.09.2026 with 260m³/day withdrawal capacity having Letter No.- CGWA/NOC/IND/REN/2/2023/8194 dated 06.09.2023. No effluent is being generated from the process. However, Effluent treatment plant of 87 KLD is already provided for treating the combined trade effluents of Zinc & Lead melting casting and Silver refining plant so ETP is not in operation.</p> <p>Combined STP of 30 KLD already installed to treat the wastewater of Zinc and Lead Melting & Casting unit as well as silver plant. Treated water of the same is being used for horticulture/plantation. Zero discharge is being maintained.</p>
5	<p>Regular monitoring of influent and effluent surface, sub-surface and ground water shall be ensured and treated wastewater shall meet the norms prescribed by the State Pollution Control Board or described under the E(P) Act whichever are more stringent. Leachate study for the effluent generated and analysis should also be regularly carried out and report submitted to the Ministry's Regional Office at Lucknow, SPCB and CPCB.</p>	<p>Being Complied. No effluent is being generated from the process. Ground water being used for plant operation and regular bore well monitoring being ensured. Zero Discharge is being maintained and no effluent discharged to surface water body.</p> <p>Provision for online monitoring of STP outlet for BOD, COD, pH, TSS & Flow has been made.</p> <p>Copy of ground water monitoring is attached herewith as Annexure 1(d).</p>
6	<p>Efforts shall be made to make use of rainwater harvested. If needed, capacity of the reservoir shall be enhanced to meet the maximum water requirement. Only balance water requirement should be met from other sources</p>	<p>Complied. Presently We have four rainwater harvesting pond for rainwater collection having capacity approx. 2542, 1500, 841 and 750 cu.m and collected rainwater is being utilized into the process. In FY 2025-26, H1, we have reused around 11,554 cu.m rainwater in the process for conserving the fresh water. Photograph of the same is attached herewith as Annexure-3.</p>
7	<p>Risk and Disaster Management Plan along with the mitigation measures should be prepared and a copy submitted to the Ministry's Regional Office at Lucknow, SPCB and CPCB within 3 months of issue of environment clearance letter.</p>	<p>Complied. Risk and Disaster Management Plan has been submitted to Ministry's Regional Office at Lucknow, SPCB and CPCB on 20.07.2011. Also, we have prepared and submitted On Site Emergency plan to the competent authority.</p> <p>Latest/amended receiving copy for submission obtained on 27.09.2024 to Dy. Chief Inspector (Factories & Boilers). Refer Annexure-7.</p>
8	<p>As proposed, green belt shall be developed in 33 % of the plant area. Selection of plant species should be as</p>	<p>Complied. More than 33% Green Belt of total</p>

	per the CPCB guidelines in consultation with the DFO.	plant area has already been provided with three rows along with boundary wall in plant premises in consultation with DFO (Divisional Forest Officer) and CPCB guidelines. Gap filling plantation being carried out for maintaining the survival rate of Plantation.
9	At least 5 % of the total cost of the project shall be earmarked towards the enterprise social commitment (ESC) and item-wise details along with time bound action plan should be prepared and submitted to the Ministry's Regional Office at Lucknow. Implementation of such program should be ensured accordingly in a time bound manner.	Being Complied. CSR plan prepared and submitted to MOEF-Regional Office Lucknow, CPCB regional office Lucknow and UEPPCB Dehradun along with E.C compliance report as dated 20.07.2012, This had been implemented in phased manner with the help of local administration. Many CSR development activities are being carried out for upliftment of nearby communities. CSR projects details is attached herewith as Annexure 4.
10	Provision shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, Safe drinking water, medical health care, crèche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.	Complied. Safe drinking water, sanitation facilities. Medical health care etc. provided at the plant premises. No housing facility provided in plant premises.
B	General Conditions	
1	The project authorities must strictly adhere to the stipulations made by the State Pollution Control Board (SPCB) and the State Government.	Noted and being Complied.
2	No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment and Forests.	Noted and being Complied.
3	At least four ambient air quality monitoring stations shall be established in the downward direction as well as where maximum ground level concentration of PM ₁₀ , SO ₂ and NO _x are anticipated in consultation with the SPCB including one ambient air quality monitoring station in the downwind direction. Data on ambient air quality and stack emission should be regularly submitted to this Ministry including its Regional Office at Lucknow and the SPCB / CPCB once in six months.	Being Complied. In consultation with RO, UEPPCB, 4 Ambient air quality monitoring location finalized including downwind direction as well as maximum ground level concentration anticipated areas. CAAQMS also installed at plant premises. Monthly monitoring is being carried out in plant area. Data on ambient air quality and stack emission is being submitted regularly as stipulated. Continuous on-line Ambient air quality monitoring station (CAAQMS) is also installed in the plant premises to monitor the ambient air continuously. Emission levels are being maintained well within the stipulated limit. Copy of Ambient air & Stack emission quality monitoring reports attached herewith as

		Annexure-1(a) & 1 (b) respectively. Photograph of CEMS & CAAQMS are attached herewith as Annexure-2.
4	Industrial wastewater shall be properly collected, treated so as to conform to the standards prescribed under GSR 422 (E) dated 19 th May, 1993 and 31 st December, 1993 or as amended from time to time. The treated wastewater shall be utilized for plantation purpose.	Being Complied. The domestic effluent is being treated in the STP to ensure stipulated quality and used for plantation. Photograph of STP is attached herewith as Annexure-5.
5	The overall noise levels in and around the plant area shall be kept well within the standards (85 dB) by providing noise control measures including acoustic hoods, silencers, enclosures etc. on all sources of noise generation. The ambient noise levels should conform to the standards prescribed under EPA Rules, 1989 viz. 75 dB (daytime) and 70 dB (nighttime)	Being Complied. Acoustic enclosures/silencers are provided for DG, compressors, blowers and exhaust fans to ensure the noise levels within the factory premises is within the stipulated levels for industrial area. Green Belt along with boundary provided to limit the noise from the plant to surrounding areas. Noise monitoring reports are attached herewith as Annexure 1(e).
6	Occupational health surveillance of the workers shall be done on a regular basis and records maintained as per the Factories Act.	Being complied. Pre-employment & periodic medical examinations are being carried out for the relevant occupational hazards at a regular frequency, as per statutory requirements.
7	The company shall develop rainwater harvesting structures to harvest the rainwater for utilization in the lean season besides recharging the ground water table.	Complied. Presently We have four rainwater harvesting pond for rainwater collection having capacity approx. 2542, 1500, 841 and 750 cu.m and collected rainwater is being utilized into the process. In FY 2025-26, H1, we have reused around 11,554 cu.m rainwater in the process for conserving the fresh water. Photograph of the same is attached herewith as Annexure-3.
8	The project proponent shall also comply with all the environmental protection measures and safeguards recommended in the EIA/EMP report. Further, the company must undertake socio-economic development activities in the surrounding villages like community development programmes, educational programmes, drinking water supply and health care etc.	Being Complied. Environment protection measures and safeguards recommended in the EIA/EMP report being implemented, Socio-Economic development activities are being implemented as per action plan. Many CSR development activities are being carried out for upliftment of nearby communities. CSR projects photographs is attached herewith as Annexure 4.
9	The requisite funds shall be earmarked towards the capital cost and recurring cost/annum for environmental protection measures and judiciously utilized to implement the conditions stipulated by the Ministry of Environment and Forests as well as the State Government. The funds so provided shall not be diverted	Being Complied. Sufficient funds available for operation and maintenance of the facility during operation phase. The said funds not been diverted for any other purpose.

	for any other purpose.	
10	A copy of clearance letter shall be sent by the proponent to concerned Panchayat, Zila Parishad / Municipal Corporation, Urban Local Body and the local NGO, if any, from whom suggestions / representations, if any, were received while processing the proposal. The clearance letter shall also be put on the web site of the company by the proponent.	<p>Complied. The copy of the clearance letter submitted to the Panchayat/ Zila Panchayat, Municipal Corporation and Urban Local Body (SIDCUL).</p> <p>EC letter is also available on company website. Link of website https://www.hzlindia.com/wp-content/uploads/Environment-Clearance-Letter-for-Pantnagar-Metal-Plant-Melting-and-Castingmpm.pdf</p>
11	The project proponent shall upload the status of compliance of the stipulated environment clearance conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of the MOEF, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; RSPM, SO ₂ , NO _x and Lead (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the projects shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.	<p>Being Complied. Submission of Six-monthly compliance report of environmental condition with monitoring results (in hard copies as well as by e-mail) to RO, MOEF&CC, Dehradun, Zonal Office CPPCB, Lucknow, MS UEPPCB, Dehradun and RO UEPPCB, Kashipur being ensured.</p> <p>Six monthly compliance reports are being uploaded on the company website. Link of website uploading EC compliance of October'24 to March'25 is https://www.hzlindia.com/wp-content/uploads/PMP-Zn-Lead-EC-Compliance-MC-H2-2024-25.pdf</p> <p>Display board on all criteria pollutants provided at main gate which is being updated regularly. Photograph of board is attached herewith as Annexure 6.</p>
12	The project proponent shall also submit six monthly reports on the status of the compliance of the stipulated environmental conditions including results of monitored data (both in hard copies as well as by e-mail) to the Regional Office of MOEF at Lucknow, the respective Zonal Office of CPCB and the SPCB. The Regional Office of this Ministry at Lucknow / CPCB / SPCB shall monitor the stipulated conditions.	<p>Being Complied. Submission of Six-monthly compliance report of environmental condition with monitoring results (in hard copies as well as by e-mail) to RO, MOEF&CC, Dehradun, Zonal Office CPPCB, Lucknow, MS UEPPCB, Dehradun and RO UEPPCB, Kashipur being ensured. Link of website uploading EC compliance of October'24 to March'25 is https://www.hzlindia.com/wp-content/uploads/PMP-Zn-Lead-EC-Compliance-MC-H2-2024-25.pdf</p>
13	The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company alongwith the status of compliance of environmental conditions and shall also be sent to the respective Regional Offices of the MOEF by e-mail.	<p>Environmental statement of every year is being submitted to Regional Office MoEF, CPCB and UEPPCB. Last Environment statement was submitted to RO, MoEF&CC vide letter no. HZL/PMP/ENV/M&C/2024-25/01 dated 12.09.2025.</p> <p>Environment statement of every year has been</p>

		uploaded on company website. Link of last Environment Statement is https://www.hzlindia.com/wp-content/uploads/Environmental-Statement-Form-V-2024-25-MC.pdf
14	The Project Proponent shall inform the public that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with the SPCB and may also be seen at Website of the Ministry of Environment and Forests at http://envfor.nic.in . This shall be advertised within seven days from the date of issue of the clearance letter, at least in two local newspapers that are widely circulated in the region of which one shall be in the vernacular language of the locality concerned and a copy of the same shall be forwarded to the Regional office at Lucknow.	Complied. Published in newspapers of Dainik Jagaran and Amar Ujala. Copies have been submitted to Regional office at Lucknow along with reply of letter No. IV/ENV/Utr/Ind-34/110/2011/156 dated 08.06.2011 & on 20.07.2011 to CPCB Regional office Lucknow and UEPPCB Dehradun.
15	Project authorities shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities and the date of commencing the land development work.	Noted & complied. Plant was commissioned in March 2012.

Hindustan Zinc Limited
Pantnagar Metal Plant
Plot No.2&3, Sector 14, IIE, SIDCUL
Rudrapur - 263153, Uttarakhand



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 2

TEST REPORT No. NCL/EW-018/27/09/25		DATE OF REPORT : 03/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : AMBIENT AIR
Analysis Start Date : 27/09/2025 Analysis End Date : 03/10/2025
Date of Sampling : 26/09/2025 Sampling Done By : NCL
Time of Sampling : 11:15 AM (26/09) TO 11:15 AM (27/09) Sampling Location : Near Main Gate Security
Sampling Protocol : IS : 5182
Sample ID No. : NCL/EW-018/27/09/25
Sampling Flow Rate for : 0.5 LPM Sampling Flow Rate of SPM : 1.275 Mtr³/Min
Gases (Average)
Sampling Duration : 24 Hrs Sampling Machine Placed at : 3.0 Mtr
Equipments Used : Respirable Dust Sampler (PM10)+Fine Particulate Sampler (PM2.5) With Gaseous Attachment
Height (from ground)

PHYSICAL OBSERVATIONS

Ambient Temperature : 35°C Wind Direction : East to West
Weather Conditions : Clear

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification As per CPCB
1	Particulate Matters (Size Less Than 10µm) (PM10)	µg/m3	IS:5182 (Part 23)	52	For 24 Hrs=100
2	Particulate Matters (Size Less Than 2.5µm) (PM2.5)	µg/m3	NCL/AIR/STP-09	26	For 24 Hrs=60
3	Sulphur Dioxide (SO2)	µg/m3	IS:5182 (Part 2)	15.2	For 24 Hrs=80
4	Carbon Monoxide (CO)	mg/m3	IS:5182 (Part 10)	0.51	For 08 Hrs=02 For 1 Hrs =04
5	Nitrogen Dioxide (NO2)	µg/m3	IS:5182 (Part 6)	26.2	For 24 Hrs=80
6	Lead (Pb)	µg/m3	IS:5182 (Part 22)	BDL(DL-0.05)	For 24 Hrs=1.0
7	Ozone (O3)	µg/m3	IS:5182 (Part-9)	BDL(DL-20.0)	For 8 Hrs=100 For 1 Hr=180
8	Ammonia (NH3)	µg/m3	NCL/AIR/STP-13	BDL(DL-20.0)	For 24 Hrs=400
9	Benzene (C6 H6)	µg/m3	IS:5182 (Part-11)	BDL(DL-1.0)	For Annual=05
10	Benzo (a) Pyrene (BaP)	ng/m3	IS:5182 (Part-12)	BDL(DL-0.1)	For Annual=01

EW-018/27/09/25-1



Checked by
Arvind Singh

Arvind Singh
Sr. Analyst

FOR NEWCON CONSULTANTS & LABORATORIES



Authorized Signatory

- The test report refers only to the particular sample/s submitted for testing and listed parameters.
- Endorsement of the same is neither inferred nor implied.
- Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
- Complaints about this report should be communicated within 10 days of the Issue date of this report.
- The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



Page No.: 2 of 2

TEST REPORT No. NCL/EW-018/27/09/25

DATE OF REPORT : 03/10/2025

S.No.	Test Parameters	Units	Test Method	Results	Specification As per CPCB
11	Arsenic (As)	ng/m3	NCL/AIR/STP-19	BDL(DL-1.0)	For Annual=06
12	Nickel (Ni)	ng/m3	NCL/AIR/STP-17	BDL(DL-5.0)	For Annual=20

End of Report

Remarks : BDL=Below Detection Limit.

EW-018/27/09/25-2



Checked by *Arvind Boudhary*

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither Inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 2

TEST REPORT No. NCL/EW-019/27/09/25		DATE OF REPORT : 03/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : AMBIENT AIR
 Analysis Start Date : 27/09/2025 Analysis End Date : 03/10/2025
 Date of Sampling : 26/09/2025 Sampling Done By : NCL
 Time of Sampling : 11:00 AM (26/09) TO 11:00 AM (27/09) Sampling Location : Back Side of DG Area
 Sampling Protocol : IS : 5182
 Sampling Flow Rate for : 0.5 LPM Sample ID No. : NCL/EW-019/27/09/25
 Gases Sampling Flow Rate of SPM : 1.27 Mtr³/Min (Average)
 Sampling Duration : 24 Hrs Sampling Machine Placed at : 3.0 Mtr
 Equipments Used : Respirable Dust Sampler (PM10)+Fine Particulate Sampler (PM2.5) With Gaseous Attachment Height (from ground)

PHYSICAL OBSERVATIONS

Ambient Temperature : 36°C Wind Direction : East to West
 Weather Conditions : Clear

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification As per CPCB
1	Particulate Matters (Size Less Than 10µm) (PM10)	µg/m3	IS:5182 (Part 23)	54	For 24 Hrs=100
2	Particulate Matters (Size Less Than 2.5µm) (PM2.5)	µg/m3	NCL/AIR/STP-09	28	For 24 Hrs=60
3	Sulphur Dioxide (SO2)	µg/m3	IS:5182 (Part 2)	16.5	For 24 Hrs=80
4	Carbon Monoxide (CO)	mg/m3	IS:5182 (Part 10)	0.53	For 08 Hrs=02 For 1 Hrs =04
5	Nitrogen Dioxide (NO2)	µg/m3	IS:5182 (Part 6)	30.8	For 24 Hrs=80
6	Lead (Pb)	µg/m3	IS:5182 (Part 22)	BDL(DL-0.05)	For 24 Hrs=1.0
7	Ozone (O3)	µg/m3	IS:5182 (Part-9)	BDL(DL-20.0)	For 8 Hrs=100 For 1 Hr=180
8	Ammonia (NH3)	µg/m3	NCL/AIR/STP-13	BDL(DL-20.0)	For 24 Hrs=400
9	Benzene (C6 H6)	µg/m3	IS:5182 (Part-11)	BDL(DL-1.0)	For Annual=05
10	Benzo (a) Pyrene (BaP)	ng/m3	IS:5182 (Part-12)	BDL(DL-0.1)	For Annual=01

EW-019/27/09/25-1



Checked by *[Signature]*

Authorized Signatory *[Signature]*

FOR NEWCON CONSULTANTS & LABORATORIES



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither Inferred nor Implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
 Mobile : 9810430345, 9205501788 | Website : www.newconlab.in
 E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



Page No.: 2 of 2

TEST REPORT No. NCL/EW-019/27/09/25

DATE OF REPORT : 03/10/2025

S.No.	Test Parameters	Units	Test Method	Results	Specification As per CPCB
11	Arsenic (As)	ng/m3	NCL/AIR/STP-19	BDL(DL-1.0)	For Annual=08
12	Nickel (Ni)	ng/m3	NCL/AIR/STP-17	BDL(DL-5.0)	For Annual=20

End of Report

Remarks : BDL=Below Detection Limit.

EW-019/27/09/25-2



Arvind K. Goudhary
Checked by Analyst

FOR NEWCON CONSULTANTS & LABORATORIES



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 2

TEST REPORT No. NCL/EW-069/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : AMBIENT AIR
 Analysis Start Date : 26/09/2025 Analysis End Date : 01/10/2025
 Date of Sampling : 25/09/2025 Sampling Done By : NCL
 Time of Sampling : 11:00 AM (25/09) TO 11:00 AM (26/09) Sampling Location : Canteen East Side
 Sampling Protocol : IS : 5182
 Sample ID No. : NCL/EW-069/26/09/25
 Sampling Flow Rate for : 0.5 LPM Sampling Flow Rate of SPM : 1.26 Mtr³/Min
 Gases (Average)
 Sampling Duration : 24 Hrs Sampling Machine Placed at : 3.0 Mtr
 Equipments Used : Respirable Dust Sampler (PM10)+Fine Particulate Sampler (PM2.5) With Gaseous Attachment
 Height (from ground)

PHYSICAL OBSERVATIONS

Ambient Temperature : 36°C Wind Direction : East to West
 Weather Conditions : Clear

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification As per CPCB
1	Particulate Matters (Size Less Than 10µm) (PM10)	µg/m ³	IS:5182 (Part 23)	56	For 24 Hrs=100
2	Particulate Matters (Size Less Than 2.5µm) (PM2.5)	µg/m ³	NCL/AIR/STP-09	30	For 24 Hrs=50
3	Sulphur Dioxide (SO ₂)	µg/m ³	IS:5182 (Part 2)	17.2	For 24 Hrs=80
4	Carbon Monoxide (CO)	mg/m ³	IS:5182 (Part 10)	0.50	For 08 Hrs=02 For 1 Hrs =04
5	Nitrogen Dioxide (NO ₂)	µg/m ³	IS:5182 (Part 6)	27.4	For 24 Hrs=80
6	Lead (Pb)	µg/m ³	IS:5182 (Part 22)	BDL(DL-0.05)	For 24 Hrs=1.0
7	Ozone (O ₃)	µg/m ³	IS:5182 (Part-9)	BDL(DL-20.0)	For 8 Hrs=100 For 1 Hr=180
8	Ammonia (NH ₃)	µg/m ³	NCL/AIR/STP-13	BDL(DL-20.0)	For 24 Hrs=400
9	Benzene (C ₆ H ₆)	µg/m ³	IS:5182 (Part-11)	BDL(DL-1.0)	For Annual=05
10	Benzo (a) Pyrene (BaP)	ng/m ³	IS:5182 (Part-12)	BDL(DL-0.1)	For Annual=01

EW-069/26/09/25-1



Checked by

Arvind Solanki
 Sr. Analyst

FOR NEWCON CONSULTANTS & LABORATORIES



- The test report refers only to the particular sample/s submitted for testing and listed parameters.
- Endorsement of the same is neither inferred nor implied.
- Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
- Complaints about this report should be communicated within 10 days of the issue date of this report.
- The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
 Mobile : 9810430345, 9205501788 | Website : www.newconlab.in
 E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



Page No.: 2 of 2

TEST REPORT No. NCL/EW-069/26/09/25

DATE OF REPORT : 01/10/2025

S.No.	Test Parameters	Units	Test Method	Results	Specification As per CPCB
11	Arsenic (As)	ng/m3	NCL/AIR/STP-19	BDL(DL-1.0)	For Annual=06
12	Nickel (Ni)	ng/m3	NCL/AIR/STP-17	BDL(DL-5.0)	For Annual=20

End of Report

Remarks : BDL=Below Detection Limit.

EW-069/26/09/25-2



Arvind Choudhary
Checked by Analyst

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither Inferred nor Implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 2

TEST REPORT No. NCL/EW-066/26/09/25		DATE OF REPORT : 03/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: STACK EMISSION	Analysis End Date	: 03/10/2025
Analysis Start Date	: 26/09/2025	Sampling Done By	: NCL
Date of Sampling	: 25/09/2025	Duration of Sampling	: 30 Minutes
Sampling Protocol	: IS : 11255	Sample ID No.	: NCL/EW-066/26/09/25
Sampling Location	: Zinc F-1 Stack	Area Category	:
Equipments Used	: Vayubodhan Stack Sampler No-1 VSS-1 (S.No-321 DTC 07)		

DETAILS OF STACK

Stack Attached to	: Furnace No.1	Capacity	: 30 TPH
Type of fuel used	: Electricity	Quantity of fuel used	: NA
Stack height above the ground level	: 30.0 Mtr	Stack height above the roof top	: NA
Stack dia at the top	: 1200 mm	Material of Construction	: MS
Attached APCS	: Bag Filter	Normal Operating Schedule	: AS PER REQUIREMENT
Commissioning date	: March 2012		

PHYSICAL OBSERVATIONS

Ambient Temperature	: 28°C	Flue gas temperature	: 74°C
Velocity of the flue gases	: 7.53 mtr/sec	Sampling Flow Rate of SPM	: 27.0 LPM
Sampling Flow Rate for Gases	: 2.4 LPM	Quantity of Emission discharged	: 25623 Nm³/hr

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification As Per CPCB
1	Particulate Matters (PM)	mg/Nm³	IS:11255 (Part-1)	39	150
2	Sulphur Dioxide (SO₂)	mg/Nm³	IS:11255 (Part-2)	BDL(DL-3.4)	Not Specified
3	Oxides of Nitrogen (NOx)	mg/Nm³	IS:11255 (Part-7)	BDL(DL-5.0)	Not Specified
4	Carbon Monoxide (CO)	% By Vol	IS:13270	BDL(DL-0.2)	1.0
5	Lead	mg/Nm³	NCL/STP/AAS/01	BDL(DL-0.1)	10.0
6	Hydro Carbon (HC)	ppm	IS:11255 (Part-15)	BDL(DL-0.1)	Not Specified

EW-066/26/09/25-1



TENDER
Checked by

Arvind Choudhary
Analyst

FOR NEWCON CONSULTANTS & LABORATORIES



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 2

TEST REPORT No. NCL/EW-067/26/09/25		DATE OF REPORT : 03/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: STACK EMISSION	Analysis End Date	: 03/10/2025
Analysis Start Date	: 26/09/2025	Sampling Done By	: NCL
Date of Sampling	: 25/09/2025	Duration of Sampling	: 30 Minutes
Sampling Protocol	: IS : 11255	Sample ID No.	: NCL/EW-067/26/09/25
Sampling Location	: Zinc F-2 Stack	Area Category	:
Equipments Used	: Vayubodhan Stack Sampler No-1 VSS-1 (S.No-321 DTC 07)		

DETAILS OF STACK

Stack Attached to	: Furnace No.2	Capacity	: 30 TPH
Type of fuel used	: Electricity	Quantity of fuel used	: NA
Stack height above the ground level	: 30.0 Mtr	Stack height above the roof top	: NA
Stack dia at the top	: 1200 mm	Material of Construction	: MS
Attached APCS	: Bag Filter	Normal Operating Schedule	: AS PER REQUIREMENT
Commissioning date	: March 2012		

PHYSICAL OBSERVATIONS

Ambient Temperature	: 28°C	Flue gas temperature	: 85°C
Velocity of the flue gases	: 7.8 mtr/sec	Sampling Flow Rate of SPM	: 27.0 LPM
Sampling Flow Rate for Gases	: 2.5 LPM	Quantity of Emission discharged	: 25726 Nm³/hr

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification As Per CPCB
1	Particulate Matters (PM)	mg/Nm³	IS:11255 (Part-1)	36	150
2	Sulphur Dioxide (SO₂)	mg/Nm³	IS:11255 (Part-2)	BDL(DL-3.4)	Not Specified
3	Oxides of Nitrogen (NOx)	mg/Nm³	IS:11255 (Part-7)	BDL(DL-5.0)	Not Specified
4	Carbon Monoxide (CO)	% By Vol	IS:13270	BDL(DL-0.2)	1.0
5	Lead	mg/Nm³	NCL/STP/AAS/1	BDL(DL-0.1)	10.0
6	Hydro Carbon (HC)	ppm	IS:11255 (Part-15)	BDL(DL-0.1)	Not Specified

EW-067/26/09/25-1



Checked by
Arvind Choudhary

Arvind Choudhary
Analyst

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-015/27/09/25	DATE OF REPORT : 03/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153

SAMPLING DETAIL

Sample Name	: STACK EMISSION	Analysis End Date	: 03/10/2025
Analysis Start Date	: 27/09/2025	Sampling Done By	: NCL
Date of Sampling	: 26/09/2025	Duration of Sampling	: 30 Minutes
Sampling Protocol	: IS : 11255	Sample ID No.	: NCL/EW-015/27/09/25
Sampling Location	: DG Set No.1 (7.5 MW)	Area Category	: --
Equipments Used	: Vayubodhan Stack Sampler No-1 VSS-1 (S.No-321 DTC 07)		

DETAILS OF STACK

Stack Attached to	: DG Set No.1	Capacity of D.G.	: 7.5 MW
Type of fuel used	: HSD	Quantity of fuel used	: 1600 lph
Stack height above the ground level	: 50.0 Mtr	Stack height above the roof top	: NA
Stack dia at the top	: 1100 mm	Material of Construction	: MS
Attached APCS	: --	Normal Operating Schedule	: AS PER REQUIREMENT
D.G.set commissioning date	: March 2012		

PHYSICAL OBSERVATIONS

Ambient Temperature	: 28°C	Flue gas temperature	: 273°C
Velocity of the flue gases	: 15.96 mtr/sec	Sampling Flow Rate of SPM	: 15.0 LPM
Sampling Flow Rate for Gases	: 1.3 LPM	Quantity of Emission discharged	: 29002 Nm ³ /hr

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification (Max) As Per CPCB
1	Particulate Matters (PM) (at 15% O ₂ Correction)	Mg/Nm ³	IS:11255 (P-1)	46	75
2	Sulphur Dioxide (SO ₂)	Mg/Nm ³	IS:11255 (P-2)	26	Not Specified
3	Oxides of Nitrogen (at 15% O ₂ Correction)	ppmv	IS:11255 (P-7)	181	710
4	Carbon Monoxide (CO) (at 15% O ₂ Correction)	Mg/Nm ³	IS:13270	42	150
5	NMHC (at 15% O ₂ Correction)	Mg/Nm ³	USEPA METHOD 25	22	100

End of Report

EW-015/27/09/25-1



Checked by
S. Singh

Arvind Singh
S. Singh

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



- The test report refers only to the particular sample/s submitted for testing and listed parameters.
- Endorsement of the same is neither inferred nor implied.
- Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
- Complaints about this report should be communicated within 10 days of the issue date of this report.
- The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/158, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-016/27/09/25		DATE OF REPORT : 03/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: STACK EMISSION	Analysis End Date	: 03/10/2025
Analysis Start Date	: 27/09/2025	Sampling Done By	: NCL
Date of Sampling	: 26/09/2025	Duration of Sampling	: 30 Minutes
Sampling Protocol	: IS : 11255	Sample ID No.	: NCL/EW-016/27/09/25
Sampling Location	: DG Set No.2 (7.5 MW)	Area Category	: --
Equipments Used	: Vayubodhan Stack Sampler No-1 VSS-1 (S.No-321 DTC 07)		

DETAILS OF STACK

Stack Attached to	: DG Set No.2	Capacity of D.G.	: 7.5 MW
Type of fuel used	: HSD	Quantity of fuel used	: 1600 lph
Stack height above the ground level	: 50.0 Mtr	Stack height above the roof top	: NA
Stack dia at the top	: 1100 mm	Material of Construction	: MS
Attached APCS	: --	Normal Oprating Schedule	: AS PER REQUIREMENT
D.G set comminssioning date	: March 2012		

PHYSICAL OBSERVATIONS

Ambient Temperature	: 28°C	Flue gas temperature	: 270°C
Velocity of the flue gases	: 16.17 mtr/sec	Sampling Flow Rate of SPM	: 15.0 LPM
Sampling Flow Rate for Gases	: 1.6 LPM	Quantity of Emission discharged	: 29546 Nm³/hr

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification (Max) As Per CPCB
1	Particulate Matters (PM) (at 15% O2 Correction)	Mg/Nm³	IS:11255 (P-1)	47	75
2	Sulphur Dioxide (SO2)	Mg/Nm³	IS:11255 (P-2)	25	Not Specified
3	Oxides of Nitrogen (at 15% O2 Correction)	ppmv	IS:11255 (P-7)	184	710
4	Carbon Monoxide (CO) (at 15% O2 Correction)	Mg/Nm³	IS:13270	44	150
5	NMHC (at 15% O2 Correction)	Mg/Nm³	USEPA METHOD 25	23	100

End of Report

EW-016/27/09/25-1



Checked by
[Signature]

Authorized Signatory
[Signature]

FOR NEWCON CONSULTANTS & LABORATORIES



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
Mobile : 9810430345, 9205501788 | Website : www.newconlab.in
E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-017/27/09/25		DATE OF REPORT : 03/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: STACK EMISSION	Analysis End Date	: 03/10/2025
Analysis Start Date	: 27/09/2025	Sampling Done By	: NCL
Date of Sampling	: 26/09/2025	Duration of Sampling	: 30 Minutes
Sampling Protocol	: IS : 11255	Sample ID No.	: NCL/EW-017/27/09/25
Sampling Location	: DG Set No.3 (1250 KVA)	Area Category	:
Equipments Used	: Vayubodhan Stack Sampler No-1 VSS-1 (S.No-321 DTC 07)		

DETAILS OF STACK

Stack Attached to	: DG Set No-3	Capacity	: 1250 KVA = 1000 KW
Type of fuel used	: HSD	Quantity of fuel used	: 250 Ltr/hr
Stack height above the ground level	: 30.0 Mtr	Stack height above the roof top	: NA
Stack dia at the top	: 500 mm	Material of Construction	: MS
Attached APCS	: --	Normal Oprating Schedule	: AS PER REQUIREMENT
Comminssioning date	: March 2012		

PHYSICAL OBSERVATIONS

Ambient Temperature	: 28°C	Flue gas temperature	: 260°C
Velocity of the flue gases	: 15.77 mtr/sec	Sampling Flow Rate of SPM	: 15.0 LPM
Sampling Flow Rate for Gases	: 1.5 LPM	Quantity of Emission discharged	: 6065.28 Nm³/hr

TEST RESULT

S.No.	Test Parameters	Units	Test Method	Results	Specification (Max) As Per CPCB
1	Particulate Matters (PM) (at 15% O2 Correction)	Mg/Nm³	IS:11255 (P-1)	45	75
2	Sulphur Dioxide (SO2)	Mg/Nm³	IS:11255 (P-2)	21	Not Specified
3	Oxides of Nitrogen (at 15% O2 Correction)	ppmv	IS:11255 (P-7)	150	710
4	Carbon Monoxide (CO) (at 15% O2 Correction)	Mg/Nm³	IS:13270	43	150
5	NMHC (at 15% O2 Correction)	Mg/Nm³	USEPA METHOD 25	20	100

End of Report

EW-017/27/09/25-1



FOR NEWCON CONSULTANTS & LABORATORIES
Authorized Signatory

Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory

- The test report refers only to the particular sample/s submitted for testing and listed parameters.
- Endorsement of the same is neither inferred nor implied.
- Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
- Complaints about this report should be communicated within 10 days of the issue date of this report.
- The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12821

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-071/26/09/25/A		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: Workzone Air	Analysis End Date	: 01/10/2025
Analysis Start Date	: 26/09/2025	Sampling Done By	: NCL
Date of Sampling	: 25/09/2025	Equipments Used	: Handy Sampler
Time of Sampling	: 11:30 AM TO 07:30 PM		
Sampling Location	: Zinc Furnace Top Floor	Sample ID No.	: NCL/EW-071/26/09/25
Sampling Protocol	: IS : 5182	Sample Duration	: 8 Hrs
Ambient Temperature	: 31°C	Sampling Flow Rate	: 2.0 LPM

TEST RESULT

S.No.	Test Parameter	Units	Test Method	Results	Specification As Per Factory Act 1948 Sch. II/OSHA (Max)
1	Particulate Matters (Size Less Than 10µm) (Pm10)	mg/m³	IS:5182 (Part 23)	0.061	5.0
2	Sulphur Dioxide (as SO2)	mg/m³	IS:5182 (Part 2)	0.0131	5.0
3	Carbon Monoxide (as CO)	mg/m³	IS:15206	0.53	55.0
4	Nitrogen Dioxide (as NO2)	mg/m³	IS:5182 (Part 6)	0.0228	5.0
5	Lead (as Pb)	mg/m³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	0.15
6	Arsenic (as As)	mg/m³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	0.2

End of Report

Remarks : BDL=Below Detection Limit.

EW-071/26/09/25-1



Checked by
Arvind Choudhary
Signature

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory

1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-071/26/09/25/B		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: Workzone Air	Analysis End Date	: 01/10/2025
Analysis Start Date	: 26/09/2025	Sampling Done By	: NCL
Date of Sampling	: 25/09/2025	Equipments Used	: Handy Sampler
Time of Sampling	: 11:30 AM TO 07:30 PM		
Sampling Location	: Zinc Furnace Top Floor	Sample ID No.	: NCL/EW-071/26/09/25
Sampling Protocol	: IS : 5182	Sample Duration	: 8 Hrs
Ambient Temperature	: 31°C	Sampling Flow Rate	: 2.0 LPM

TEST RESULT

S.No.	Test Parameter	Units	Test Method	Results	Specification As Per Factory Act 1948 Sch. II/OSHA (Max)
1	Zinc (as Zn)	mg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified
2	Antimony (as Sb)	µg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified
3	Bismuth (as Bi)	µg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified
4	Iron (as Fe)	µg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified

End of Report

Remarks : BDL=Below Detection Limit.

EW-071/26/09/25-1



Arvind K. Boudhary
Checked by Analyst

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-072/26/09/25/A		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: Workzone Air	Analysis End Date	: 01/10/2025
Analysis Start Date	: 26/09/2025	Sampling Done By	: NCL
Date of Sampling	: 25/09/2025	Equipments Used	: Handy Sampler
Time of Sampling	: 12:00 PM TO 08:00 PM		
Sampling Location	: Zinc Casting Machine Floor	Sample ID No.	: NCL/EW-072/26/09/25
Sampling Protocol	: IS : 5182	Sample Duration	: 8 Hrs
Ambient Temperature	: 30°C	Sampling Flow Rate	: 2.0 LPM

TEST RESULT

S.No.	Test Parameter	Units	Test Method	Results	Specification As Per Factory Act 1948 Sch. II/OSHA (Max)
1	Particulate Matters (Size Less Than 10µm) (Pm10)	mg/m³	IS:5182 (Part 23)	0.057	5.0
2	Sulphur Dioxide (as SO2)	mg/m³	IS:5182 (Part 2)	0.0124	5.0
3	Carbon Monoxide (as CO)	mg/m³	IS:15206	0.50	55.0
4	Nitrogen Dioxide (as NO2)	mg/m³	IS:5182 (Part 6)	0.0215	6.0
5	Lead (as Pb)	mg/m³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	0.15
6	Arsenic (as As)	mg/m³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	0.2

End of Report

Remarks : BDL=Below Detection Limit.

EW-072/26/09/25-1



Checked by

Arvind Choudhary

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
Mobile : 9810430345, 9205501788 | Website : www.newconlab.in
E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-072/26/09/25/B		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : Workzone Air
 Analysis Start Date : 26/09/2025 Analysis End Date : 01/10/2025
 Date of Sampling : 25/09/2025 Sampling Done By : NCL
 Time of Sampling : 12:00 PM TO 08:00 PM Equipments Used : Handy Sampler
 Sampling Location : Zinc Casting Machine Floor Sample ID No. : NCL/EW-072/26/09/25
 Sampling Protocol : IS : 5182 Sample Duration : 8 Hrs
 Ambient Temperature : 30°C Sampling Flow Rate : 2.0 LPM

TEST RESULT

S.No.	Test Parameter	Units	Test Method	Results	Specification As Per Factory Act 1948 Sch. II/OSHA (Max)
1	Zinc (as Zn)	mg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified
2	Antimony (as Sb)	µg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified
3	Bismuth (as Bi)	µg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified
4	Iron (as Fe)	µg/m ³	NCL/LAB/STP/AIR-9	BDL(DL-0.001)	Not Specified

End of Report

Remarks : BDL=Below Detection Limit.

EW-072/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 2

TEST REPORT No. NCL/EW-025/29/09/25/A		ULR No.: TC126212500000336F	DATE OF REPORT : 04/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153		

SAMPLING DETAILS

Sample Name	: Ground Water	Analysis End Date	: 04/10/2025
Analysis Start Date	: 29/09/2025	Sample ID No.	: NCL/EW-025/29/09/25
Date of Sampling	: 27/09/2025	Sample Receipt Date	: 29/09/2025
Time of Sampling	: 11:00 AM	Environmental Condition	: 27±2°C
Sampling Done By	: NCL	Sample Quantity	: 10+1 Ltr
Sample Description	: Ground Water	Packing	: PVC CANE
Sampling Location	: Borewell		
Sampling Protocol	: IS:17614 (P-1)		
Packing Condition	: Sealed		

TEST RESULT

S.No.	Parameters	Unit	Test Method	Result	Specification /Limit As Per IS:10500-2012/Amd. 2021	
					Desirable Limit	Permissible Limit
Organoleptic and Physical Parameter						
1	Colour	Hazen	IS : 3025 (P-4)	BDL(DL-1.0)	5.0	15
2	Odour	--	IS : 3025 (P-5)	Agreeable	Agreeable	Agreeable
3	Taste	--	IS : 3025 (P-8)	Agreeable	Agreeable	Agreeable
4	Turbidity	NTU	IS : 3025 (P-10)	BDL(DL-1.0)	1.0	5.0
5	pH Value	--	IS : 3025 (P-11)	7.64	6.5-8.5	No Relaxation
6	Total Dissolved Solids	mg/L	IS : 3025 (P-16)	190	500	2000
General Parameter						
7	Total Hardness (as CaCO3)	mg/L	IS : 3025 (P-21)	86	200	600
8	Calcium (as Ca)	mg/L	IS : 3025 (P-40)	22.4	75	200
9	Magnesium (as Mg)	mg/L	APHA 3500 (mg)	7.3	30	100
10	Total Alkalinity (as CaCO3)	mg/L	IS : 3025 (P-23)	39	200	600
11	Chloride (as Cl)	mg/L	IS : 3025 (P-32)	54	250	1000
12	Nitrate (as NO3)	mg/L	IS : 3025 (P-34)	BDL(DL-0.2)	45	No Relaxation
13	Sulphate (as SO4)	mg/L	IS : 3025 (P-24)	BDL(DL-10.0)	200	400

EW-025/29/09/25-1



Swati Chauhan
3rd Analyst
Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory

1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
Mobile : 9810430345, 9205501788 | Website : www.newconlab.in
E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

Page No.: 2 of 2

TEST REPORT No. NCL/EW-025/29/09/25/A

ULR No.:TC126212500000336F

DATE OF REPORT : 04/10/2025

S.No.	Parameters	Unit	Test Method	Result	Specification /Limit As Per IS:10500-2012/Amd. 2021	
					Desirable Limit	Permissible Limit
14	Sulphide (as H ₂ S)	mg/L	IS : 3025 (P-29)	BDL(DL-0.05)	0.05	No Relaxation
15	Fluoride (as F)	mg/L	APHA 24th Edition 4500 (F-D)	BDL(DL-0.1)	1.0	1.5
16	Free Residual Chlorine (as Cl ₂)	mg/L	IS : 3025 (P-26)	BDL(DL-0.2)	0.2	1.0
17	Chloramines (as Cl ₂)	mg/L	IS : 3025 (P-26)	BDL(DL-0.2)	4.0	No Relaxation
18	Phenolic Compound (as C ₆ H ₅ OH)	mg/L	IS : 3025 (P-43)	BDL(DL-0.001)	0.001	0.002
19	Anionic Surfactant (as MBAS)	mg/L	IS : 3025 (P-68)	BDL(DL-0.1)	0.2	1.0
20	Mineral Oil	mg/L	IS : 3025 (P-39)	BDL(DL-0.1)	0.5	No Relaxation
21	Sodium (as Na)	mg/L	APHA 3500 Na (B)	BDL(DL-10.0)	Not Specified	Not Specified
22	Potassium (as K)	mg/L	APHA 3500 K (B)	BDL(DL-1.0)	Not Specified	Not Specified
Heavy Metals Parameter						
23	Iron (as Fe)	mg/L	IS : 3025 (P-65)	BDL(DL-0.01)	1.0	No Relaxation
24	Zinc (as Zn)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	5.0	15.0
25	Boron (as B)	mg/L	IS : 3025 (P-65)	BDL(DL-0.01)	0.5	1.0
26	Nickel (as Ni)	mg/L	IS : 3025 (P-65)	BDL(DL-0.01)	0.02	No Relaxation
27	Manganese (as Mn)	mg/L	IS : 3025 (P-65)	BDL(DL-0.01)	0.1	0.3
28	Lead (as Pb)	mg/L	IS : 3025 (P-65)	BDL(DL-0.005)	0.01	No Relaxation
29	Copper (as Cu)	mg/L	IS : 3025 (P-65)	BDL(DL-0.01)	0.05	1.5
30	Chromium (as Cr)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	0.05	No Relaxation
31	Aluminium (as Al)	mg/L	IS : 3025 (P-65)	BDL(DL-0.01)	0.03	0.2
Microbiological Parameter						
32	E. Coli	MPN/100ml	IS : 1622	<2	Not Specified	Not Specified
33	Total Coliform	MPN/100ml	IS : 1622	<2	Not Specified	Not Specified

End of Report

Remarks : BDL=Below Detection Limit.

* Parameters are outsource tested from other Lab. Report No. SQC /NR-25100404

EW-025/29/09/25-2



Swati Chaudhary
Checked by

Arvind Chaudhary
Sr. Analyst

ISHA KAGI
Jr. Analyst

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory

TEST REPORT

Page No.: 1 of 2

TEST REPORT No. NCL/EW-025/29/09/25/B		DATE OF REPORT : 04/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAILS

Sample Name	: Ground Water	Analysis End Date	: 04/10/2025
Analysis Start Date	: 29/09/2025	Sample ID No.	: NCL/EW-025/29/09/25
Date of Sampling	: 27/09/2025	Sample Receipt Date	: 29/09/2025
Time of Sampling	: 11:00 AM	Environmental Condition	: 27±2°C
Sampling Done By	: NCL		
Sample Description	: Ground Water		
Sampling Location	: Borewell		
Sampling Protocol	: IS:17614 (P-1)	Sample Quantity	: 10+1 Ltr
Packing Condition	: Sealed	Packing	: PVC CANE

TEST RESULT

S.No.	Parameters	Unit	Test Method	Result	Specification /Limit As Per IS:10500-2012/Amd. 2021	
					Desirable Limit	Permissible Limit
1	Cyanide (as CN)	mg/L	IS : 3025 (P-27)	BDL(DL-0.05)	0.05	No Relaxation
2	Ammonia (as total Ammonia)	mg/L	IS : 3025 (P-34)	BDL(DL-0.5)	0.5	No Relaxation
3	Selenium (as Se)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	0.01	No Relaxation
4	Arsenic (as As)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	0.01	No Relaxation
5	Cadmium (as Cd)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	0.003	No Relaxation
6	Molybdenum (as Mo)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	0.07	No Relaxation
7	Silver (as Ag)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	0.1	No Relaxation
8	Barium (as Ba)	mg/L	IS : 3025 (P-65)	BDL(DL-0.001)	0.7	No Relaxation
9	Mercury (as Hg)	mg/L	IS : 3025 (P-65)	BDL(DL-0.0005)	0.001	No Relaxation
Pesticides Residue						
10	Poly Chlorinated Biphenyls (PCB)	mg/L	APHA 6431 B	BDL(DL-0.00005)	0.0005	No Relaxation
11	Polynuclear Aromatic Hydrocarbon (PAH)	mg/L	APHA 6440	BDL(DL-0.00005)	0.0001	No Relaxation
12	Alachlor	µg/L	USEPA 525.2	BDL(DL-0.005)	20.0	No Relaxation

EW-025/29/09/25-1



Swati Chauhan
Checked by Analyst

FOR NEWCON CONSULTANTS & LABORATORIES



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
Mobile : 9810430345, 9205501788 | **Website :** www.newconlab.in
E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory

Page No.: 2 of 2

TEST REPORT No. NCL/EW-025/29/09/25/B

DATE OF REPORT : 04/10/2025

S.No.	Parameters	Unit	Test Method	Result	Specification /Limit As Per IS:10500-2012/Amd. 2021	
					Desirable Limit	Permissible Limit
13	Atrazine	µg/L	USEPA 525.2	BDL(DL-0.005)	2.0	No Relaxation
14	Aldrin	µg/L	USEPA 508	BDL(DL-0.005)	0.03	No Relaxation
15	Dieldrin	µg/L	USEPA 508	BDL(DL-0.005)	0.03	No Relaxation
16	Alpha HCH	µg/L	USEPA 508	BDL(DL-0.005)	0.01	No Relaxation
17	Beta HCH	µg/L	USEPA 508	BDL(DL-0.005)	0.04	No Relaxation
18	Butachlor	µg/L	USEPA 525.2	BDL(DL-0.005)	125.0	No Relaxation
19	Chlorpyrifos	µg/L	USEPA 525.2	BDL(DL-0.005)	30.0	No Relaxation
20	Delta HCH	µg/L	USEPA 508	BDL(DL-0.005)	0.04	No Relaxation
21	2,4 dichlorophenoxyacetic acid	µg/L	USEPA 515.1	BDL(DL-0.001)	30.0	No Relaxation
22	4,4-DDE	µg/L	USEPA 508	BDL(DL-0.005)	1.0	No Relaxation
23	4,4-DDD	µg/L	USEPA 508	BDL(DL-0.005)	1.0	No Relaxation
24	4,4-DDT	µg/L	USEPA 508	BDL(DL-0.005)	1.0	No Relaxation
25	2,4-DDD	µg/L	USEPA 508	BDL(DL-0.005)	1.0	No Relaxation
26	2,4-DDT	µg/L	USEPA 508	BDL(DL-0.005)	1.0	No Relaxation
27	2,4-DDE	µg/L	USEPA 508	BDL(DL-0.005)	1.0	No Relaxation
Trihalomethane						
28	Bromoform	mg/L	NCL/SOP/INST/112	BDL(DL-0.01)	0.1	No Relaxation
29	Dibromochloromethane	mg/L	NCL/SOP/INST/112	BDL(DL-0.01)	0.1	No Relaxation
30	Bromodichloromethane	mg/L	NCL/SOP/INST/112	BDL(DL-0.01)	0.06	No Relaxation
31	Chloroform	mg/L	NCL/SOP/INST/112	BDL(DL-0.01)	0.2	No Relaxation
Radioactive Parameters						
32	Gross Alpha (Bq/l)*	mg/L	IS: 14194 (Part-2) 2022	BDL	Not Specified	Not Specified
33	Gross Beta ((Bq/l)*	mg/L	IS: 14194 (Part-1) 2023	BDL	Not Specified	Not Specified

End of Report

Remarks : BDL=Below Detection Limit.

* Parameters are outsource tested from other Lab. Report No. SQC /NR-25100404

EW-025/29/09/25-2



Swati Chughan
Sr. Analyst
Checked-by

Arvind Choudhary
Sr. Analyst

ISHA SINGH
Jr. Analyst

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-026/29/09/25/A		DATE OF REPORT : 04/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAILS

Sample Name	: WASTE WATER	Analysis End Date	: 04/10/2025
Analysis Start Date	: 29/09/2025	Sample ID No.	: NCL/EW-026/29/09/25
Date of Sampling	: 27/09/2025	Sample Receipt Date	: 29/09/2025
Time of Sampling	: 11:30 AM	Environmental Condition	: 27±2°C
Sampling Done By	: NCL		
Sample Description	: SEWAGE WATER AFTER TREATMENT		
Sampling Location	: STP OUTLET FINAL EXIT POINT		
Sampling Protocol	: IS:17614 (P-1)	Sample Quantity	: 2+1 Ltr
Packing Condition	: Sealed	Packing	: PVC CANE

TEST RESULT

S.No.	Parameter	Units	Test Method	Results	Specification/Limits as per CPCB
1	pH	-	IS : 3025 (P-11)	7.47	6.5-9.0
2	Total Suspended Solids (TSS)	mg/L	IS : 3025 (P-17)	BDL(DL-5.0)	50.0
3	Bio Chemical Oxygen Demand (3 days at 27°C)	mg/L	IS : 3025 (P-44)	12	20.0
4	Chemical Oxygen Demand (COD)	mg/L	APHA-5220 (B)	60	Not Specified
5	Oil & Grease	mg/L	IS : 3025 (P-39)	BDL(DL-5.0)	Not Specified
6	Total Dissolved Solids (TDS)	mg/L	IS:3025 (P-16)	352	Not Specified
7	Feecal Coliform	MPN/100ml	APHA-9221 24th Edition	840	1000
8	Total Phosphorous(P)	mg/L	4500-D, P-APHA, 23rd ED.	BDL(DL-0.05)	Not Specified
9	Ammonical Nitrogen (as N)	mg/L	APHA 4500 (B,C)	1.0	5.0

End of Report

Remarks : BDL = Below Detection Limit.

EW-026/29/09/25-1



Swati Chhaban
Checked by

ISHA ZYAGI
Jr Analyst

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory

1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
Mobile : 9810430345, 9205501788 | Website : www.newconlab.in
E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-026/29/09/25/B		DATE OF REPORT : 04/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAILS

Sample Name : WASTE WATER
Analysis Start Date : 29/09/2025
Date of Sampling : 27/09/2025
Time of Sampling : 11:30 AM
Sampling Done By : NCL
Sample Description : SEWAGE WATER AFTER TREATMENT
Sampling Location : STP OUTLET FINAL EXIT POINT
Analysis End Date : 04/10/2025
Sample ID No. : NCL/EW-026/29/09/25
Sample Receipt Date : 29/09/2025
Environmental Condition : 27±2°C
Sampling Protocol : IS:17614 (P-1)
Packing Condition : Sealed
Sample Quantity : 2+1 Ltr
Packing : PVC CANE

TEST RESULT

S.No.	Parameter	Units	Test Method	Results	Specification/limits as per CPCB
1	Total Nitrogen	mg/L	APHA 4500-Norg (B)	2.3	Not Specified

End of Report

Remarks : BDL = Below Detection Limit.

EW-026/29/09/25-1



Swati Chauhan
Analyst
Checked by

ISHA YAGI
Jr. Analyst

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12821

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-078/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : Ambient Noise
 Analysis Start Date : 26/09/2025 Analysis End Date : 26/09/2025
 Date of Monitoring : 25/09/2025 Monitoring Done By : NCL
 Monitoring Duration : 10 Minutes Place of Monitoring : Near Main Gate
 Time of Monitoring : 11:20 AM TO 11:30 AM Protocol : NCL/AIR/STP/20
 Category of Area : Industrial Area

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Day Time Reading (dB(A))	62.4	62.6	63.9	63.2	64.8	64.3	65.1	65.7	66.5	66.6

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	64.5	-
2	L Max	66.6	-
3	L Min	62.4	-
4	Day Leq	64.7	75.0 Max

End of Report

EW-078/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory

- The test report refers only to the particular sample/s submitted for testing and listed parameters.
- Endorsement of the same is neither inferred nor implied.
- Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
- Complaints about this report should be communicated within 10 days of the issue date of this report.
- The report is not to be produced wholly or in part without prior permission of the Managing Partner, All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)
 Mobile : 9810430345, 9205501788 | Website : www.newconlab.in
 E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

As ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-079/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : Ambient Noise
 Analysis Start Date : 26/09/2025 Analysis End Date : 26/09/2025
 Date of Monitoring : 25/09/2025 Monitoring Done By : NCL
 Monitoring Duration : 10 Minutes Place of Monitoring : Near Main Gate
 Time of Monitoring : 10:20 PM TO 10:30 PM Protocol : NCL/AIR/STP/20
 Category of Area : Industrial Area

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Night Time Reading (dB(A))	51.7	51.3	52.6	52.2	53.9	53.4	53.8	54.1	55.5	55.3

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	53.4	-
2	L Max	55.5	-
3	L Min	51.3	-
4	Night Leq	53.6	75.0 Max

End of Report

EW-079/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-080/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: Ambient Noise	Analysis End Date	: 26/09/2025
Analysis Start Date	: 26/09/2025	Monitoring Done By	: NCL
Date of Monitoring	: 25/09/2025	Place of Monitoring	: East Side of Canteen in New Plot
Monitoring Duration	: 10 Minutes	Protocol	: NCL/AIR/STP/20
Time of Monitoring	: 11:30 AM TO 11:40 AM		
Category of Area	: Industrial Area		

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Day Time Reading (dB(A))	61.1	62.7	62.8	63.5	63.2	64.6	64.4	65.9	65.7	66.9

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	64.1	-
2	L Max	66.9	-
3	L Min	61.1	-
4	Day Leq	64.3	75.0 Max

End of Report

EW-080/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither Inferred nor Implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12821

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-081/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : Ambient Noise
 Analysis Start Date : 26/09/2025 Analysis End Date : 26/09/2025
 Date of Monitoring : 25/09/2025 Monitoring Done By : NCL
 Monitoring Duration : 10 Minutes Place of Monitoring : East Side of Canteen in New Plot
 Time of Monitoring : 10:30 PM TO 10:40 PM Protocol : NCL/AIR/STP/20
 Category of Area : Industrial Area

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Night Time Reading (dB(A))	51.4	52.1	52.5	53.7	53.2	54.8	54.3	55.6	55.9	56.3

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	54.0	-
2	L Max	56.3	-
3	L Min	51.4	-
4	Night Leq	54.2	75.0 Max

End of Report

EW-081/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-074/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: Ambient Noise	Analysis End Date	: 26/09/2025
Analysis Start Date	: 26/09/2025	Monitoring Done By	: NCL
Date of Monitoring	: 25/09/2025	Place of Monitoring	: Near Compressor Area
Monitoring Duration	: 10 Minutes	Protocol	: NCL/AIR/STP/20
Time of Monitoring	: 11:00 AM TO 11:10 AM		
Category of Area	: Industrial Area		

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Day Time Reading (dB(A))	62.5	62.2	63.9	63.1	64.7	64.6	65.8	65.3	66.8	66.9

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	64.6	-
2	L Max	66.9	-
3	L Min	62.2	-
4	Day Leq	64.8	75.0 Max

End of Report

EW-074/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-075/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : Ambient Noise
 Analysis Start Date : 26/09/2025 Analysis End Date : 26/09/2025
 Date of Monitoring : 25/09/2025 Monitoring Done By : NCL
 Monitoring Duration : 10 Minutes Place of Monitoring : Near Compressor Area
 Time of Monitoring : 10:00 PM TO 10:10 PM Protocol : NCL/AIR/STP/20
 Category of Area : Industrial Area

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Night Time Reading (dB(A))	52.1	53.6	53.8	53.2	54.7	54.3	55.6	55.4	56.8	56.5

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	54.6	-
2	L Max	56.8	-
3	L Min	52.1	-
4	Night Leq	54.8	75.0 Max

End of Report

EW-075/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)
An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12021

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-076/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name : Ambient Noise
Analysis Start Date : 26/09/2025 Analysis End Date : 26/09/2025
Date of Monitoring : 25/09/2025 Monitoring Done By : NCL
Monitoring Duration : 10 Minutes Place of Monitoring : Back Side of DG Area
Time of Monitoring : 11:10 AM TO 11:20 AM Protocol : NCL/AIR/STP/20
Category of Area : Industrial Area

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Day Time Reading (dB(A))	63.2	63.4	64.9	64.7	65.3	65.2	66.1	67.8	68.5	68.6

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	65.8	-
2	L Max	68.6	-
3	L Min	63.2	-
4	Day Leq	66.0	75.0 Max

End of Report

EW-076/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



- The test report refers only to the particular sample/s submitted for testing and listed parameters.
- Endorsement of the same is neither inferred nor implied.
- Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
- Complaints about this report should be communicated within 10 days of the issue date of this report.
- The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.

Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in

E-mail : newconlab@gmail.com, newconlabfinance@gmail.com



Newcon Consultants & Laboratories

(GOVERNMENT APPROVED TESTING LABORATORIES)

An ISO 9001 : 2015, ISO 14001 : 2015, ISO 45001 : 2018 Certified Laboratory



TC-12621

TEST REPORT

Page No.: 1 of 1

TEST REPORT No. NCL/EW-077/26/09/25		DATE OF REPORT : 01/10/2025
Name and Address of Customer	M/S HINDUSTAN ZINC LIMITED Pantnagar Metal Plant, Pantnagar-263153	

SAMPLING DETAIL

Sample Name	: Ambient Noise	Analysis End Date	: 26/09/2025
Analysis Start Date	: 26/09/2025	Monitoring Done By	: NCL
Date of Monitoring	: 25/09/2025	Place of Monitoring	: Back Side of DG Area
Monitoring Duration	: 10 Minutes	Protocol	: NCL/AIR/STP/20
Time of Monitoring	: 10:10 PM TO 10:20 PM	Category of Area	: Industrial Area

OBSERVATIONS

Observation No.	1	2	3	4	5	6	7	8	9	10
Night Time Reading (dB(A))	52.4	52.2	53.9	53.3	54.1	54.6	55.8	55.1	56.5	56.9

TEST RESULT

S.No.	Test Parameter	Results	Specification As Per CPCB
1	Average Noise Level	54.5	-
2	L Max	56.9	-
3	L Min	52.2	-
4	Night Leq	54.7	75.0 Max

End of Report

EW-077/26/09/25-1



Checked by

FOR NEWCON CONSULTANTS & LABORATORIES

Authorized Signatory



1. The test report refers only to the particular sample/s submitted for testing and listed parameters.
2. Endorsement of the same is neither Inferred nor implied.
3. Laboratory shall maintain the confidentiality of all information related to the samples & test reports.
4. Complaints about this report should be communicated within 10 days of the issue date of this report.
5. The report is not to be produced wholly or in part without prior permission of the Managing Partner. All disputes subject to Ghaziabad Jurisdiction.


Laboratory : A-1/156, Sector-17, (Swadeshi Compound) Kavi Nagar Industrial Area, GHAZIABAD - 201 002 (U.P.)

Mobile : 9810430345, 9205501788 | Website : www.newconlab.in


E-mail : newconlab@gmail.com, newconlabfinance@gmail.com

ANNEXURE-2

CAAQMS

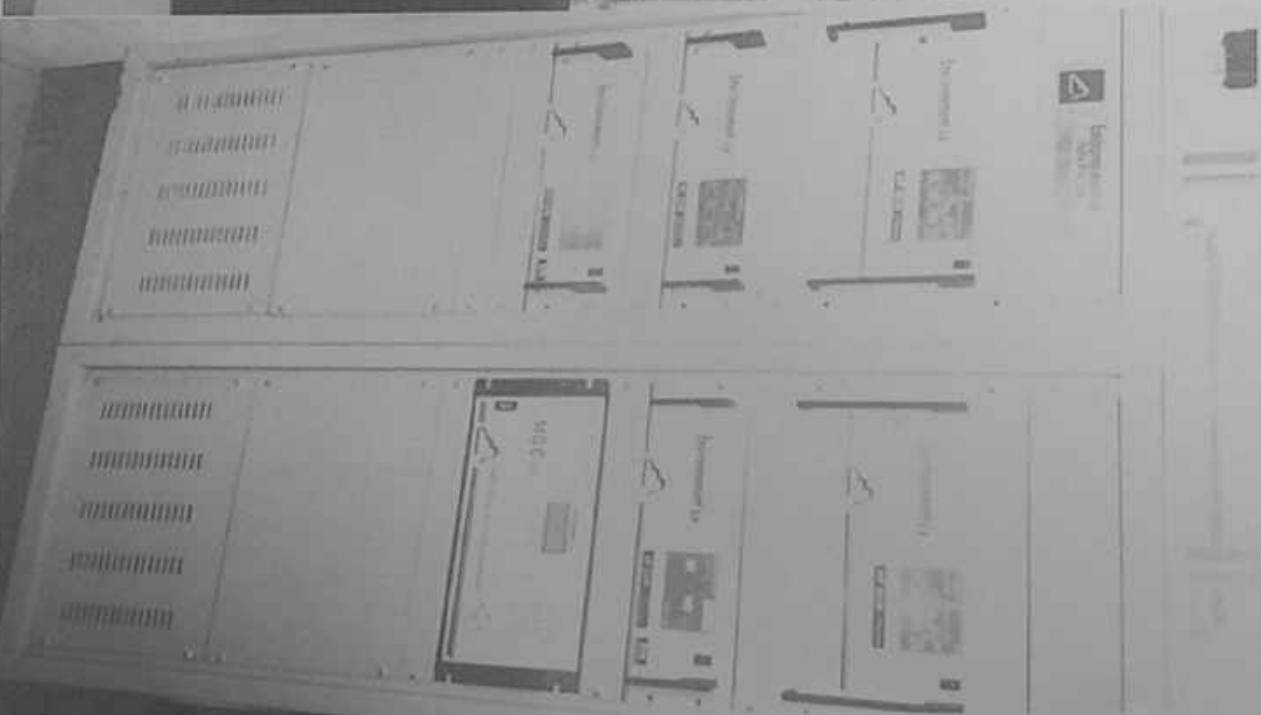

PH analyzer installed at stack

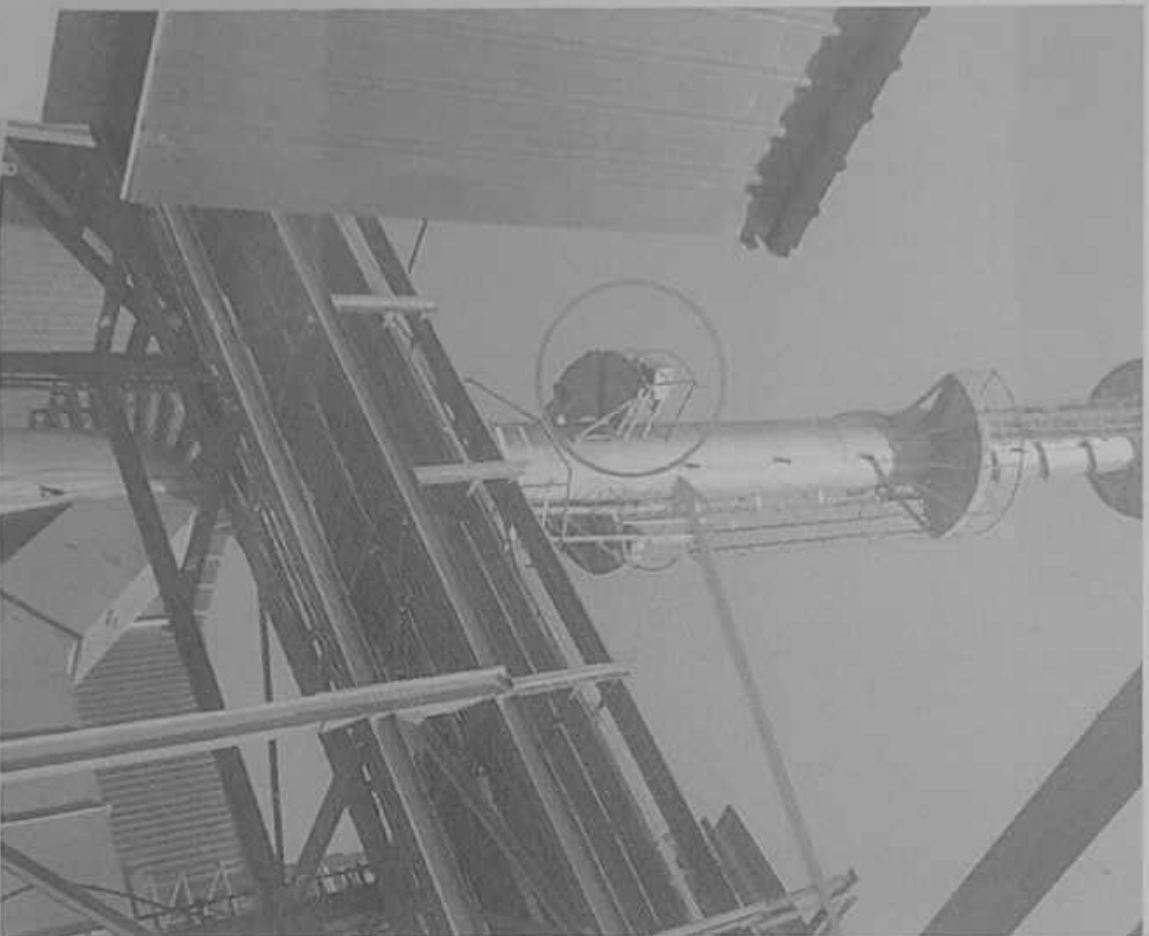

PM analyzer

Hygiene ventilation system



Bag filter
arrangement for
hygiene ventilation

Rainwater Storage Pond HZL-Pantnagar

ANNEXURE-3

Ground Water Withdrawal FY 2025-26			
Month	Ground Water Withdrawal	UOM	Rainwater utilization
Apr-25	4686	Cu.m	38
May-25	5177	Cu.m	954
Jun-25	2926	Cu.m	1951
Jul-25	2199	Cu.m	2616
Aug-25	1656	Cu.m	3113
Sep-25	2054	Cu.m	2882
		Cu.m	
		Cu.m	
		Cu.m	
		Cu.m	
		Cu.m	
		Cu.m	
Total	18,698	Cu.m	11,554

- All reading recorded in cubic meter.

Water Withdrawal Point – Borewell



Tanda Range, Uttarakhand, India
Hindustan Zinc Ltd Rd, Tanda Range, Uttarakhand 263153, India
Lat 29.036093°
Long 79.396594°

On-Going CSR Activities at PMP FY2025-26

Flag Ship Projects: Continuing in FY 25-26

1. Sakhi Project – Strengthening Women Empowerment.
2. ME – Providing Micro Enterprises support to SHG women for their sustainability.
3. Health Project - Mobile Health project started by covering 100 patients per day from 25 villages per month.
4. STEM lab : established in government school to support students

Other Activities:

- Organized various volunteering initiatives .
- Conducted awareness program on Menstrual Hygiene in nearby Govt. Girls schools.
- Conducted safety awareness program to Summer camp students while going for training by Head - Safety.
- Reviewed all projects on quarterly basis
- In July 2025, conducted Unchi Udaan screening exams which was attended by around 50 parents and students..
- Mensural Hygiene awareness program conducted in nearby schools with the health team.
- HIV AIDS awareness session was conducted in nearby community as well.

Rain Water Storage Ponds and reuse the water into the process

1.



2.



3.



4.



Sakhi : women empowerment initiative



Sakhi : women empowerment initiative



SHGs savings : 2.9 Cr.

Credit Linkage : 1.93 Cr.

Loan amount disbursed: 7.31 Cr.

Women entrepreneurs : 138

On-Going CSR Activities at PMP FY2025-26



Women Skill Development & Empowerment- Strengthening of Self-Help Group by This project (Sakhi) was implementing through Manjari Foundation. Started in the year 2017 and continuing.

Microenterprises

- Two Home-Grown Brands; Daichi and Upaya: Honey unit and stitching unit at Pantnagar
- 57% YoY increase in Sakhi's customer base



Women : 500 engaged

14 Production units
208 stores, sakhi
hubs & retail outlets

Strong E-platform
presence

INR 5 crores Revenue

INR 1 crores Income of Production
Sakhis

Hearts
with
Fingers

SAKHI
UPADAN SAMITI



DAICHI
THE BEST FROM RURAL INDIA

Source: Internal

upaya



SWASTHYA SEWA: MOBILE HEALTH VEHICLE

Inaugurated by CM Shri Pushkar Singh Dhami, Rudrapur CMO, DM and other dignitaries

Total villages : 25

Well equipped medical staff including MBBS doctor

Free of cost consultation and medication



On-Going CSR Activities at PMP FY205-26




Health Camp for nearby Community- Under Health, Water & Sanitation, Running mobile health clinic van in 25 villages on daily basis. Providing free doctor consultation, free medicine distribution etc. being done through this project. Daily in one village this camp will be held.

Unchi Udaan : Aspiring engineers

7

Total 34 engineering aspiring students have been benefitted from Panthagar since inception
A four-year residential program nurturing engineering talent through conceptual learning, language development, and targeted coaching.

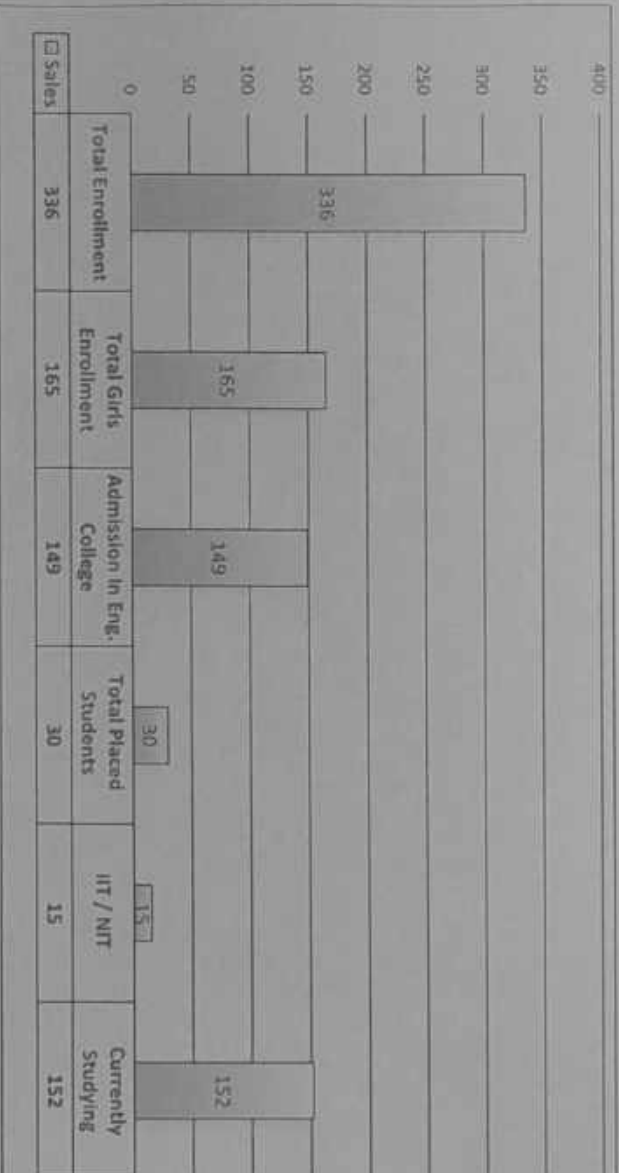

Stem Lab: Education initiative

Hindustan Zinc's first STEM Lab was established at Pantnagar
Govt Girls Inter College Pant Nagar, Rudrapur


Total number of School Children-753

The STEM Lab is equipped with over 20 interactive models and an advanced audio-visual setup to enhance experiential learning across all scientific concepts.



ANNEXURE - 5

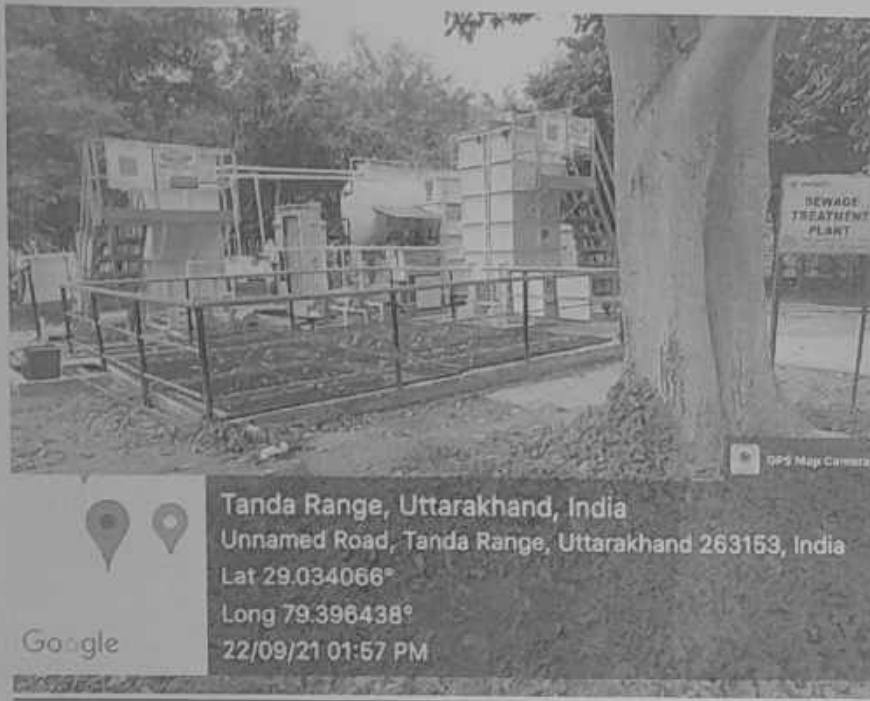


STP PLANT



ETP PLANT



PHOTOGRAPHS OF HAZARDOUS WASTE STORAGE YARD

S. No.	Name of the waste	Photographs
1.	Zinc Dross Storage Yard	
2.	Lead Dross Storage Yard	
3.	Used Oil Storage Yard	



PMP/F&S/2024-25/01


Date: 27/09/2024

To,
Dy. Chief Inspector (Factories & Boilers),
Shram Bhawan, Haldwani
Distt. Nainital (U.K.)

Subject: Regarding submission of updated On-site emergency response and contingency plan for Hindustan Zinc Limited- Pantnagar Metal Plant, Rudrapur, Uttarakhand,

Respected Sir,

With reference to the above subject, we are enclosing here the updated onsite emergency response and contingency plan for Hindustan Zinc Limited- Pantnagar Metal Plant, Rudrapur, Uttarakhand, for your kind information and record.

Yours Sincerely,

(Anamika Jha)
SBU Director
Hindustan Zinc Limited
Pantnagar Metal Plant
Pin Code-263153
Factory Manager U.S. Nagar (U.K.)
Pantnagar Metal Plant
Hindustan Zinc Ltd,
Rudrapur, Uttarakhand

10/27/24
कार्यालय
उप निदेशक कारखाना/ब्यापार, उत्तराखण्ड
नैनीताल (नैनीताल)

Hindustan Zinc Limited
Pantnagar Metal Plant
Plot No. 2 & 3, Sector 14, IIE, SIDCUL Pantnagar
☎ 05944-257300, www.hzindia.com

Regd. Office: Yashad Bhawan, Udaipur (Rajasthan) - 313 004
CIN: L27204RJ1766PLC001208

